

Third Party Evaluation of the Schemes/Programmes of Department of Animal Husbandry & Dairying (DAHD) –

1. Livestock Health Disease Control Program (LHDCP)

2. Supporting Dairy Cooperatives & Farmer Producer Organizations (SDCFPO)

Document Type:	Proposal
Version:	2.0
Date (DD/MM/YYYY):	15/07/2025
Submitted to:	Department of Animal Husbandry and Dairying (DAHD)
Submitted by:	Project Planning & Implementation Division (PPID), QCI



Quality Council of India (QCI) is an autonomous organisation established in 1997, through joint initiative of the Government of India and the Indian industry, pursuant to resolution of the Indian Cabinet in 1996. It is registered as a Society under the Societies Registration Act, 1860 with the mandate to establish and operate the national accreditation system in India and promote quality in all aspects of life, industry, environment, and governance. It is a self-sustaining independent organisation with complete financial, administrative, and functional autonomy. The Department for Promotion of Industry and Internal Trade (DPIIT), Ministry of Commerce and Industry, Government of India is the nodal point in the government for QCI and all matters concerning quality. The Governing Council of the Society is the apex governing organ of QCI and consists of equal representation of government, industry, and other stakeholders. Chairperson, QCI is nominated by the Prime Minister of India.

Regd. Office: 2nd Floor, Institution of Engineers Building, 2, Bahadur Shah Zafar Marg, New Delhi-02
Ph.: +91-11-2323 8736, +91 98990 15306, +91 70096 22718

TABLE OF CONTENTS

Quality Council of India (QCI)	4
1. Introduction to QCI	4
2. Mandate & Structure of QCI	4
3. Project Experiences of QCI: Evaluation of various schemes of DAHD & Other Ministries/ Departments	5
Background of Schemes- LHDCP & SDCFPO	7
4. Livestock Health Disease Control Program (LHDCP) Scheme	7
5. Supporting Dairy Cooperatives & Farmer Producer Organizations (SDC&FPO)	7
Genesis of the Study	8
6. Genesis of the Independent Third-Party Evaluation	8
7. Potential Outcomes through Evaluation Study	8
Objectives & Scope of Work for the Third-Party Evaluation	9
8. Livestock Health Disease Control Program (LHDCP)	9
8.1. Objective of the Study for LHDCP	9
8.2. Scope of Work for LHDCP Scheme Evaluation	9
9. Supporting Dairy Cooperatives & Farmer Producer Organizations (SDC&FPO)	11
9.1. Objective of the Study for SDC&FPO	11
9.2. Scope of Work for SDC&FPO	11
Methodological Framework	12
10. Research design and approach	12
11. Proposed Activities/Actions and Expected Insights	13
12. Identification of Stakeholders	14
Sampling	14
13. Sampling Strategy for Livestock Health Disease Control Program (LHDCP)	14
13.1. Proposed Sampled States & Districts for LHDCP Scheme Evaluation	14
14. Sampling Strategy for Supporting Dairy Cooperatives & Farmer Producer Organizations (SDCFPO) 15	
14.1. Proposed Sampled States & Districts for SDCFPO Scheme Evaluation	15
Operational Framework & Execution Plan	15
15. Preliminary Analysis and Development of Evaluation Framework	15
16. Preparation and Optimization of IT Platform	15
17. Pilot Study	16
18. Training and Deployment of Assessors	16
19. Primary Survey, Stakeholder Interviews and Focus Group Discussions (FGDs)	16
20. Data Quality Assurance	16
21. Data Analysis and Interpretation	16

22.	Final Reporting.....	16
Brief Work Plan & Key Deliverables		17
23.	Project Timelines for Third-Party Evaluation of respective Schemes	17
Financials		18
24.	Project Financials for Livestock Health Disease Control Program (LHDCP)	18
25.	Project Financials for Supporting Dairy Cooperatives & Farmer Producer Organizations (SDCFPO) 20	
26.	Payment Structure:	22
Annexures.....		23
27.	QCI's Previous Projects with DAHD	23
27.1.	Third-Party Evaluation of National Programme for Dairy Development (NPDD) Scheme	23
27.2.	Third-Party Evaluation of Animal Infrastructure Development Fund (AHIDF) Scheme	24
27.3.	Screening of Applications received through online National Award Portal for National Gopal Ratna Award 2024, 2023, & 2022 (on Nomination Basis)	29
28.	QCI's Previous Projects on Nomination Basis with different Ministries	35
28.1.	National Horticulture Board (NHB), Ministry of Agriculture & Farmers Welfare, GoI	35
28.2.	Third-Party Re-Assessment of FCI owned Warehouses	40
28.3.	Third-Party Assessment of Procurement Centers in KMS 2021-22 & RMS 2022-23	45
28.4.	Third-Party Assessment of FCI Warehouses	50
28.5.	Audit Assessment and Issuance of Warehouse rating for CWC warehouses on warehouse management practices, safety standards and infrastructure including the audit from point of improvement in efficiency and new initiatives	54
28.6.	Mid-Term Evaluation of Deendayal Antyodaya Yojana- National Urban Livelihood Mission (NULM).....	56
28.7.	PAN India Trans Fat Survey.....	57
28.8.	Assessment of various ODF, ODF+, & ODF++ status	60

List of Figures

Figure 1: QCI Organisational Structure.....	5
Figure 2: Triangulation Approach	12
Figure 3: Project Timelines for Third-Party Evaluation of the NHDPC & SDCFPO	17

List of Tables

Table 1: Proposed Activities/Action and Expected Insights from Third-Party NPDD Scheme Evaluation.....	13
Table 2: Proposed Sampled States & Districts for LHDCP Scheme Evaluation	14
Table 4: Proposed Sampled States & Districts for SDCFPO Scheme Evaluation	15
Table 5: Brief Work Plan with Key Activities & Deliverables for Independent Third-Party Evaluation each respective Schemes	17
Table 6: Estimated Project Financials for LHDCP Scheme	18
Table 8: Estimated Project Financials for SDCFPO Scheme.....	20
Table 9: Payment Structure for each respective Schemes (LHDCP & SDCFPO).....	22

Quality Council of India (QCI)

1. Introduction to QCI

- 1.1. The Quality Council of India (QCI) has been set up as a non-profit autonomous society registered under the Societies Registration Act XXI of 1860 to establish an accreditation structure in the country and to spread quality movement in India by undertaking a National Quality Campaign.
- 1.2. QCI was established as the National body for Accreditation on recommendations of the Expert Mission of the EU after consultations between the Inter-Ministerial Task Force, Committee of Secretaries, and Group of Ministers and finally a Cabinet decision in 1996.
- 1.3. The Council was made an autonomous non-profit organisation through seed funding initially by the Government of India and the Indian Industry represented by the three premier industry associations: Associated Chambers of Commerce and Industry of India (ASSOCHAM), Confederation of Indian Industry (CII) and Federation of Indian Chambers of Commerce and Industry (FICCI).
- 1.4. The Department for Promotion of Industry and Internal Trade (DPIIT), Ministry of Commerce and Industry is the nodal point for all matters connected with Quality and QCI. The Council was established to create a mechanism for third-party assessment of products, services, and processes.

2. Mandate & Structure of QCI

- 2.1. Quality Council of India (QCI) has been set up as a non-profit autonomous society to establish and operate the national accreditation system in the country and to spread the quality movement in India by undertaking a national quality campaign.
- 2.2. It was formed by a joint initiative of the Government of India and the Indian Industry associations like the Associated Chambers of Commerce and Industry of India (ASSOCHAM), Confederation of Indian Industry (CII) and Federation of Indian Chambers of Commerce and Industry (FICCI).
- 2.3. QCI has established Constituent Boards, Divisions, and Cells catering to various aspects of quality. Its Boards are full members of international systems of accreditation and have multilateral mutual recognition arrangements (MRAs/MLAs) that allow for international equivalence and recognition of conformity assessment outcomes.

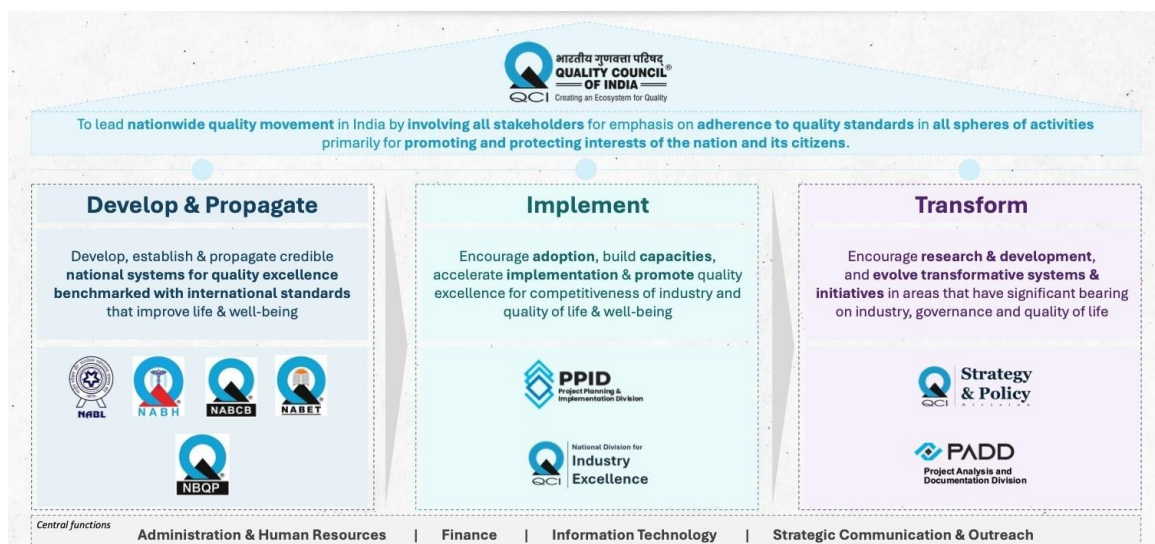


Figure 1: QCI Organisational Structure

2.4. Constituent Boards of QCI

- 2.4.1. **National Accreditation Board for Testing & Calibration Laboratories (NABL):** NABL accredits testing, calibration, and medical labs, as well as proficiency testing providers and reference material producers, based on international standards. NABL is a member of ILAC and APAC.
- 2.4.2. **National Accreditation Board for Certification Bodies (NABCB):** NABCB accredits Certification, Inspection, and Validation/Verification Bodies based on international standards and is a full member of IAF, ILAC, and APAC.
- 2.4.3. **National Accreditation Board for Hospitals and Healthcare Providers (NABH):** NABH accredits hospitals and healthcare organisations, with internationally recognized accreditations.
- 2.4.4. **National Accreditation Board for Education & Training (NABET):** NABET accredits education, training, and skill development organisations to national and international standards, enhancing quality and credibility. It operates under the Quality Council of India (QCI).
- 2.4.5. **National Board for Quality Promotion (NBQP):** NBQP promotes quality and excellence in India by setting standards, providing certifications, and conducting audits to enhance competitiveness and customer satisfaction.
- 2.4.6. **Special Projects Group (Cells and Divisions)**
 - 2.4.6.1. **Project Planning and Implementation Division (PPID)**
 - 2.4.6.2. **National Division for Industry Excellence (NDIE)**
 - 2.4.6.3. **Projects Analysis and Documentation Division (PADD)**
 - 2.4.6.4. **Strategy & Policy Division (SPD)**

3. Project Experiences of QCI: Evaluation of various schemes of DAHD & Other Ministries/ Departments

- 3.1. In 25 years, the Quality Council of India (QCI) has improved quality of life through initiatives in green development, inclusive growth, digital economy, public infrastructure, and

technology. It involves stakeholders to uphold quality standards and enhance citizens' well-being.

3.2. As the National Accreditation body of the country, it has been ranked 5th in the world in the recent Global Quality Infrastructure Index (GQII) 2021. In the past 10 years, QCI Professionals have engaged with 90+ ministries and departments of the Union and State Governments in executing 400+ projects across multivariate spheres.

3.3. The various Third-Party Evaluation of projects undertaken by QCI include the following:

List of few projects being awarded to QCI on nomination basis:

- 3.3.1. Third-Party Evaluation of the National Programme for Dairy Development (NPDD) Scheme
- 3.3.2. National Gopal Ratna Award 2022
- 3.3.3. National Gopal Ratna Award 2023
- 3.3.4. National Gopal Ratna Award 2024
- 3.3.5. Third-Party Evaluation of Scheme 1 & 2 of National Horticulture Board (NHB)
- 3.3.6. MSME Sustainable (ZED) Certification Scheme for FY 2023-24 (Ongoing)
- 3.3.7. Third Party Sampling & Analysis of Coal (Ongoing)
- 3.3.8. GeM vendor assessment
- 3.3.9. Quality Intervention to create a Quality Ecosystem for Khadi
- 3.3.10. Transformation of Food Corporation of India – Assessment of FCI Warehouses

List of few DAHD projects awarded through tendering process:

- 3.3.11. Third-Party Evaluation of Animal Husbandry & Infrastructure Development Fund (AHIDF) Scheme

and more than 100 further projects are being awarded to QCI on nomination basis. Work Order will be provided as per requirement.

Background of Schemes- LHDCP & SDCFPO

4. Livestock Health Disease Control Program (LHDCP) Scheme

- 4.1. The Livestock Health and Disease Control Program (LHDCP) is a vital initiative in India that focuses on safeguarding the health of the country's large livestock population. With one of the largest livestock populations in the world, maintaining their health is crucial not only for the well-being of the animals but also for India's economy, food security, and the livelihoods of millions of animal farmers.
- 4.2. The program emphasizes on disease prevention, control, and management, contributing significantly to the productivity and efficiency of the animal husbandry sector. Implemented by the Department of Animal Husbandry & Dairying (DAHD), under the Ministry of Fisheries, Animal Husbandry & Dairying, Government of India, the LHDCP, a Centrally Sponsored Scheme (CSS) aims to mitigate risks to animal health through vaccination, enhanced veterinary services, improved disease surveillance, and better veterinary infrastructure.
- 4.3. Following are the major components of the LHDCP scheme, each targeting specific aspects of livestock health & disease control:
 - 4.3.1. **National Animal Disease Control Program (NADCP):** NADCP aims to control and subsequently eradicate Foot & Mouth Disease (FMD) in cattle, buffaloes, sheep, goat and pigs and also for control of Bovine Brucellosis, with vaccination. The program implements large-scale vaccination drives to develop herd immunity and reduce disease incidence.
 - 4.3.2. **Livestock Health & Disease Control (LH&DC):** LH&DC aims to improve the animal health sector by control of economically important, zoonotic, exotic and emergent diseases by prophylactic vaccination, capacity building, disease surveillance and strengthening of veterinary infrastructure. LH&DC consists of three sub-components, as below:
 - 4.3.2.1. **Critical Animal Disease Control Program (CADCP):** Critical Animal Disease Control Program (CADCP) is aimed to control and eradicate Peste des Petits Ruminants (PPR) disease in sheep and goats and control Classical Swine Fever (CSF) disease in pigs, with vaccination.
 - 4.3.2.2. **Establishment and Strengthening of Veterinary Hospitals & Dispensaries - Mobile Veterinary Units (ESVHD-MVU):** ESVHD-MVU is envisaged for delivery of veterinary services at the farmers' doorstep through 1962 Toll-free No.
 - 4.3.2.3. **Assistance to States for Control of Animal Diseases (ASCAD):** Under ASCAD financial assistance is provided to States & UTs for controlling zoonotic, exotic, emergent, and economically important diseases other than those under NADCP and CADCP. This includes strengthening of diagnostic labs, surveillance, outbreak containment, and compensation to farmers for culling affected animals.

5. Supporting Dairy Cooperatives & Farmer Producer Organizations (SDC&FPO)

- 5.1. The Supporting Dairy Cooperatives and Farmer Producer Organizations (SDCFPO) scheme was launched in 2017–18 with the objective of assisting Cooperative Societies and Farmer

Producer Organizations (FPOs) engaged in dairy activities by providing soft working capital loans to help manage crises arising from adverse market conditions or natural calamities.

- 5.2. In response to the economic impact of COVID-19 on the dairy sector, the Ministry of Fisheries, Animal Husbandry and Dairying introduced Component "B" – Interest Subvention on Working Capital Loans for the Dairy Sector in 2020–21, with an outlay of ₹203 crore. Simultaneously, Component "A" (Working Capital Loan) has been kept in suspension since 2020–21.
- 5.3. Subsequently, the Union Cabinet approved the implementation of this scheme as part of the umbrella Infrastructure Development Fund for the period 2021–22 to 2025–26, with a total outlay of ₹500 crore (i.e., ₹100 crore per year).
- 5.4. Under Component "B", a 2% interest subvention per annum is provided on working capital loans availed by Producer Owned Institutions (POIs). Additionally, an extra 2% interest subvention is awarded to borrowers who ensure prompt and timely repayment at the end of the loan servicing period.
- 5.5. The Supporting Dairy Cooperatives and Farmer Producer Organizations (SDC&FPO) scheme aims to assist Cooperative Societies and Farmer Producer Organizations (FPOs) engaged in dairy activities by providing interest subvention on working capital loans, particularly in the aftermath of crises such as the COVID-19 pandemic. The scheme is designed to ensure stable market access for dairy farmers by enabling cooperatives and FPOs to maintain timely payments to farmers and continue milk procurement at remunerative prices, even during periods of high supply such as the flush season.

Genesis of the Study

6. Genesis of the Independent Third-Party Evaluation

- 6.1. In view of evaluating the effectiveness, outcomes, and areas for improvement within LHDCP and SDC&FPO schemes and to present an independent third-party evaluation report to department to present its scheme outcomes on the ground to 16th Finance Commission for further continuation (in the existing form or with modification as required) or to discontinue of respective schemes, QCI proposes a time bound and effective & independent third-party evaluation of following schemes:
 - 6.1.1. Livestock Health Disease Control Program (LHDCP) Scheme
 - 6.1.2. Supporting Dairy Cooperatives & Farmer Producer Organizations (SDC&FPO)

7. Potential Outcomes through Evaluation Study

- 7.1. Assess the implementation status and on-ground outcomes of the respective schemes.
- 7.2. Capture beneficiary-level experiences and feedback on the schemes.
- 7.3. Identify operational bottlenecks, highlight best practices, and recommend improvements for future policy iterations.
- 7.4. Provide evidence-based insights on the respective scheme's contribution to the dairy sector's growth and sustainability.

Objectives & Scope of Work for the Third-Party Evaluation

8. Livestock Health Disease Control Program (LHDCP)

8.1. Objective of the Study for LHDCP

- 8.1.1. To study and evaluate / appraise the impact of different components of LHDCP on the targeted objects in terms of both quantitative and qualitative factors.
- 8.1.2. To do the physical assessment of infrastructure created under LHDCP on sample basis.
- 8.1.3. To undertake an output-outcome analysis of LHDCP as per the objectives of the scheme.
- 8.1.4. To assess if the funds released by GoI under LHDCP has been utilized as per the Scheme Guidelines / Operational Guidelines / Financial Management Manual and only for the purposes for which the funds were provided.
- 8.1.5. To study the gaps in implementation if any, qualitative aspects of implementation, suggest measures for improvement in the future, and highlighting best practices through case studies.
- 8.1.6. To give suitable recommendations for the continuation / modification / discontinuation of components / activities of the scheme.

8.2. Scope of Work for LHDCP Scheme Evaluation

- 8.2.1. Review program documents, guidelines, and reports to gain a comprehensive understanding of the program's objectives, strategies, and implementation modalities.
- 8.2.2. Conduct field visits to project sites across different regions in India to assess the on-ground implementation of the Program.
- 8.2.3. Collecting and analyzing relevant data and information from various stakeholders, State Animal Husbandry Departments, Farmers, Veterinary Professionals, Program Managers, and Government Officials participating under the program.
 - 8.2.3.1. Whether process followed in scheduling the vaccination and other logistics so that same are available before the commencement of the vaccination campaign – whether accessories, logistics, cold chain continuity of vaccines, training of manpower arranged beforehand; whether vaccination calendar prepared beforehand for all 4 vaccination programmes which are 100% centrally funded.
 - 8.2.3.2. Whether vaccination is delivered at farmers doorstep, where there are no camps or nearby hospitals and if any fees charged for vaccination.
 - 8.2.3.3. Whether farmer/livestock keepers are aware of importance of ear tagging, vaccination, and when & where vaccination and other veterinary health services can be availed; are they aware of 1962 call number? What are the means of creating awareness for ear tagging, vaccination among farmers were followed by states?
 - 8.2.3.4. Whether facilities at all laboratories engaged in the sero-monitoring/ surveillance work are available with adequate liaising among concerned ICAR laboratories/ ICAR-NIVEDI, etc.

- 8.2.3.5. Are systems in place for the regulatory movement of animals, wherever required?
- 8.2.3.6. Whether quality vaccines used under the programme are kept and carried under the programme are kept and carried till the last-mile in prescribed cold chain conditions.
- 8.2.3.7. Whether remunerators to vaccinators have been distributed as envisaged under the scheme.
- 8.2.3.8. Time taken by vaccinators in uploading data on Bharat Pashudhan Portal data base. Physical verification of data entered by vaccinators from the field will be done.
- 8.2.3.9. Physical verification of animals covered under the programme in at least 10 villages per sampled districts (two) of the sampled states in respective zones (North, Central, East, West, South, & North East).
- 8.2.3.10. Report constraints, if any, faced by the States in ear-tagging of the animals.
- 8.2.3.11. How suspected outbreak is investigated and specimens arranged to be sent for laboratory confirmation.
- 8.2.3.12. What are monitoring & supervision plan for Mobile Veterinary Units (MVUs) at state level, whether call center(s) operational in the State and is an App/CRM system in place?
- 8.2.3.13. How much time does it take for the Mobile Veterinary Unit (MVU) to arrive after call is made and whether on-site basic medicines provided for treatment?
- 8.2.3.14. Availability of medicines and equipment in Mobile Veterinary Units (MVUs). Also, mode of operation of MVUs in respective states- Call or Route based.
- 8.2.3.15. Status of vaccination against state-prioritized economically important disease & livestock poultry and zoonotic diseases.
- 8.2.3.16. Steps taken for strengthening disease diagnostic laboratories and how many veterinarians/ paravet trained from funding under ASCAD.
- 8.2.3.17. Whether compensation given to the farmers against culling of animals, if any?
- 8.2.3.18. Whether awareness generation have been organized by the States as per sanction orders.
- 8.2.3.19. How often state nodal officer and/or senior officials of State Animal Husbandry Department carry out a monitoring visit to each district/ block etc.?
- 8.2.3.20. Is there any integration of the programme with other scheme for rural development/ PRI or convergence with other State/Central Department agencies?
- 8.2.3.21. Whether financial and other resources from other Departments/ Ministry/ Agency obtained by the States for strengthening of the programme (like RIDF, interest free loans to states for capital expenditure from MoF etc.)

- 8.2.3.22. Perception of Stakeholders (beneficiaries) in terms of their requirements from the project. What benefits do farmers see from vaccination and ear tagging?
- 8.2.4. Assessment of the program's impact on key performance indicators, such as vaccination coverage, farmers benefitted, and animals treated etc.
- 8.2.5. Role & performance of Programme Implementing Agencies, Programme Logistics Agency, and Programme Management Agency as per the scheme guideline as per the project.
- 8.2.6. Identifying successful practices, innovations, and lessons learned from the implementation of the program to inform future interventions and replication in other regions or countries.
- 8.2.7. Providing actionable recommendations for enhancing the program's effectiveness, efficiency, and sustainability.

9. Supporting Dairy Cooperatives & Farmer Producer Organizations (SDC&FPO)

9.1. Objective of the Study for SDC&FPO

- 9.1.1. To study and evaluate/appraise the impact of component B of SOC&FPO scheme on leveraging the Working Capital requirements of Dairy Cooperatives and Farmer Producer Organization engaged in dairy activities.
- 9.1.2. To do the physical assessment of implementation procedure so as to ensure it is conducted as per guidelines of the scheme.
- 9.1.3. To undertake an output-outcome analysis of SDC&FPO scheme as per the objectives of the scheme.
- 9.1.4. To assess that the funds released by GoI under SDC&FPO scheme has been utilized as per the SDC&FPO Scheme Guidelines/ Operational Guidelines/ Financial Management Manual and only for the purposes for which the funds were provided, assess diversion or duplication in project implementation if any.
- 9.1.5. To study the gaps in implementation if any, qualitative aspects of implementation, and suggest measures for improvement in the future.
- 9.1.6. To give suitable recommendations for the continuation/ modification/ dis-continuation of components / activities of the scheme.

9.2. Scope of Work for SDC&FPO

- 9.2.1. Review program documents, guidelines, and reports to gain a comprehensive understanding of the program's objectives, strategies, and implementation modalities.
- 9.2.2. Conduct field visits to project sites across different regions in India to assess the on-ground implementation of the Program.
- 9.2.3. Collecting and analyzing relevant data and information from various stakeholders like Bank/ Financial Institutions, NDDDB, Participating Agencies, and relevant State Departments and Government Officials participating under the program.
- 9.2.4. Identifying successful practices, innovations, and lessons learned from the implementation of the program to inform future interventions and replication in other regions or countries.

- 9.2.5. Providing actionable recommendations for enhancing the program's effectiveness, efficiency, and sustainability.

Methodological Framework

10. Research design and approach

- 10.1.** To conduct a robust evaluation of the **Livestock Health Disease Control Program (LHDCP)**, and **Supporting Dairy Cooperatives & Farmer Producer Organizations (SDCFPO)**, QCI proposes a comprehensive methodological framework rooted in a mixed-methods research design. This approach leverages both quantitative and qualitative data to assess the programme's implementation, outcomes, and stakeholder experiences. The framework is designed to ensure evidence-based insights, regional representativeness, and practical recommendations.
- 10.2.** The evaluation will follow a triangulation-based model, incorporating:
- 10.2.1.** Research (Primary & Secondary)
 - 10.2.1.1.** Primary research (on-field assessments, beneficiary interviews, KIs, FGDs)
 - 10.2.1.2.** Secondary research (review of policy documents, scheme guidelines, reports)
 - 10.2.2.** Expert/stakeholder consultations (including SIAs, milk federations & unions, DAHD officials, state & district level officials)
 - 10.2.3.** Financial Assessment (assessment of funds released by GoI under LHDCP and SDCFPO and its utilization as per their respective Scheme Guidelines/ Operational Guidelines/ Financial Management Manual and only for the purpose the fund was provided)
- 10.3.** Triangulation Approach will offer a comprehensive analysis of respective Scheme, by integrating primary research, secondary research, and expert/stakeholder consultations.

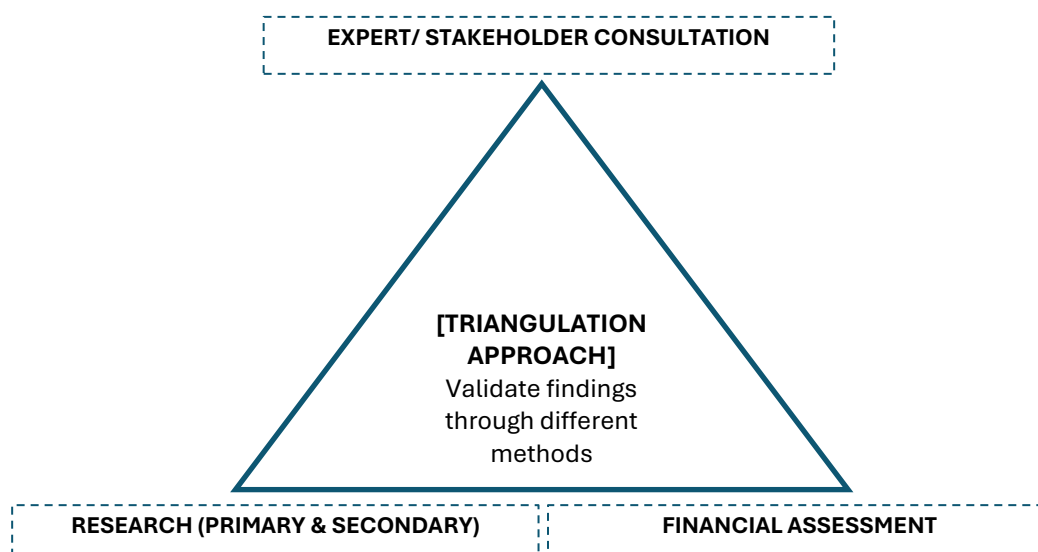


Figure 2: Triangulation Approach

- 10.4.** This blended approach ensures a multi-perspective understanding of the programme, helping validate findings, highlight best practices, and identify areas for policy strengthening.

11. Proposed Activities/Actions and Expected Insights

Table 1: Proposed Activities/Action and Expected Insights from Third-Party NPDD Scheme Evaluation

Sr. No.	Research Method	Activities/Actions	Expected Insights
1	Research (Primary & Secondary)	- Review scheme documents, DPRs, fund release orders, monitoring reports, operational manuals, and MIS data. - Design and deploy structured & semi-structured evaluation framework & tools (questionnaires, discussion guides) - Conduct primary data collection via household surveys, KIs, and FGDs.	- Contextual understanding of implementation models across states (sample basis). - Trends in fund disbursement, utilization, and physical achievement. - Ground-level feedback from beneficiaries and implementing agencies.
2	Output-Outcome cum Gap Analysis	- Develop a Framework Matrix aligned with scheme objectives and components. - Map outputs (e.g., infrastructure created) to outcomes (e.g., increased procurement, improved milk quality). - Analyze data through comparative and time-series aspects.	- Degree of alignment between intended and actual outcomes. - Effectiveness of infrastructure in meeting programme objectives. - Identification of areas where output hasn't translated into impact. - Identification of Gaps (if any) in implementation of the scheme.
3	Financial Assessment	- Review fund allocation, release, and utilization reports. - Assess compliance with financial guidelines and fund flow processes. - Examine utilization certificates, audit records, and potential duplication/ diversion of funds.	- Efficiency and timeliness of financial processes. - Financial compliance across implementing agencies. - Insights into potential bottlenecks in fund usage or reporting.
4	Stakeholder & Expert Consultation	- Conduct consultations with DAHD, NDDB, SIAs, Milk Federations, Milk Unions, and DCSs. - Hold expert panels and roundtables with domain specialists in dairy economics and cooperative governance. - Analyze qualitative feedback and policy suggestions.	- Strategic and operational feedback from key Informants. - Identification of systemic challenges and good practices. - Recommendations for future policy improvement. - Identification of successful practices, innovation & lessons learned.

12. Identification of Stakeholders

To ensure a comprehensive and grounded evaluation of the **Livestock Health Disease Control Program (LHDCP)** and **Supporting Dairy Cooperatives & Farmer Producer Organizations (SDCFPO)** schemes, QCI has identified the following key stakeholders for structured interactions and consultations:

- Department of Animal Husbandry and Dairying (DAHD) – Central Nodal Ministry
- State Animal Husbandry Departments – State Nodal Departments
- District Animal Husbandry Offices – District Level Nodal Officials
- National Dairy Development Board (NDDB) – Scheme Implementation Agency for SDC&FPO
- Milk Federations and Milk Unions/ Milk Producing Companies – Key institutional intermediaries in dairy value chains, responsible for procurement, processing, and distribution of milk, and facilitating linkages between producers (DCSs) and markets
- Dairy Cooperative Societies (DCSs) – Grassroots-level implementing and beneficiary interface
- Beneficiary Farmers/ Animal Owners – End users and direct recipients of scheme benefits
- Subject Matter Experts and Policy Advisors – Specialists in dairy economics, cooperative management, and infrastructure governance

These stakeholders will be engaged through in-depth interviews, focus group discussions (FGDs), and field-level interactions to gather diverse and meaningful insights across operational, financial, and policy dimensions of the programme.

Sampling

For the purpose of ensuring balanced regional representation, QCI proposes to divide the country into six zones, namely *North, Central, South, East, West, & North East* as per the NSSO guidelines and aspirational districts/ blocks will be kept in mind.

The final selection of states and districts will be undertaken in consultation with the Department of Animal Husbandry and Dairying (DAHD). However, to initiate the planning process, QCI proposes the following indicative sampling distribution across levels for respective zones.

13. Sampling Strategy for Livestock Health Disease Control Program (LHDCP)

To ensure national representation and capture regional diversity, the proposed sampling framework adopts a zone-based, multi-stage stratified sampling approach. The sampling plan is as follows:

- No. of States/UTs: 20
- No. of Villages: 400
- No. of Districts: 40
- No. of Farmers: 4000

13.1. Proposed Sampled States & Districts for LHDCP Scheme Evaluation

The following is the proposed distribution of states and districts for field data collection, aligned with the zonal sampling strategy. Final selection will be undertaken in consultation with DAHD.

Table 2: Proposed Sampled States & Districts for LHDCP Scheme Evaluation

S. No.	Zone	Proposed State
1	North	Haryana, Jammu & Kashmir, Punjab, Rajasthan
2	Central	Madhya Pradesh, Uttarakhand, Uttar Pradesh
3	East	Bihar, Odisha, West Bengal
4	West	Goa, Gujarat, Maharashtra
5	South	Andhra Pradesh, Karnataka, Tamil Nadu, Telangana
6	North East	Assam, Sikkim, Tripura

14. Sampling Strategy for Supporting Dairy Cooperatives & Farmer Producer Organizations (SDCFPO)

To ensure national representation and capture regional diversity, the proposed sampling framework adopts a zone-based, multi-stage stratified sampling approach. The sampling plan includes assessment at milk federation & milk union/ milk producing companies level as per the proposed sampled states:

14.1. Proposed Sampled States & Districts for SDCFPO Scheme Evaluation

The following is the proposed distribution of states and districts for field data collection, aligned with the zonal sampling strategy. Final selection will be undertaken in consultation with DAHD.

Table 3: Proposed Sampled States & Districts for SDCFPO Scheme Evaluation

Sr. No.	Zone	States/UTs	No. of Supported Milk Unions/ Milk Producer Companies	Sampled Milk Unions / Milk Producer Companies
1	North & Central	Haryana	1	1
2		Madhya Pradesh	1	1
3		Punjab	6	2
4	South	Andhra Pradesh	3	2
5		Karnataka	12	3
6		Tamil Nadu	4	2
7	East	Bihar	6	2
8	West	Gujarat	12	3
9		Maharashtra	2	2
10		Rajasthan	8	2
	Total		55	20

Operational Framework & Execution Plan

To ensure timely, efficient, and high-quality execution of the evaluation, QCI proposes a structured operational framework comprising the following key stages:

15. Preliminary Analysis and Development of Evaluation Framework

A preliminary exploratory review will be conducted through consultations with key stakeholders and a scan of existing documents. Based on this, an Evaluation Framework will be developed, outlining the key indicators, domains of inquiry, and analytical models aligned with respective scheme objectives and scope of work.

16. Preparation and Optimization of IT Platform

QCI will deploy latest and most convenient technology platforms for the digital data collection via mobile/tablet-based platform to execute the study that includes real time monitoring of the study to maintain the highest level of accuracy. The approved questionnaires shall be uploaded onto the CAPI platform with all necessary checks and balances, leaving no room for error. It shall include features such as flagging, geo-

tagging, time-stamping of images, short (30 seconds) video-recording, and real-time monitoring of the primary collected data to maintain the integrity of the data captured.

17. Pilot Study

A pilot study will be conducted to check the effectiveness of the questionnaire and the data collection tools for respective schemes under third-party evaluation. The learnings and observations from the pilot study will be shared with the DAHD & concerned divisions for inputs (if any). It will be helpful to identify and address the probable challenges, resolve the bottlenecks, and make the evaluation study smooth and seamless. The inputs and recommendations from DAHD & concerned divisions will be further incorporated in the study.

18. Training and Deployment of Assessors

A team of enumerators and field supervisors will undergo detailed training on scheme objectives, survey tools, digital platforms, and ethical guidelines. Deployment will be staggered across zones to ensure coordinated and high-quality data collection.

19. Primary Survey, Stakeholder Interviews and Focus Group Discussions (FGDs)

Extensive field surveys/ interviews will be conducted with identified beneficiaries and stakeholders across sampled locations. This includes structured interviews with farmers, Dairy Cooperative Society (DCS) members, district level milk union and state level federation officials, implementing agencies like NDDB, and implementation personnel at district & state level on behalf of State Animal Husbandry Departments.

Focus Group Discussions (FGDs) will be organized to complement quantitative data with collective qualitative insights. These discussions will focus on implementation experiences, challenges, and context-specific dynamics among key stakeholder groups.

20. Data Quality Assurance

A dedicated team of professionals will be deployed at the QCI headquarters for real-time monitoring of the interviews and feedback to the ground team of interviewers. The collected data will be quality checked in real time by the QCI professional at the backend and will be further re-checked at multiple levels by the experienced quality check professionals to eliminate the margin of error and maintain the quality and authenticity of the data.

During the on-ground assessment, a team of senior QCI professionals will visit the locations for monitoring and providing the required support where the interviewers will be deployed for assessment.

21. Data Analysis and Interpretation

The data collected through the primary survey will be collated and analyzed using appropriate statistical and thematic techniques for drawing observations and suggestions for the report as per the respective scheme objectives.

22. Final Reporting

Findings will be synthesized into a comprehensive report, including insights, best practices, and actionable recommendations. A stakeholder presentation will be made before final submission of the evaluation report, datasets, case studies, and supporting annexures.

Brief Work Plan & Key Deliverables

23. Project Timelines for Third-Party Evaluation of respective Schemes

QCI proposes 3 months implementation plan from the date of the award of work for the successful execution of activities including key activities like conceptualization and development of evaluation framework including schedules/questionnaires, training of assessors and deployment/mobilization plan of resources, pilot, improvisation based on pilot experiences, field survey, data analysis and reporting after the contract is awarded. Mentioned below is the timeline breakup (*the timeline is subject to cooperation from DAHD, including necessary approvals and review*).

Table 4: Brief Work Plan with Key Activities & Deliverables for Independent Third-Party Evaluation each respective Schemes

Key Activity	Activity Start (Months)	Activity End (Months)	Duration (Months)	Key Deliverable
Framework development & Submission of Inception Report	0	0.5	0.5	Inception Report
On-Field Assessment & Stakeholder Consultation	0.5	2.25	1.75	Mid-term Report & Presentation
Preparation of Draft Report	1	2.5	1.5	Draft Report
Presentation before DAHD (seeking comments on the Draft Report)	2.5	2.75	0.25	Presentation on Draft Report
Submission of Final Report	2.75	3	0.25	Final Report
Total		3 Months		

Graphical representation of the project timelines are as follows:

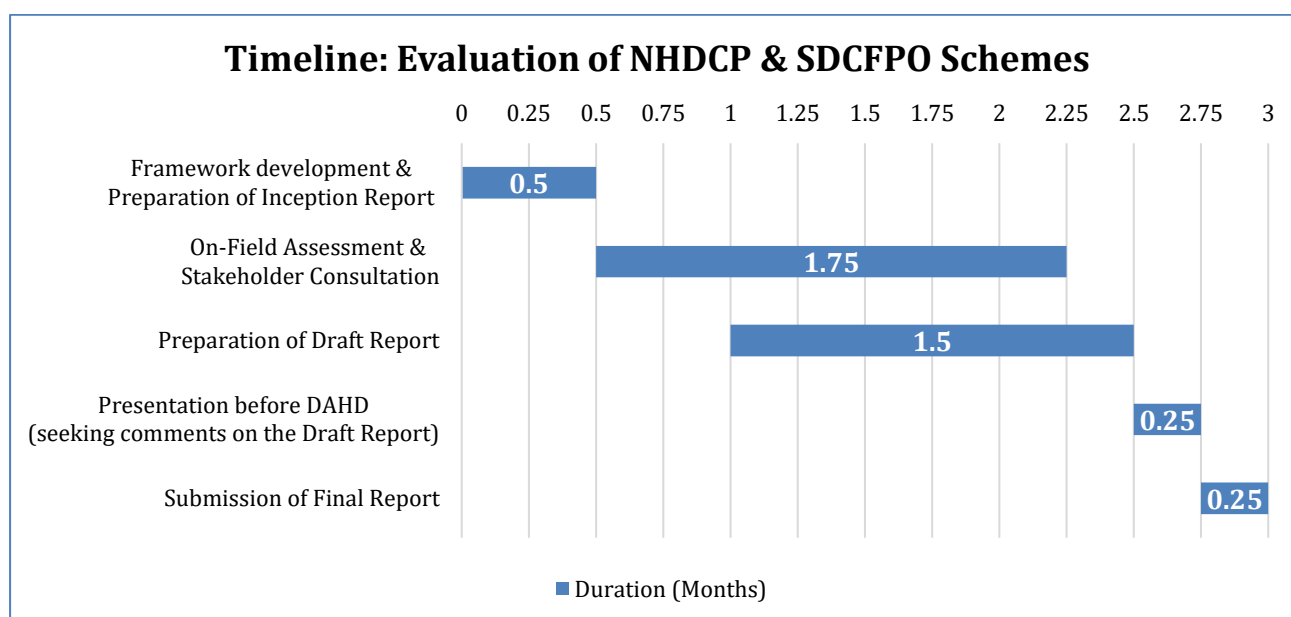


Figure 3: Project Timelines for Third-Party Evaluation of the NHDPC & SDCFPO

Financials

The total cost for conducting the Third-Party Evaluation of the **Livestock Health Disease Control Program (LHDCP)** and **Supporting Dairy Cooperatives & Farmer Producer Organizations (SDCFPO)** are proposed to be borne by the Department of Animal Husbandry and Dairying (DAHD), Ministry of Fisheries, Animal Husbandry and Dairying, Government of India (GoI).

24. Project Financials for Livestock Health Disease Control Program (LHDCP)

The brief summary of the project financials is as follows:

Table 5: Estimated Project Financials for LHDCP Scheme

Estimated Project Financials					
A. Third-Party Evaluation (Assessment/Survey, KII & FGD) Cost					
Sr.	Heads and Particulars	Proposed Sample Size	Required Man-Days	Man-Day Rates	Total (INR)
A1.	On-Field Beneficiary Farmers Survey	4000	400	Rs. 4,000/-	Rs. 16,00,000/-
A2.	Districts Animal Husbandry Department	40	80	Rs. 8,000/-	Rs. 6,40,000/-
A3.	State/UT Animal Husbandry Department	20	80	Rs. 8,000/-	Rs. 6,40,000/-
A4.	DAHD & Ministry of Fisheries, Animal Husbandry & Dairying, GoI	1	12	Rs. 8,000/-	Rs. 96,000/-
Fixed Cost (A)					Rs. 29,76,000/-
B. Third-Party Evaluation (Field Travel & Logistics) Cost					
Sr.	Heads and Particulars	Required Number	Rate	Total (INR)	
B1.	Air Travel/ Inter State Taxi	72	Rs. 7,500/-	Rs. 5,40,000/-	
B2.	Railway Travel for Intra District Travel	72	Rs. 2,000/-	Rs. 1,44,000/-	
B3.	Intra District (Local) Taxi	144	Rs. 3,000/-	Rs. 4,32,000/-	
B4.	Hotel Accommodation	144	Rs. 4,500/-	Rs. 6,48,000/-	
B5.	Food/Daily Allowance	288	Rs. 1,500/-	Rs. 4,32,000/-	
Fixed Cost (B)					Rs. 21,96,000/-
C. Subject Matter Expert					
S. No.	Heads and Particulars	Number	Required Man-Days	Rate	Total (INR)

C1.	Subject Matter Expert	10	8	Rs. 8,000/-	Rs. 6,40,000/-
Fixed Cost (C)					Rs. 6,40,000/-
D. Project Implementation Team					
S. No.	Heads and Particulars	Number	Months	Avg. Rate (Monthly)	Total (INR)
D1.	Director/ Sr. Director	0.25	3	Rs. 3,00,000/-	Rs. 2,25,000/-
D2.	Deputy / Assistant Director	0.25	3	Rs. 1,50,000/-	Rs 1,12,500/-
D3.	Project Manager	1	3	Rs. 1,00,000/-	Rs. 3,00,000/-
D4.	Associate Manager	2	3	Rs. 88,000/-	Rs. 5,28,000/-
D5.	Project Analyst	2	3	Rs. 55,000/-	Rs. 3,30,000/-
D6.	Project Coordinator	4	3	Rs. 40,000/-	Rs. 4,80,000/-
Fixed Cost (D)					Rs. 19,75,500/-
E. Other Associated Cost					
Sr.	Heads and Particulars				Total (INR)
E1.	Pilot Study & Enumerator Training Cost				Rs. 3,56,000/-
E2.	Technology & Reporting Cost				Rs. 3,92,000/-
E3.	Misc. Office Exp.				Rs. 1,50,000/-
E4.	QCI Support Cost (incl. Office Space, HR, Finance, etc.)				Rs. 10,46,446/-
E5.	QCI Admin Overhead Cost				Rs. 7,32,512/-
Fixed Cost (E)					Rs. 26,76,958/-
Total (Exclusive of GST)					Rs. 1,04,64,458/-
GST (@18%)					Rs. 18,83,602/-
Grand Total (Inclusive of GST)					Rs. 1,23,48,060/-
Total Amount (in Words): One Crore Twenty-Three Lakhs Forty-Eight Thousand Sixty Only					

Note:

- In the event of any extension in project timeline or scope, additional charges will be applicable on a pro-rata basis.
- The above financials do not include any additional costs related to:
 - Dashboard or portal development, if required separately.

25. Project Financials for Supporting Dairy Cooperatives & Farmer Producer Organizations (SDCFPO)

The brief summary of the project financials is as follows:

Table 6: Estimated Project Financials for SDCFPO Scheme

Estimated Project Financials					
A. Third-Party Evaluation (Assessment, KII & FGD) Cost					
Sr.	Heads and Particulars	Proposed Sample Size	Required Man-Days	Man-Day Rates	Total (INR)
A1.	Concerned DAHD & Ministry of Fisheries, Animal Husbandry & Dairying	1	4	Rs. 8,000/-	Rs. 32,000/-
A2.	National Dairy Development Board (NDDB)	1	4	Rs. 8,000/-	Rs. 32,000/-
A3.	Milk Federations	10	10	Rs. 8,000/-	Rs. 80,000/-
A4.	Milk Unions	20	40	Rs. 8,000/-	Rs. 3,20,000/-
A5.	Dairy Cooperative Society (DCS)	100	100	Rs. 4,000/-	Rs. 4,00,000/-
Fixed Cost (A)					Rs. 8,64,000/-
B. Third-Party Evaluation (Field Travel & Logistics) Cost					
Sr.	Heads and Particulars	Required Number	Rate	Total (INR)	
B1.	Air Travel/ Inter State Taxi	10	Rs. 7,500/-	Rs. 75,000/-	
B2.	Railway Travel for Intra District Travel	20	Rs. 2,000/-	Rs. 40,000/-	
B3.	Intra District (Local) Taxi	20	Rs. 3,000/-	Rs. 60,000/-	
B4.	Hotel Accommodation	20	Rs. 4,500/-	Rs. 90,000/-	
B5.	Food/Daily Allowance	40	Rs. 1,500/-	Rs. 60,000/-	
Fixed Cost (B)					Rs. 3,25,000/-
C. Subject Matter Expert					
S. No.	Heads and Particulars	Number	Required Man-Days	Rate	Total (INR)
C1.	Subject Matter Expert	2	5	Rs. 8,000/-	Rs. 80,000/-
Fixed Cost (C)					Rs. 80,000/-

D. Project Implementation Team					
S. No.	Heads and Particulars	Number	Months	Avg. Rate (Monthly)	Total (INR)
D1.	Director/ Sr. Director	0.1	3	Rs. 3,00,000/-	Rs. 90,000/-
D2.	Project Manager	0	3	Rs. 1,00,000/-	Rs. 0/-
D3.	Associate Manager	0	3	Rs. 88,000/-	Rs. 0/-
D4.	Project Analyst	1	3	Rs. 55,000/-	Rs. 1,65,000/-
D5.	Project Coordinator	2	3	Rs. 40,000/-	Rs. 2,40,000/-
Fixed Cost (D)					Rs. 4,95,000/-
E. Other Associated Cost					
Sr.	Heads and Particulars				Total (INR)
E1.	Technology & Reporting Cost				Rs. 72,000/-
E2.	Misc. Office Exp.				Rs. 50,000/-
E3.	QCI Support Cost (incl. Office Space, HR, Finance, etc.)				Rs. 2,27,229/-
E4.	QCI Admin Overhead Cost				Rs. 1,59,060/-
Fixed Cost (E)					Rs. 5,08,289/-
Total (Exclusive of GST)					Rs. 22,72,289/-
GST (@18%)					Rs. 4,09,012/-
Grand Total (Inclusive of GST)					Rs. 26,81,301/-
Total Amount (in Words): Twenty-Six Lakhs Eighty-One Thousand Three Hundred One Only					

Note:

- In the event of any extension in project timeline or scope, additional charges will be applicable on a pro-rata basis.
- The above financials do not include any additional costs related to:
 - Dashboard or portal development, if required separately.

26. Payment Structure:

The payment structure for the proposed methodology is outlined based on this timeline.

Table 7: Payment Structure for each respective Schemes (LHDCP & SDCFPO)

Sr. No.	Schedule / Milestones	Percentage (%) of Contract Value
1	Award of Work Order (Mobilization Advance)	20 %
2	Submission of Draft Report	30 %
3	Submission & Approval of Final Report	50 %

Note:

- The schedule/milestones mentioned earlier under “Brief Work Plan & Key Deliverables (point no. 23)” will be applicable to the total cost.
- Any term/condition that is unaccounted for would not be considered waived and would be determined in consultation with both parties.

Annexures

27. QCI's Previous Projects with DAHD

27.1. Third-Party Evaluation of National Programme for Dairy Development (NPDD) Scheme

Work Order NPDD Scheme Evaluation

No. M-01004/2/2024-DADF-Dept (E-27769)
Government of India
Ministry of Fisheries, Animal Husbandry & Dairying
Department of Animal Husbandry & Dairying
(Dairy Division)

Krishi Bhawan, New Delhi-110001
Dated, the 06th June 2025

To,

M/s Quality Council of India
2nd Floor, Institution of Engineers Building
2- Bahadur Shah Zafar Marg, New Delhi - 110002.

Subject: Appointment of M/s Quality Council of India (QCI) for Mid-term Evaluation of Central Sector Scheme- National Programme for Dairy Development (NPDD) implemented by the Department of Animal Husbandry and Dairying (DAHD)-reg

Sir,

I am directed to convey the approval of the competent authority for appointment of M/s Quality Council of India as an Agency for Mid-Term Evaluation of Central Sector Scheme- National Programme for Dairy Development (NPDD) implemented by the Department of Animal Husbandry and Dairying (DAHD) with the terms and conditions indicated in **Annexure**.

2. Statutory tax/ GST will be applicable as per GST rules. M/s QCI will provide the name of all project team members for the duration of project before the start of the project to enable them entry-pass of DAHD.
3. An agreement between DAHD and M/s QCI regarding terms and condition will be finalized by M/s QCI and signed by DAHD & M/s QCI both.
4. The payment of project fee shall be paid by DAHD as per the mechanism stipulated in Para 6 of Terms and Conditions for Mid-term Evaluation of the scheme- National Programme for Dairy Development (NPDD) implemented by the Department of Animal Husbandry and Dairying (DAHD) (**Annexure**).
5. This issues with the approval of the competent authority and concurrence of AS&FA vide File No. E-27769 Note#70 dated 25.05.2025.

Encl: a/a

Yours faithfully,

(Signature)
(Dayanand Appa Sawant)

Deputy Commissioner (Dairy Development)

Copy to:

1. Sr.PPS to Secretary (AHD); PPS to Additional Secretary (C&DD); PSO to AS&FA
2. NIC for uploading the work order on Department's website

Copy for Information to:

1. PS to Hon'ble Minister of Fisheries, Animal Husbandry & Dairying
2. PS to Hon'ble MoS of Fisheries, Animal Husbandry & Dairying

Page 1 of 7

27.2. Third-Party Evaluation of Animal Infrastructure Development Fund (AHIDF) Scheme

Completion Certificate AHIDF Scheme Evaluation

217210/2024/ADMIN_1-DADF



सत्यमेव जयते

संयुक्त सचिव
भारत सरकार
मत्स्यपालन, पशुपालन एवं डेयरी मंत्रालय
पशुपालन एवं डेयरी विभाग
कृषि भवन, नई दिल्ली-110001
Joint Secretary
Government of India
Ministry of Fisheries, Animal Husbandry & Dairying
Department of Animal Husbandry and Dairying
Krishi Bhawan, New Delhi-110001

डॉ. ओ.पी. चौधरी
Dr. O.P. Chaudhary




D.O.No.AA-17/1/2023-NLM-DADF Dated.01.07.2024

Dear Mr. Hari Prakash Sir,

This completion certificate is to certify that the "Mid-Term Third-Party Evaluation of Animal Husbandry Infrastructure Development Fund (AHIDF)" as per the F. No.: AA-17/1/2023-NLM-DADF dated 23rd December 2023 was satisfactory concluded by Quality Council of India (QCI) and submitted all deliverables within the stimulated project timelines. QCI was selected for the said assessment through a competitive bidding process. The evaluation study was commenced on 2nd January 2024 and final report after the brief presentation was submitted on 28th March 2024. The project details are as follows:

- Project Name:** Third-Party Evaluation of Animal Husbandry Infrastructure Development Fund (AHIDF)
- Duration:** 3 Months
- Location:** PAN India
- Project Fee:** ₹ 87,68,816/- (Eighty-Seven Lakh Sixty-Eight Thousand Eight Hundred Sixteen Only)
- Key Components:** Impact Evaluation of the AHIDF Scheme on the overall creation/enhancement of capacities/capabilities associated with the following sectors:
 - Dairy Processing and Value Addition Industries
 - Meat Processing and Value Addition Industries
 - Breed Improvement Technology and Breed Multiplication Farm
 - Animal Feed Manufacturing Industries
 - Animal Waste to Wealth Management Units
 - Veterinary Vaccine and Drug Production Facilities
- Client:** Department of Animal Husbandry and Dairying (DAHD), Ministry of Fisheries, Animal Husbandry and Dairying, Government of India
- Scheme Budget:** ₹ 15,000 Crore for FY 2020-21 to 2022-23

2. QCI fulfilled all requirements and delivered the final report after a brief presentation, demonstrating comprehensive evaluation and adherence to project timelines.

3. This certificate is issued as recognition of QCI's commitment and professionalism in executing the evaluation study.

Warm Regards,

Dr. Hari Prakash
Director, PPID
Quality Council of India (QCI)



(Dr. O.P. Chaudhary)

1

File No. AA-17/1/2023-NLM-DADF, Contact No. +91-11-23387804, Fax: +91-11-23386115, E-mail: jspfdadf@gmail.com, jspf-dadf@nic.in
Generated from eOffice by LPI SAIKAWAL, DEPUTY COMMISSIONER(NLM-DADF), DEPUTY COMMISSIONER, DADF-DEPARTMENT on 01/07/2024 02:17 PM

F. No. AA-17/1/2023-NLM-DADF

Government of India

Ministry of Fisheries, Animal Husbandry and Dairying

Department of Animal Husbandry and Dairying

Chandralok Building, New Delhi.

Dated, the 23rd December, 2023

To,

M/s Quality Council of India

2nd Floor, Institution of Engineers Building

Bahadur Shash Zafar Marg, New Delhi – 110002.

Subject:- Appointment of an agency for evaluation study of Animal Husbandry Infrastructure Development Fund (AHIDF)

Sir,

I am directed to convey the approval of the competent authority for appointment of M/s Quality Council of India as a mid-term evaluation Agency for evaluation of AHIDF with the following terms and conditions including those mentioned under **Other Conditions**:

2. Terms of Reference (TOR) for the evaluation study are, as follows:

- i. Infrastructure created vis-à-vis the infrastructure requirement i.e., the infrastructure gap vis-à-vis the level of production of dairy/feed/meat poultry/agro-waste in the States
- ii. Capacity utilization of the assets created
- iii. Impact of the scheme across the value chains including the benefit flowing down the line
- iv. Impact on availability of milk and meat & poultry products to consumers
- v. Impact on unorganized dairy and meat & poultry sector
- vi. Impact on export promotion w.r.t to dairy and meat & poultry products
- vii. Availability of quality and cost-effective concentrated animals feed to the cattle, buffalo, sheep, goat, pig and poultry
- viii. The impact on the level of income of farmers and proportion of local farmers benefited directly and indirectly
- ix. The impact on generation of employment i.e., both in number and types of employment generated directly and indirectly.
- x. Recommendations for the overall improvement of the functioning of the scheme
- xi. The implementation/ operational difficulties on the ground and suggest/recommend corrective measures to improve efficiency of implementation
- xii. Suggestion on changes/modification in the Scheme Guidelines for timely & effective implementation of the scheme


अनामिका निगम / Anamika Nigam
 अधीन सचिव / Under Secretary
 भारत सरकार / Govt. of India
 मत्स्यपालन, पशुपालन एवं डेयरी विभाग
 Ministry of Fisheries, Animal Husbandry & Dairying
 पशुपालन और डेयरी विभाग
 Department of Animal Husbandry & Dairying
 क्रि. भवन, नई दिल्ली / Krishi Bhawan, New Delhi-110001

- xiii. Performance of the scheme based on the Output / Outcome indicators, among others, in the following format:

S.No.	Output	Outcome
a)	Number of applicants/beneficiaries/units supported for development of infrastructure	No. of Animal Husbandry and allied sector units operationalised
b)	Investment leveraged	Capacity Creation/enhancement
c)	Amount of interest subvention provided to beneficiaries	Employment Generated

NOTE: Site visits are envisaged as part of the Mid-term Evaluation Agency's scope of work.

Other Conditions:

- This work order of engagement of M/s Quality Council of India as Mid-term Evaluation Agency shall be valid for 3 (three) months from the date of acceptance of this work order. However, its performance as Mid-term Evaluation Agency shall be reviewed initially, after completion of 1 month from the date of acceptance of this work order by M/s Quality Council of India.
- All technical information and manuals, from time to time, shall be drawn up in English language.
- M/s Quality Council of India shall, at its sole cost and expense, deploy staff and personnel as indicated in the Technical Bids according to the requisite qualification mentioned in the Technical Bid of the company. The number of manpower to be provided has already been mentioned in the RFP. The manpower shall not be liable for frequent replacement unless the personal resigned from the post where has been deputed. In case of resignation, prior intimation at least one month before to be indicated to DAHD.
- M/s Quality Council of India shall ensure that the information/details related to the assignment which comes to the knowledge of M/s Quality Council of India or its personnel, during the course of provision of services under this work order, are kept confidential and are not, directly or indirectly, disclosed to any third party.
- If any dispute or difference of any kind whatsoever arises between DAHD and M/s Quality Council of India in connection with or arising out of or relating to or under this order, both parties shall promptly and in good faith negotiate with a view to its amicable resolution and settlement. In the event that no amicable resolution or settlement is reached within a period of thirty (30) days from the date on which the above mentioned dispute or difference arose, such dispute or difference shall be settled finally by Secretary, DAHD whose decision shall be final and binding.



अनामिका निगम / Anamika Nigam
 अवर सचिव / Under Secretary
 भारत सरकार / Govt. of India
 मत्स्यपालन, पशुपालन एवं डेयरी विभाग
 Ministry of Fisheries, Animal Husbandry & Dairying
 पशुपालन और डेयरी विभाग
 Department of Animal Husbandry & Dairying
 प्लॉट नं. 1, विट्ठल/विष्णु भिक्षा, नई दिल्ली-110001

- f) DAHD shall have the right to terminate the appointment vide this order by giving a notice of 15 (Fifteen) days in writing. In the event of termination of the appointment for reasons not solely attributable to M/s Quality Council of India, DAHD will reimburse all the expenses incurred by M/s Quality Council of India upon submission of appropriate evidence by M/s Quality Council of India. If the appointment is terminated due to reasons attributable solely to M/s Quality Council of India or in case of termination of the appointment by M/s Quality Council of India for reasons not solely attributable to DAHD, the latter will forfeit the performance security, if any, of M/s Quality Council of India.
- g) For carrying out services as Mid-term Evaluation Agency as per this order DAHD shall pay, M/S Quality Council of India @ Rs. 87,68,816/- (Rs. Eighty Seven Lakh Sixty Eight Thousand Eight Hundred Sixteen only) inclusive of all taxes as per terms of RFP for evaluation study of Animal Husbandry Infrastructure Development Fund (AHIDF).
- h) Rs 4,38,500/- (Rupees Four Lakh Thirty Eight Thousand Five Hundred only) shall be deposited by M/s Quality Council of India as Performance Security (equivalent to 5 (Five) percent of the cost of financial proposal) from a Nationalized/Scheduled Bank, before start of work on assignment, in form of a Bank Guarantee substantially in the form specified at Annexure A of the Work Order in RfP. Performance Security will be retained by DAHD until the completion of the assignment by the M/s Quality Council of India and be released 60 (Sixty) Days after the completion of the assignment.
- i) Work Order shall be issued, in duplicate, by the DAHD to M/ Quality Council of India and M/s Quality Council of India shall, within 3 (three) days of the receipt of the Work Order, sign and return the duplicate copy of the Work Order in acknowledgement thereof. In the event the duplicate copy of the Work Order duly signed by M/s Quality Council of India is not received within 3 (three) days of the receipt of the Work Order, DAHD may, unless it consents to extension of time for submission thereof, appropriate the Earnest Money Deposit of such Applicant in full or to the extent of mutually agreed pre-estimated loss and damage suffered by DAHD on account of failure M/s Quality Council of India to acknowledge the Work Order, and the next highest ranking Applicant shall be considered.
- j) Payments to M/s Quality Council of India
- DAHD will not consider advance payment to M/s Quality Council of India.
 - M/s Quality Council of India will submit pre-receipted invoices in triplicate, complete in all respects, on satisfactory completion of work, for necessary settlement to DAHD. Payment would be made by DAHD within 30 days of submission of invoice, subject to successful completion of the required work detailed in the RfP Document. The invoice should be submitted along with complete details of the work undertaken during the contract, supporting documents and bills (if required) as well



अनामिका निगम / Anamika Nigam
 अवर सचिव / Under Secretary
 भारत सरकार / Govt. of India
 मत्स्यपालन, पशुपालन एवं डेयरी विभाग
 Ministry of Fisheries, Animal Husbandry & Dairying
 पशुपालन और डेयरी विभाग
 Department of Animal Husbandry & Dairying
 हरी बल चौक दिल्ली / Haripur Chowk, Delhi

as copies of the work/ material / produced during the contract, for which the bills are submitted.

- iii. For facilitating Electronic transfer for funds, the M/s Quality Council of India shall be required to indicate the name of the Bank and Branch, account number (i.e. bank names, IFSC Code and Bank A/c No.) and also forward a cheque leaf duly cancelled to verify the details furnished to DAHD. These details should also be furnished on the body of bill submitted for payment by M/s Quality Council of India.
- iv. Currency: The price is payable to M/s Quality Council of India in local currency i.e. Indian Rupees.
- v. Payment for Additional Services: For the purpose of determining the remuneration due for additional services as may be agreed under relevant clauses for modification in this Work Order by DAHD.
- k) The Evaluation team of M/s Quality Council of India shall report to Joint Secretary, AHIDF for necessary directions.
- l) All future communications by M/s Quality Council of India shall be done with the office of Joint Secretary AHIDF (email jspf-dadff@nic.in, cc to lipi.s@gov.in).
- m) The conditions mentioned in RfP shall be considered to be integral part of this Work Order.

This issues with the approval of the Competent Authority and as concurred by IFD vide No. 117/25383 dated 18.12.2023.

Yours faithfully,



(Anamika Nigam)

Under Secretary to Government of India

Copy to:

- 1 PPS to Secretary, AHD
- 2 PPS to AS&FA, DAHD
- 3 PPS to Animal Husbandry Commissioner, DAHD
- 4 PPS to JS (NLM/PC)
- 5 JC (AH)/DC (AHIDF)
- 6 NIC for uploading the work order on Department's website

अनामिका निगम / Anamika Nigam
अवर सचिव / Under Secretary
भारत सरकार / Govt. of India
मत्स्यपालन, पशुपालन एवं डेयरी मंत्रालय
Ministry of Fisheries, Animal Husbandry & Dairying
पशुपालन और डेयरी विभाग
Department of Animal Husbandry & Dairying
एन सी ई विंग / NSE Wing, New Delhi-110001

Copy for Information to:

1. PPS to Hon'ble Union Minister for Fisheries, Animal Husbandry & Dairying
2. PPS to Hon'ble MoS for Animal Husbandry & Dairying

27.3. Screening of Applications received through online National Award Portal for National Gopal Ratna Award 2024, 2023, & 2022 (on Nomination Basis)

Work Order for National Gopal Ratna Award 2024

F. No. N-05015/114/2020-CDD (E-17998)
Government of India
Ministry of Fisheries, Animal Husbandry and Dairying
Department of Animal Husbandry and Dairying
R. No 532, Krishi Bhawan, New Delhi
Date: 3rd October, 2024

To,
The Secretary General,
Quality Council of India(QCI),
2nd Floor, Institution of Engineering Building,
Bahadurshah Zafar Marg, New Delhi.

Subject: Work order for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2024-reg.

Sir,

I am directed to refer to your proposal submitted vide e-mail dated 04.09.2024 on the above subject and to convey the approval of the Competent Authority for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2024 as under:

S No.	Scope of Work/Exercise	No. of Resources/ day	Duration (tentative) in days	Total fees to be paid by DAHD (Amount in Rs.)
1.	Updating the strategy and evaluation scorecard, in consultation with DAHD, and developing a detailed roadmap for timely execution of the project	4 (1 Project Lead and 3 Research Associate)	1 st – 15 th Oct 2024 (15 Days)	Rs. 4,20,000/- (Rupees four lakh twenty thousand only) (Exclusive GST)
2.	Data cleaning of applications received to find unique nominations			
3.	Scrutinizing and scoring of all the applications as per score card provided by DAHD (enclosed) and selecting top 20 applications from non- NER States and 10 applications from NER States in each of the three categories			
4.	Re-scoring and creating detailed profiles for selected top 20 applications from non- NER States and 10 applications from NER States (as instructed by DAHD) in each of the three categories-based post field verification i.e. on the basis of factual information collected by NDDB/DAHD.	4 (1 Project Lead and 3 Research Associate)	1 st -10 th Nov., 2024 (10 days)	
5.	Creating detailed profiles for the top 20 applications in each category for non-NER States and top 10 applications in each category for NER States based on the parameters mentioned in the objective for Award Screening Committee.			

1 /2...



-2-

2. Statutory tax/GST will be applicable as per GST rules. Resource cost is calculated by considering various factors- Professional fee, Promotion & Bonus, Logistical support like Travel & Food Allowance, Laptop, stationery and Phone Allowance e.t.c. The QCI will provide the name of all project team members for the duration of project before the start of the project to enable them entry-pass of DAHD. The undersigned is the nodal officer /contact point for the NGRA 2024.
3. If necessary, the time schedule may be reduced with the mutual consent of QCI & DAHD, accordingly, QCI will have to depute more manpower to complete the task within the given timeframe.
4. The QCI will provide scoring of all the applications and detailed profiles of the top 20 shortlisted applications in each category for non-NER States and top 10 applications in each category for NER States to DAHD in soft and hard copies, duly signed, on it's letter head.
5. The payment of project fee shall be paid by DAHD as 30% advance and remaining 70% after the satisfactory completion of the project.
6. An agreement between DAHD and QCI regarding terms and condition will be finalized by QCI and signed by DAHD & QCI both.
7. QCI is therefore requested to start the work as mentioned above right from the date of issue of this letter.
8. This issues with the approval of the competent authority and AS&FA vide Dy No. E-17998 Note#608 dated 01.10.2024.

Encl. Score card

Yours sincerely


(Ajith Kumar K.)
Assistant Commissioner (DD)
011-23383812
[e-mail : ajith.kk@gov.in]

Copy to:

1. The Joint Commissioner (RGM), DAHD, Krishi Bhawan NEW Delhi –With the request to make 30% advance payment to QCI from RMG head.
2. PPS to the Additional Secretary (CDD), DAHD

Work Order for National Gopal Ratna Award 2023

F. No. N-05015/114/2020-CDD (E-17998)
Government of India
Ministry of Fisheries, Animal Husbandry and Dairying
Department of Animal Husbandry and Dairying
R. No 532, Krishi Bhawan, New Delhi
Date: 12th October, 2023

To,
The Secretary General,
Quality Council of India(QCI),
2nd Floor, Institution of Engineering Building,
Bahadurshah Zafar Marg, New Delhi

Subject: Work order for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2023(to be conferred on 26.11.2023).

Sir,

I am directed to refer to your proposal vide e-mail dated 25.09.2023 on the above subject and convey the approval of the Competent Authority for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2023(to be conferred on 26.11.2023) as under:

S No.	Scope of Work/Exercise	No. of Resources/ day	Duration (tentative) in days	Total fees to be paid by DAHD (Amount in Rs.)
1.	Updating strategy and evaluation score card in consultation with DAHD, and developing a detailed roadmap for timely execution of the project.	4 (1 Project Lead and 3 Research Associate)	16 th -25 th Oct 2023 (10 Days)	Rs. 2,75,360/- (Rupees Two lakh seventy five thousand three hundred sixty only) (Inclusive of GST/all taxes)
2.	Data cleaning of applications received to find unique nominations.			
3.	Analyzing data provided by applicants, verifying claims made in the nominations via secondary research and looking for more relevant information via open search (social media, internet and other source platforms), while making the profiles.			
4.	Scrutinizing and scoring of all the received applications based on the evaluation score card and selecting top 20 applications in each of the three categories and handed over to the Award Screening Committee, DAHD.			
5.	Re-scoring and creating detailed profiles for selected top 20 applications in each category, post field verification by NDDDB/DAHD.	4 (1 Project Lead and 3 Research Associate)	11 th -15 th Nov,2022 (5 days)	

1 / 2...

Cond...

-2-

2. If necessary, the time schedule may be reduced with the mutual consent of QCI & DAHD, accordingly, QCI will have to depute more manpower to complete the task within the given timeframe.
3. The QCI will provide the name of all project team members for the duration of project before the start of the project to enable them entry-pass of DAHD. The undersigned is the nodal officer /contact point for the NGRA 2023.
4. The payment of project fee shall be paid by DAHD as 30% advance and remaining 70% after the satisfactory completion of the project.
5. An agreement between DAHD and QCI regarding terms and condition will be finalized by QCI and signed by DAHD & QCI both.
6. QCI is therefore requested to start the work as mentioned above right from the 16th October 2023.

This issues with the approval of the competent authority and AS&FA vide Dy No. E-17998 Note#.457 dated 10.10.2023

Yours sincerely



(Ajith Kumar K.)
Assistant Commissioner (DD)
011-23383812
[e-mail : ajith.kk@gov.in]

Copy to:

1. The Joint Commissioner (RGM), DAHD, Krishi Bhawan NEW Delhi –With the request to make 30% advance payment to QCI from RMG head before the closing date of the applications i.e 15th Oct-2023.
2. PPS to the Secretary(AHD)/ PPS to Additional Secretary (CDD), DAHD

Work Order for National Gopal Ratna Award 2022

N-050158114/2020-CDD(Part(1) [E-23066]
Government of India
Ministry of Fisheries, Animal Husbandry and Dairying
Department of Animal Husbandry and Dairying
(Dairy Division)

R. No 532, Krishi Bhawan, New Delhi

Date: 7th October, 2022

To,
The Secretary General,
Quality Council of India(QCI),
2nd Floor, Institution of Engineering Building,
Bahadurshah Zafar Marg,
New Delhi

Subject: Work order for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2022(to be conferred on 26.11.2022).

Sir,

I am directed to refer to your proposal vide e-mail dated 26.09.2022 on the above subject and convey the approval of the Competent Authority for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2022(to be conferred on 26.11.2022) as under:

S No.	Scope of Work/Exercise	No. of Resources/ day	Duration (tentative) in days	Total fees to be paid by DAHD (Amount in Rs.)
1.	Updating evaluation scorecard and checklist for field verification in consultation with DAHD, and developing a detailed roadmap for timely execution of the project.	4	11 th Oct - 20 th Oct 2022 (10 Days)	Rs. 2,04,848/- (Rupees two lakh four thousand eight hundred forty eight only) (Inclusive of GST/all taxes)
2.	Data cleaning of applications received to find unique nominations.			
3.	Analyzing data provided by applicants, verifying claims made in the nominations via secondary research and looking for more relevant information via open search (social media, internet and other source platforms), while making the profiles.			
4.	Scrutinizing and scoring of all the received applications and selecting top 20 applications (as instructed by DAHD) in each of the three categories and handed over to DAHD by 20 th Oct 2022 for field verification.			
5.	Creating detailed profiles for the top 20 applications in each category based on the parameters mentioned in the objective evaluation scorecard and on the basis of factual information collected via field verification by NDDB. To recommend best 20 applications in each category to the Award Screening Committee constituted by DAHD.	7	7 th -9 th Nov,2022 (3 days)	


1 /2...

Cond...

2. If necessary, the time schedule may be reduced with the mutual consent of QCI & DAHD, accordingly, QCI will have to depute more manpower to complete the task within the revised timeframe.
3. The QCI will provide the name of all project team members for the duration of project before the start of the project to enable them entry-pass of DAHD. The undersigned is the nodal officer /contact point for the NGRA 2022.
4. The payment of project fee shall be paid by DAHD as 30% advance and remaining 70% after the satisfactory completion of the project.
5. An agreement between DAHD and QCI regarding terms and condition will be finalized by QCI and signed by DAHD & QCI both.
6. QCI is therefore requested to start the work as mentioned above right from the 11th October 2022.

This issues with the approval of the competent authority and AS&FA vide Dy No. E-23066, Note#20 dated 06.10.2022.

Yours sincerely,


(Ajith Kumar K.)
Assistant Commissioner (DD)
011-23383812
[e-mail : ajith.kk@gov.in]


Copy to:

1. The Joint Commissioner (RGM), DAHD, Krishi Bhawan NEW Delhi –With the request to make 30% advance payment to QCI from RGM head (as per concurrence of AS&FA vide Dy No. E-23066, Note#20 dated 06.10.2022) before the closing date of the applications i.e 10th Oct-2022.
2. PPS to the Additional Secretary (CDD), DAHD

28. QCI's Previous Projects on Nomination Basis with different Ministries

28.1. National Horticulture Board (NHB), Ministry of Agriculture & Farmers Welfare, GoI

Completion Certificate cum Receipt of Payment

 राष्ट्रीय बागवानी बोर्ड National Horticulture Board NHB/CC/QCI/2024-25/ 14555	 कृषि एवं किसान कल्याण अफ़ैयर्स अफ़ैयर्स	राष्ट्रीय बागवानी बोर्ड कृषि एवं किसान कल्याण मंत्रालय, भारत सरकार 85, इन्स्टीट्यूशनल एरिया, सेक्टर-18, गुरुग्राम-122015 National Horticulture Board Ministry of Agriculture & Farmers Welfare, Govt. of India Plot No. 85, Sector-18, Institutional Area, Gurgaon-122015 By <u>Handel</u> March, 27 2025
To, M/s Quality Council of India 2nd Floor, Institution of Engineers Building, 2, Bahadur Shah Zafar Marg New Delhi-110002		
Sub:- Payment of Rs. 62,47,045/- to M/s Quality Council of India, New Delhi for conducting of 3rd Party evaluation for the Schemes of NHB for the years 2019-20 to 2022-23 -Reg.		
Sir, With reference to your letter dated 29.07.2024 regarding QCI's Invoices for the "Third Party Evaluation of the NHB Schemes 1 & 2 for the "FY 2019-20 to 2022-23". In this regard, I am directed to inform that the amount of Rs. 62,47,045/- (Rupees Sixty two lakh forty seven thousand and forty five only) (After deduction TDS@10% Rs. 5,89,344/- and IGST TDS@2% Rs. 1,17,870/-) vide APPA No. C012553145320 dated 01.02.2025 through NEFT/RTGS. Kindly acknowledge the receipt of the same. Thanking you Yours faithfully  (C.P. Gandhi) Joint Director (Coord)		



राष्ट्रीय बागवानी बोर्ड
National Horticulture Board

राष्ट्रीय बागवानी बोर्ड
कृषि एवं किसान कल्याण मंत्रालय, भारत सरकार
85, इंस्टीट्यूशनल एरिया, सेक्टर-18, गुडगाँव-122015
National Horticulture Board
Ministry of Agriculture & Farmers Welfare, Govt. of India
85, Institutional Area, Sector - 18, Gurgaon - 122015

NHB/HD/CC/QCI/2023-24

To

M/s Quality Council of India
2nd Floor, Institution of Engineers Building,
2, Bahadur Shan Zafar Marg,
New Delhi-110002

November 8, 2023

Subject : Work Award letter for conducting 3rd party evaluation for the schemes of NHB for the years 2019-20 to 2022-23 and also concurrent evaluation of the schemes for the year 2023-24 – reg.

Sir,

Kindly refer to the correspondence held between NHB and QCI on the subject, resting with your email dated 03.08.2023 with a final revised proposal for conducting 3rd party evaluation for the schemes of NHB for the years 2019-20 to 2022-23 and also your email/proposal dated 23.10.2023 for conducting concurrent 3rd party evaluation for the projects funded by NHB during the year 2023-24. Copies of the both the proposals are attached herewith for ready reference.

In this regard, I am directed to convey the approval of competent authority to the following projects for conducting above said 3rd party evaluation:

Project – I : Conducting 3rd party evaluation for the schemes of NHB for the years 2019-20 to 2022-23

Schemes	Total Population	Sample size (at 95% CL and 5% MoE)	Population component
Scheme I	1094	285	Open Field Cultivation, Protected Cultivation, PHM, Primary Processing Units, & Others
Scheme II	127	96	Cold Storage establishment
Total	1221	381	

NHB shall make payment of Rs. 58,93,440/- plus GST for the above assignment as per following details:-

Sl. No.	Activity	Total Cost
1	Professional & Quality Control Cost	₹ 16,65,000.00
2	Assessment Cost	
2.1	Assessment of Scheme- I (285 Projects)	₹ 21,66,389.00

.../- *[Signature]*

दूरभाष / Tel. : (0124) - 2347439-42, 2343416-17, 2342989-92, 2343414, 2348313, 2341209, 2341239, 2343348

फैक्स / Fax: (0124) - 2342991, ईमेल / E-mail: md@nhb.gov.in

वेबसाइट / Website: www.nhb.gov.in

2.2	Assessment of Scheme- II (96 Projects)	₹ 12,30,611.00
3	Technology, IT Infrastructure, & Reporting Cost	₹ 2,00,000.00
QCI Admin Cost @12%		₹ 6,31,440.00
Total Project Cost		₹ 58,93,440.00*
		+ Applicable Taxes.

Project - 2 : Conducting concurrent 3rd party evaluation for the schemes of NHB during the year 2023-24, as per following details :

Schemes	Total Population	Sample size (10% of Sanctioned Projects)	Population component
Scheme I	900 (Approx.)	90	1. Open Field Cultivation, 2. Protected Cultivation, 3. PHM, 4. Primary Processing Units, & 5. Others
Scheme II	80 to 100 (Approx.)	8 to 10	1. Cold Storage establishment

NHB shall make payment of Rs. 18,34,924/- plus GST for the above assignment as per following details:-

Sl. No.	Activity	Total Cost
1	Professional & Quality Control Cost	₹ 6,50,000.00
2	Assessment Cost	
2.1	Assessment of Scheme- I (10% of sanctioned projects under scheme I)	₹ 7,60,136.00
2.2	Assessment of Scheme- II 10% of sanctioned projects under scheme II)	₹ 1,28,189.00
3	Technology, IT Infrastructure, & Reporting Cost	₹ 1,00,000.00
QCI Admin Cost @12%		₹ 1,96,599.00
Total Project Cost		₹ 18,34,924.00*
		+ Applicable Taxes

*This amount is exclusive of any taxes and levies.

Handwritten signature

- 3 -

The payment milestones for each of the above projects will be as under:-

Project-1		
Milestones	Stages	Amount to be disbursed
Milestone 1	On Submission of Inception Report	25%
Milestone 2	After completion of 50% of On-Field Assessment	25%
Milestone 3	After completion of 100% of On-Field Assessment	25%
Milestone 4	On Final Submission of Assessment Report	25%
Project-2		
Milestones	Stages	Amount to be disbursed
Milestone 1	After completion of 50% of On-Field Assessment for phase I and Phase II	50%
Milestone 2	On Final Submission of Assessment Report for phase I and Phase II	50%

The other terms and conditions of the contract, scope and objective of third party evaluation, development of framework, training and deployment of Assessors, data quality check, data analysis, reports, deliverables linked to the project timeline etc. will be strictly as per the project proposals submitted by QCI to NHB as attached to this letter.

Further, the QCI will use tech enabled GIS based services to verify the works and provide good quality photographs (Google Map image with location, images of the infrastructure with important component with time and date stamp and a brief mention how the facility has been used in the last three years). QCI

Submission of Report: QCI will submit a detailed report with all kinds of analytics for NHB to enable it to take appropriate decisions. The Enumerator of QCI will also point out any anomaly he/she enumerates in the field and take photographs with time, date and GPS stamp. The final list of selected sites will be as per sampling formulae and should not be changed after that. QCI will handover the App being used in enumeration of the projects to NHB and it will be a property of NHB. At least three hard copies of Draft report and Final Report shall be submitted by QCI.

Amendment of Agreement: No amendment or modification of the agreement authorizing this project shall be valid unless it is made in writing jointly by both parties or by their authorized representatives, especially stating the amendments reason to this agreement. The modification/changes shall be effective from the date they are made/executed unless otherwise agreed to.

Force Majeure: The parties shall ensure compliance with the terms of this agreement. However, no party shall be liable for any claim for any loss or damage whatsoever arising out of failure to carry out the terms of the agreement to the extent such a failure is due to force

hwh

-4-

majeure events such as fire, rebellion, mutiny, civil commotion, riots, strike, lockout, the force of nature, accident, the of God, or any other reason beyond the control of the concerned party.

Arbitration: The disputes, if arising, shall be settled by arbitration with the sole arbitrator (to be jointly appointed in 30 days) following the procedure prescribed in the Indian Arbitration and Conciliation Act, 1996 or any statutory modification or reenactment thereof and the Rules made thereunder and for the time being in force. Proceedings shall unless otherwise agreed by the parties, be held in Delhi, India. The governing law will be the laws of India. The language will be English.


Termination of Contract : Either party shall have the right to terminate this contract at any time by giving thirty days' notice in writing in advance indicating reasons for the same to the other party. The reasons, however, will need to be justified, and in case the termination leads to delay/pause/abortion of the project, the Authority reserves the right to not make any payments further to the date of project termination as indicated by either party.

Confidentiality:

Both the parties shall maintain confidentially or information and the interaction between them and shall not disclose any relevant confidential information to any third parties. Disclosure of any confidential information by the staff members or agencies hired by any party shall be deemed disclosure of such confidential information by such party, which shall be held liable for breach of this agreement.

You are requested to kindly convey your acceptance to the above said offer of NHB for conducting the third party evaluation for its schemes alongwith its terms and conditions and thereafter, you may start the evaluation work as per miles at the earliest.

Yours sincerely,



(C.P. Gandhi)

Deputy Director (Coord.)

Copy to :

1. Accounts Officer, NHB
2. PS to MD/DMD

28.2. Third-Party Re-Assessment of FCI owned Warehouses

Completion Certificate

FCI HQ-S-C012(18)/2/2022-S C

I/614819/2023

तार : 'फूडकोर्प' Gram : 'FOODCORP' फेक्स नं: एचएफसीआई एन डी Fax No.: HFCI ND 00911123413241 00911143527433	भारतीय खाद्य निगम  FOOD CORPORATION OF INDIA 16-20, सारखम्बा लाने, नई दिल्ली-110001, तृतीय: 011-43527697, 43527698 16-20, SARAKHAMBA LANE, NEW DELHI - 110001, PHONE: 011-43527697, 43527698	मुख्यालय नई दिल्ली Head Quarters New Delhi
No. FCI HQ-S-C012(18)/2/2022-S C Signature Date		Date:

Project Completion Certificate

This is to certify that the project titled 'Third Party Reassessment of FCI Owned Warehouses', undertaken by Quality Council of India for the Food Corporation of India as per work order no. FCI HQ-S-C012(18)/1/2022-SC dated 07.12.22, and with total amount of Rs.89,19,120 has been successfully completed in accordance with the agreed-upon terms and specifications within the timeline.

Key Output

- Reassessment of 489 upgraded depots and comparative statement to FCI with original grading and upgraded rating.
- Identification of best practices within the current system. Focus on replicating these practices and implementing necessary reforms.

Submissions by QCI:

- Submission of reports of all 489 warehouses re-assessed.
- A consolidated National Report summarizing the findings and recommendations.

This certificate is issued in recognition of the successful completion of the aforementioned project.

Signed by Ram Babu Meena
 (Ram Babu Meena)
 Asstt. Genl. Manager (S&C)
 Date: 05-10-2023 15:56:10
 Reason: Approved

Work Order

I/24498/2022

FCI HQ-S-C012(18)/1/2022-S C**Dated: 07.12.2022**

The Secretary General,
Quality Council of India,
Bahadur Shah Zafar-Marg, New Delhi

Sub: Third party re-assessment of FCI owned warehouses-reg.**Ref:**

1. MOU between QCI and FCI dated 24.03.2021 concerning transformation of FCI.
2. This Office letter of even no. 68756/2022/S&C-HQ dated 03.10.22 and 18.11.22
3. QCI Proposal for re-validation of 492 FCI owned depots dated 27.11.22.

Sir,

A Memorandum of Understanding (MOU) was signed on 24.03.2021 between FCI and QCI with the objective of taking up projects for transformation of FCI. Following clauses are part of the MOU:-

4.1.a.i - Review current standards and guidelines and benchmark them to global best practices and international standards and suggest relevant changes, whenever required, to be implemented immediately.

4.1.e.i - Third party audit of complete value chain, including stages of procurement and distribution for a period of 5 years or mutually agreed time period to monitor and standardize the processes based on mutually agreed audit plans conducted through professionally qualified experts engaged through a transparent process of price discovery.

In pursuance to the above MoU, work order was issued to QCI vide this office letter no E.1(1)/QCI/2021/Stg VIII, dated: 12.08.2021. QCI submitted its final report to FCI in the month of July 2022 and accordingly improvements were made in all the FCI owned depots. FCI Regional / Zonal offices have reported that 492 depots have been up-graded to 4 Star, 5 Star and Excellent Category.

It is directed by DFPD to get all the FCI owned depots re-validated from QCI, that have been up-graded to 4 Star, 5 Star and Excellent Category. Accordingly, QCI was requested vide this office letter of even no. dated 03.10.22 and 18.11.22 to submit proposal for the same. Subsequently, QCI submitted the proposal on 27.11.22.

The proposal dated 27.11.22 has been examined and the Competent Authority has accorded approval for undertaking Third party re-assessment of 492 warehouses (FCI owned) at the estimated cost of Rs 92,94,880/- (Ninety two lakhs ninety four thousand eight hundred and eighty only) excluding taxes, to be carried out by professionally qualified experts engaged through a transparent process of price discovery. Following shall be the Terms and Conditions:

Scope of Work:

The parameters as stated at Annexure-I & II of the QCI proposal dated

I/24498/2022

27.11.2022, which are attached herewith, shall be covered under the third party assessment. QCI will capture information of the up-graded depots in the same format as was done for the original assessment. The marking scheme shall also remain the same.

Exercise is to be undertaken for all the 492 FCI Owned up-graded warehouses across Pan-India. List enclosed.

Key Output:

- All 492 up-graded depots will be reassessed with respect to original grading and up-graded rating. The comparative statement be submitted to FCI.
- Best practices within the current system for replication with a focus on reforms required for improving the performances/ efficient utilization of warehousing space.
- Action plan for improving the performance to international best practices.

Payment:

The proposal dated 27.11.2022 has been worked out on the basis of 492 warehouses for which estimated cost worked out is Rs 92,94,880/- (Ninety two lakhs ninety four thousand eight hundred and eighty only). The proposal of QCI has fixed and variable cost. The fixed cost shall remain the same and the variable cost will vary based on number of man days (fixed as per capacity) which is based on actual number of depots inspected. It is clarified that the extra cost on account of change in technology during the assessment shall not be payable to QCI.

The actual payment shall be made as per criteria provided in the QCI proposal and the number of warehouses covered during the exercise. The Schedule of Payment shall be as under:

Sl.	Schedule / Milestones	Percentage (%) of Contract Value
1	Award of Work Order	10%
2	Submission and acceptance of final Report	90%

The QCI will raise all the claim bills in FCI Hqrs. The storage Division shall collect the details from Regions and process the same accordingly. Certificate of GM (Region) regarding number of man days utilized (not exceeding the ceiling) will be the basis of regulating the final payment. The Zonal Offices shall compile data on submission of draft report of Regions under their jurisdiction and submit the same to FCI, Hqrs. (the Storage Division, FCI, Hqrs. will seek and compile such information for the purpose of processing the claim).

It shall be made clear that no additional claim on whatsoever, ground for any other payment/re-imbursement of expenditure on other account would be entertained.

Timeline:

- The timeline for completing the said work is 2 Months which commences from the date of receipt of Work Order from this office.
- In case, QCI fails to submit the reports (complete in all respect)

I/24498/2022

within 60 days (including all the holidays) from the date of issue of work order from this office, Liquidated damages will be applicable for delay based on the number of days by which the submission of report is delayed (10% of sub-total, as mentioned under the head "7. Financials" i.e. Rs. 82,99,000/- for every 15 days and part thereof).

2. In case of delay in completion of study for the reasons beyond the control of the party, suitable extension of the time shall be considered at the sole discretion of FCI.

Submission of Report: At least three hard copies each of Draft and Final Report shall be submitted by QCI.

Amendment of Agreement: No amendment or modification of the agreement authorizing this project shall be valid unless it is made in writing jointly by both parties or by their authorized representatives, especially stating the amendment's reason to this agreement. The modification/changes shall be effective from the date they are made/executed unless otherwise agreed to.

Force Majeure:

The parties shall ensure compliance with the terms of this agreement. However, no party shall be liable for any claim for any loss or damage whatsoever arising out of failure to carry out the terms of the agreement to the extent such a failure is due to force majeure events such as fire, rebellion, mutiny, civil commotion, riots, strike, lockout, the force of nature, accident, the act of God, or any other reason beyond the control of the concerned party.

Arbitration:

The disputes, if arising, shall be settled by arbitration with the sole arbitrator (to be jointly appointed in 30 days) following the procedure prescribed in the Indian Arbitration and Conciliation Act, 1996 or any statutory modification or reenactment thereof and the Rules made thereunder and for the time being in force. Proceedings shall unless otherwise agreed by the parties, be held in Delhi, India. The governing law will be the laws of India. The language will be English.

Notice:

All notices permitted or required to be given under the provisions of this agreement shall be deemed to be sufficiently given if written and delivered personally or sent to the other party by telefax or certified or registered airmail or email and addressed to the registered office of the other party as follows or to such other party address as the party may give notice in writing.

Unless otherwise provided herein, all such notices shall be deemed to have been given as of the date they are personally delivered or transmitted by telefax or email or deposited in the mail.

Termination of agreement:

Either party shall have the right to terminate the agreement at any time by giving thirty days' notice in writing in advance indicating reasons for the same to the other party. The reasons, however, will need to be justified, and

I/24498/2022

in case the termination leads to delay/pause/abortion of the project, the Authority reserves the right to not make any payments further to the date of project termination as indicated by either party.

Confidentiality:

Both the parties shall maintain confidentiality of information and the interaction between them and shall not disclose any relevant confidential information to any third party. Disclosure of any confidential information by the staff members or agencies hired by any Party shall be deemed disclosure of such confidential information by such Party, which shall be held liable for breach of this Agreement.

Formal acceptance of the work order and its terms and conditions may be communicated to FCI immediately.

Yours Faithfully

Signed by Alok Kumar Uday

Bhanu Singh

Date: 06-12-2022 13:20:43

Reason: Approved

Dy. General Manager

Attachment: List of 492 depots.

Copy to:

1. Secretary (DFPD), MoCAF&PD Krishi Bhawan, New Delhi... for information.
2. PA to C&MD, FCI Hqrs., New Delhi... for information.
3. General Manager (PI Cell/ QCI/ Purchase) FCI Hqrs., New Delhi... for information.
4. ED (Zone), Zonal offices (North, East, West, South, NE)... for information.
5. General Manager (All FCI Regions).... for information.
6. Board Cell, FCI Hqrs., New Delhi... for information.

28.3. Third-Party Assessment of Procurement Centers in KMS 2021-22 & RMS 2022-23

Completion Certificate

FCI HQ-Proc021/5/2023-PROC

I/1390490/2024

Project Completion Certificate

This is to certify that the project titled **Third Party Assessment of Procurement Centers in KMS 2021-22 and RMS 2022-23**, undertaken by Quality Council of India for the Food Corporation of India as per work order no. **Proc. I/1(1)/2021/QCI** dated **10.12.2021**, has been successfully completed in accordance with the agreed-upon terms and specifications.

Key Output:

- Analysis report on the current infrastructural facilities available at the procurement center.
- Comprehensive assessment report on activities performed at procurement centers from observations and data analysis.
- Feedback from farmers and other stakeholders.
- Data of grain analyzed (defining the moisture contents, physical parameters) at which they were procured.

Submissions by QCI:

- Submission of reports for 23 states involved in the project.
- A consolidated National Report summarizing the findings and recommendations.
- Provision of a link to access the Procurement Dashboard.

This certificate is issued in recognition of the successful completion of the aforementioned project.

Signed by
Sanjay Pathy
Date: 31-07-2024 14:52:07
Asstt. Genl. Manager(Procurement)

No: FCI HQ-Proc021/5/2023-PROC(154270) Dated: 31-07-2024

Work Order



No. Proc.I/ 1(1)/ 2021/QCI
The Secretary General,
Quality Council of India,
Bhadur Shah Zafar-Marg, New Delhi

Dated: 10.12.2021

Sub: Third party assessment of Procurement Centers in KMS 2021-22 and RMS 2011-23-reg.

Ref: QCI proposal for Third party assessment Procurement Centers dated 17.11.2021.

Sir,

A Memorandum of Understanding (MOU) was signed on 25.03.2021 between FCI and QCI with the objective of taking up projects for transformation of FCI. Following clauses are part of the MOU:

4.1.a.i - Review current standards and guidelines and benchmark them to global best practices and international standards and suggest relevant changes, wherever required, to be implemented immediately.

4.1.e.i - Third party audit of complete value chain, including stages of procurement and distribution for a period of 5 years or mutually agreed time period to monitor and standardize the processes based on mutually agreed audit plans conducted through professionally qualified experts engaged through a transparent process of price discovery.

In Pursuance to the above, proposal was received from QCI vide e-mail dated 17.11.2021 for conducting a Third-Party Assessment of Procurement centers based on indicative parameters as per Annexure I to IV of the proposal. The proposal has been examined and the Competent Authority has accorded in-principle approval for proposal submitted by QCI for undertaking third party assessment of procurement centers to be carried out by professionally qualified experts, engaged through a transparent process of price discovery, over 8 months. Following shall be the Terms and Conditions:

Scope of Work:

The parameters as stated in the QCI proposal dated 17.11.2021, which are attached herewith, shall be covered under the third-party assessment.

Third party assessment is to be carried out in 434 purchase centers as per the state wise list attached as Annexure I, over 8 months covering both Kharif Marketing Season and Rabi Marketing Season.

Key Objectives:

- a) Assessment of infrastructural facilities at the procurement centre.
- b) Comprehensive assessment of activities performed in procurement centres vis-à-vis standard operating procedures.
- c) Detailed feedback from farmers and other stake holders.
- d) Random assessment of quality of grain procured.





Key Output:

- Analysis report on the current infrastructural facilities available at the procurement center.
- Comprehensive assessment report on activities performed at procurement centers from observations and data analysis.
- Feedback from farmers and other stakeholders.
- Data of grain analyzed (defining the moisture contents, physical parameters) at which they were procured.

Following outcomes anticipated from the exercise

- Identification of necessary areas for intervention for bridging gaps and curation of technology interventions in procurement operations
- Identification of good practices which can be replicated and ideation of prototype of a modern grain procurement centre
- Identification of current practices and gaps between policies and implementation
- Identification of concerns and pain points of stakeholders at the time of procurement.
- Assessment of the quality of grain being procured.

Costing and Payment:

The financial proposal submitted in the proposal in respect of 3 items are hereby approved as under:

1. A.1 QCI Professionals * : Rs. 2,30,40,000/-
(36 Professionals X 80,000/Month X 8)
2. Logistics and Travel Cost : Rs. 98,82,000/-
3. Administrative Cost @12% * : On actuals, based on total cost of project.

* Final payment shall be made based on utilization Certificate alongwith particulars of personnel engaged for the project.

For all other items of cost mentioned in the proposal, approval is hereby conveyed subject to the condition that QCI shall follow the procedure as mentioned in Annexure V of the proposal and ensure proper price discovery. The final cost payable for each of these items will be the discovered price with the upper ceiling of the unit prices mentioned in the Clause 6 (Financials) of the proposal, after due verification of relevant documents.

The proposal of QCI has elements of fixed and variable costs. The fixed cost shall remain the same and the variable cost will vary based on number of man days actually consumed. It is clarified that the extra cost on account of change in technology or any other factor during the assessment shall not be payable. Further, taxes on the above mentioned cost will be levied as applicable.

The actual payment shall be made as per criteria provided in the QCI proposal and the number of purchase centers covered during the exercise. The Schedule of Payment shall be as under:

per

48

QUALITY COUNCIL OF INDIA
 15, PLOUGH FIELD ROAD, NEW DELHI - 110 016
 TEL: 011-26109111 FAX: 011-26109112
 E-MAIL: qci@qci.org.in

Arbitration: The disputes, if arising, shall be settled by arbitration with the sole arbitrator (to be jointly appointed in 30 days) following the procedure prescribed in the Indian Arbitration and Conciliation Act, 1996 or any statutory modification or reenactment thereof and the Rules made thereunder and for the time being in force. Proceedings shall unless otherwise agreed by the parties, be held in Delhi, India. The governing law will be the laws of India. The language will be English.

Notice: All notices permitted or required to be given under the provisions of this agreement shall be deemed to be sufficiently given if written and delivered personally or sent to the other party by telefax or certified or registered airmail or email and addressed to the registered office of the other party as follows or to such other party address as the party may give notice in writing.

Unless otherwise provided herein, all such notices shall be deemed to have been given as of the date they are personally delivered or transmitted by telefax or email or deposited in the mail.

Termination of agreement: Either party shall have the right to terminate the agreement at any time by giving thirty days' notice in writing in advance indicating reasons for the same to the other party. The reasons, however, will need to be justified, and in case the termination leads to delay/pause/abortion of the project, the Authority reserves the right to not make any payments further to the date of project termination as indicated by either party.

Confidentiality

Both the parties shall maintain confidentiality of information and the interaction between them and shall not disclose any relevant confidential information to any third parties. Disclosure of any confidential information by the staff members or agencies hired by any Party shall be deemed disclosure of such confidential information by such Party, which shall be held liable for breach of this Agreement.

Formal acceptance of the work order and its terms and conditions may be communicated to FCI immediately.

Yours Faithfully,

(Signature)
 10.12.2021

(Rajeev Mishra)

Dy. General Manager (Proc.)

28.4. Third-Party Assessment of FCI Warehouses

Completion Certificate

FCI HQ-S-C012(18)/2/2022-S C

I/631663/2023

तार : 'फूडकोर्प'
 Gram : 'FOODCORP'
 फेस नं: एचएफसीआई एन डी
 Fax No.: HFCI ND
 00911123413241
 00911143527433

भारतीय खाद्य निगम
 FOOD CORPORATION OF INDIA
 मुख्यालय नई दिल्ली
 Head Quarters New Delhi
 16-20, बाराकम्बा लेन, नई दिल्ली - 110001, टेलीफोन: 011- 43527697, 43527698
 16-20, BARAKHAMBHA LANE, NEW DELHI - 110001, PHONE: 011-43527697, 43527698

No. FCI HQ-S-C012(18)/2/2022-S C

Date:

Signature Date

Project Completion Certificate

This is to certify that the project titled 'Third Party Assessment of FCI Warehouses', undertaken by Quality Council of India for the Food Corporation of India as per work order no. **E.1(1)/QCI/2021/Stg VIII** dated **12.08.21**, and with a total amount of Rs.2,29,77,360 has been successfully completed in accordance with the agreed-upon terms and specifications within the timeline.

Key Output

- Report cards for each warehouse with specific grades based on predefined parameters.
- Finalization of draft report in consultation with the concerned GM(Region).
- Identify best practices within the current system for potential replication.
- Focus on reforms needed to improve warehouse performance and space utilization.
- Develop a plan for aligning with international best practices in warehousing.

Submissions by QCI:

- Submission of individual reports for all 2,147 assessed warehouses.
- Submission of reports covering all 26 Regions in the project.
- A consolidated National Report providing a summary of findings and recommendations.
- Ownership-specific reports categorized by FCI, CWC, SWC, PEG Owned, Private Owned, and PWS Owned warehouses.
- Provision of a link to access the Warehouse Dashboard.

This certificate is issued in recognition of the successful completion of the aforementioned project.

Signed by Ram Babu Meena
 (Ram Babu Meena)
 Asstt. Genl. Manager (S&C)
 Date: 11-10-2023 09:55:43
 Reason: Approved

Work Order

नाम : 'फूडकोर्प'
 Group : 'FOODCORP'
 फैक्ट्री नं : एमएफपीआई एनपी
 Fax No : HFCEI ND
 00911123413241
 00911123413103

भारतीय खाद्य निगम
 FOOD CORPORATION OF INDIA
 आइ-एस-ओ 9001:2000 प्रमाणित
 10-20, बाराकम्बा लाने, नई दिल्ली - 110001, टीनप - 011-23413271, 23414872, 23414880
 10-20, BARAKAMBA LANE, NEW DELHI-110001. PHONE : 011-23413271, 23414872, 4880

मुख्यालय
 नई दिल्ली
 Head Quarters
 New Delhi

No. E.1(1)/QCI/2021/Stg VIII

Dated: 12.08.2021

The Secretary General,
 Quality Council of India,
 Bhadur Shah Zafar-Marg, New Delhi

Sub: Third party assessment of FCI warehouses-reg.

Ref: QCI proposal for Third party assessment of FCI (Own & Hired) warehouses dtd 23.07.2021.

Sir,

A Memorandum of Understanding (MOU) was signed on 25.03.2021 between FCI and QCI with the objective of taking up projects for transformation of FCI. Following clauses are part of the MOU:-

- 4.1.a.i - Review current standards and guidelines and benchmark them to global best practices and international standards and suggest relevant changes, wherever required, to be implemented immediately.
- 4.1.e.i - Third party audit of complete value chain, including stages of procurement and distribution for a period of 5 years or mutually agreed time period to monitor and standardize the processes based on mutually agreed audit plans conducted through professionally qualified experts engaged through a transparent process of price discovery.

In Pursuance to the above, proposal was received from QCI vide e-mail dated 23.07.2021 for conducting a Third Party Assessment of FCI warehouses based on framework parameters. The proposal has been examined and the competent authority has accorded in-principle approval for proposal submitted by QCI for undertaking Third party assessment of warehouses (FCI owned and hired) at the estimated cost of Rs 2,39,89,840/- (Two Crore Thirty-Nine Lakhs Eighty-Nine Thousand Eight Hundred Forty only) to be carried out by professionally qualified experts engaged through a transparent process of price discovery. Following shall be the Terms and Conditions:

Scope of Work:

The parameters as stated at Annexure-I & II of the QCI proposal dated 23.07.2021, which are attached herewith, shall be covered under the third party assessment.

Exercise is to be undertaken for all the warehouses with FCI (both owned & hired) across Pan-India. Since the number of depots is a dynamic figure and varies from month to month due to hiring and de-hiring of godowns, QCI may undertake the exercise for actual number of godowns as available during the audit period. As on 30.06.2021, total number of godowns was 2323.

Key Output:

- A report card for each warehouse against current SoPs with specific grading prepared based on pre-defined parameters (Annexure I & II). The draft report will be finalized in consultation with concerned GM(Region).
- Best practices within the current system for replication with a focus on reforms required for improving the performances/ efficient utilization of warehousing space.
- Action plan for improving the performance to international best practices.



Page 1/3

नाम : "फूडकोर्प"
 Gram : "FOODCORP"
 पतेका नं. : एमएफसीआई, एनडी
 Fax No. : HFCEI ND
 00911123413241
 00911123413103

भारतीय खाद्य निगम

 FOOD CORPORATION OF INDIA
 आइ-एफ-सी- 0001:2000 प्रमाणित
 16-20, बाराहम्बा लाने, नई दिल्ली - 110011, फ़ोन : 011-23413871, 23413872, 23413873
 16-20, BARAHAMBA LANE, NEW DELHI-110011. PHONE : 011-23413871, 23413872-4899

मुख्यालय
 Hq. Headquarters
 Head Quarters
 New Delhi

Payment:

The proposal dated 23.07.2021 has been worked out on the basis of 2272 warehouses for which estimated cost worked out is Rs 2,39,89,840/- (Two Crore Thirty-Nine Lakhs Eighty-Nine Thousand Eight Hundred Forty only). The proposal of QCI has elements of fixed and variable cost. The fixed cost shall remain same and the variable cost will vary based on number of man days (fixed as per capacity) which is based on actual number of depots inspected. It is clarified that the extra cost on account of change in technology during the assessment shall not be payable to QCI.

The actual payment shall be made as per criteria provided in the QCI proposal and the number of warehouses covered during the exercise. The Schedule of Payment shall be as under:

Sl.	Schedule / Milestones	Percentage (%) of Contract Value
1	Award of Work Order	10%
2	End of Assessment and submission of Draft report	60%
3	Submission and acceptance of final Report	30%

The QCI will raise all the claim bills in FCI Hqrs. The Storage Division shall collect the details from Regions and process the same accordingly. Certificate of GM (Region) regarding number of mandays utilized (not exceeding the ceiling) will be the basis of regulating of the final payment. The Zonal Offices shall compile data of submission of draft reports of Regions under their jurisdiction and submit the same to FCI Hqrs (The Storage Division FCI Hqrs will seek and compile such Information for purpose of processing the claim).

It shall be made clear that no additional claim on whatsoever ground for any other payment/reimbursement of expenditure on any other account would be entertained.

Time line:

1. The timeline for completing the said work is 8 (Eight) weeks which commences from the date of receipt of Work Order from this office.
2. In case of delay in completion of study for the reasons beyond the control of the party, suitable extension of the time shall be considered at the sole discretion of FCI.

Submission of Report: At least three hard copies of Draft report and Final Report shall be submitted by QCI.

Amendment of Agreement: No amendment or modification of the agreement authorizing this project shall be valid unless it is made in writing jointly by both parties or by their authorized representatives, especially stating the amendment's reason to this agreement. The modification/changes shall be effective from the date they are made/executed unless otherwise agreed to.

Force Majeure: The parties shall ensure compliance with the terms of this agreement. However, no party shall be liable for any claim for any loss or damage whatsoever arising out of failure to carry out the terms of the agreement to the extent such a failure is due to force majeure events



Page 2/3

नाम : 'सुसुकोर'
 Gram : 'FOODCORP'
 पोस्ट नं : एनएचएनएनएनएनएन
 Fax No. : HFCI ND
 00011123413241
 00011123413103

भारतीय खाद्य निगम
 भारत
 FOOD CORPORATION OF INDIA
 3RD FLOOR, 3RD FLOOR, 3RD FLOOR
 10-20, BARAKHAMBA LAKE, NEW DELHI-110001, PHONE : 011-25415671, 25415672-4000

भारतीय खाद्य निगम
 भारत
 FOOD CORPORATION OF INDIA
 3RD FLOOR, 3RD FLOOR, 3RD FLOOR
 10-20, BARAKHAMBA LAKE, NEW DELHI-110001, PHONE : 011-25415671, 25415672-4000

such as fire, rebellion, mutiny, civil commotion, riots, strike, lockout, the force of nature, accident, the act of God, or any other reason beyond the control of the concerned party.

Arbitration: The disputes, if arising, shall be settled by arbitration with the sole arbitrator (to be jointly appointed in 30 days) following the procedure prescribed in the Indian Arbitration and Conciliation Act, 1996 or any statutory modification or reenactment thereof and the Rules made thereunder and for the time being in force. Proceedings shall unless otherwise agreed by the parties, be held in Delhi, India. The governing law will be the laws of India. The language will be English.

Notice: All notices permitted or required to be given under the provisions of this agreement shall be deemed to be sufficiently given if written and delivered personally or sent to the other party by telefax or certified or registered airmail or email and addressed to the registered office of the other party as follows or to such other party address as the party may give notice in writing.

Unless otherwise provided herein, all such notices shall be deemed to have been given as of the date they are personally delivered or transmitted by telefax or email or deposited in the mail.

Termination of agreement: Either party shall have the right to terminate the agreement at any time by giving thirty days' notice in writing in advance indicating reasons for the same to the other party. The reasons, however, will need to be justified, and in case the termination leads to delay/pause/abortion of the project, the Authority reserves the right to not make any payments further to the date of project termination as indicated by either party.

Confidentiality

Both the parties shall maintain confidentiality of information and the interaction between them and shall not disclose any relevant confidential information to any third parties. Disclosure of any confidential information by the staff members or agencies hired by any Party shall be deemed disclosure of such confidential information by such Party, which shall be held liable for breach of this Agreement.

Formal acceptance of the work order and its terms and conditions may be communicated to FCI immediately.

This issues with the approval of CMD.

Yours Faithfully


 (Vinod Kumar)

Dy. General Manager (S&C)

Copy to:

1. Secretary(DFPD), MoCAF&PD Krishi Bhawan, New Delhi.....for information.
2. PA to CMD, FCI Hqrs. New Delhi.....for information.
3. General Manager (PI-Cell)/General Manager(QCI/Purchase), FCI Hqrs. New Delhi.....for information.
4. Board Cell, FCI Hqrs. New Delhi.....for information.


 Dy. General Manager (S&C)

Page 3/3

28.5. Audit Assessment and Issuance of Warehouse rating for CWC warehouses on warehouse management practices, safety standards and infrastructure including the audit from point of improvement in efficiency and new initiatives.

Completion Certificate



केन्द्रीय भण्डारण निगम
(भारत सरकार का उपक्रम)
CENTRAL WAREHOUSING CORPORATION
(A Govt. of India Undertaking)
जन-जन के लिए भण्डारण/Warehousing for Everyone



क्रमांक: CWC-CO-QS0QS/6/2023-24/ **दिनांक: 23.07.2024**

TO WHOM IT MAY CONCERN

This is to certify that work cited below was awarded to M/s Quality Council of India, 2nd Floor, Institution of Engineers Building, Bahadur Shah Zafar Marg, New Delhi-11002. They have completed the work as per details given below: -

यह प्रमाणित किया जाता है कि नीचे उल्लिखित कार्य मेसर्स क्वालिटी काउंसिल ऑफ इंडिया, द्वितीय तल, इंस्टीट्यूशन ऑफ इंजीनियर्स बिल्डिंग, बहादुर शाह जफर मार्ग, नई दिल्ली-11002 को सौंपा गया था। उन्होंने नीचे दिए गए विवरण के अनुसार कार्य पूरा कर लिया है: - :-

1.	Name of work कार्य का नाम	Audit, assessment and issuance of Warehouse ratings for CWC Warehouses on warehouse management practice, safety standards and infrastructure including the audit from point of improvement in efficiency and new initiatives. गोदाम प्रबंधन प्रवृत्ति, सुरक्षा मानकों और बुनियादी ढांचे पर सीडब्ल्यूसी गोदामों के लिए गोदाम रेटिंग का लेखा-परीक्षण, मूल्यांकन और जारी करना, साथ ही दक्षता में सुधार और नई पहलों के दृष्टिकोण से भी लेखा-परीक्षण करना।
2.	Letter of Acceptance No. स्वीकृति पत्र सं.	CWC-CO-QS0QS/6/2022/2022-23 Dt. 27.02.2023
3.	Total contract period कुल अनुबंध अवधि	03 Years 03 वर्ष
4.	Scope of Service सेवा का दायरा	a) To develop in consultation with CWC the framework consisting the audit parameters for evaluation and award of star rating based on CWC operations in warehouses, CFS, ICDs and rail linked terminals. b) To conduct audit, assess and evaluate CWC warehouses for release of Warehouse ratings on warehouse management practice, safety standards and infrastructure based on mutually accepted parameters including the audit from the point of improvement in efficiency and new initiatives. c) To submit a report card evident with photographic views for each warehouse with specific grading (marking), area of improvement required, good practices followed and award the star ratings.




केन्द्रीय भण्डारण निगम
 (भारत सरकार का उपक्रम)
CENTRAL WAREHOUSING CORPORATION
 (A Govt. of India Undertaking)
जन-जन के लिए भण्डारण/Warehousing for Everyone



		क) सीडब्ल्यूसी के परामर्श से गोदामों, सीएफएस, आईसीडी और रेल लिंकड टर्मिनलों में सीडब्ल्यूसी संचालन के आधार पर मूल्यांकन और स्टार रेटिंग प्रदान करने के लिए लेखापरीक्षा मापदंडों से युक्त रूपरेखा विकसित करना। ख) दक्षता में सुधार और नई पहलों के दृष्टिकोण से लेखापरीक्षा सहित पारस्परिक रूप से स्वीकृत मापदंडों के आधार पर गोदाम प्रबंधन अभ्यास, सुरक्षा मानकों और बुनियादी ढांचे पर वेयरहाउस रेटिंग जारी करने के लिए सीडब्ल्यूसी गोदामों का लेखापरीक्षा, आकलन और मूल्यांकन करना। ग) प्रत्येक गोदाम के लिए विशिष्ट ग्रेडिंग (मार्किंग), आवश्यक सुधार के क्षेत्र, अपनाई गई अच्छी कार्यप्रणाली के साथ फोटोग्राफिक दृश्यों के साथ एक रिपोर्ट कार्ड प्रस्तुत करना और स्टार रेटिंग प्रदान करना।
5.	Actual Work done Amount under 1 st Iteration प्रथम पुनरावृत्ति के अंतर्गत वास्तविक कार्य की मात्रा	Rs. 80,29,994.00 (Rupees Eighty Lakh Twenty-Nine Thousand Nine Hundred Ninety-Four Only) रु. 80,29,994.00 (रुपये अस्सी लाख उनतीस हजार नौ सौ चौरानव्वे मात्र)
6.	Status of completion of Work कार्य पूर्ण होने की स्थिति	Audit and rating of 376 Nos. of warehouses completed. 376 गोदामों का ऑडिट और रेटिंग पूरा हो गया।

The certificate is issued at the request of M/s Quality Council of India for tendering purposes only.
यह प्रमाण-पत्र केवल निविदा प्रयोजन हेतु मेसर्स क्वालिटी काउंसिल ऑफ इंडिया के अनुरोध पर जारी किया गया है।



Digitally signed by
Roopendra Kumar Sharma
Date: 2024.07.23 10:57:19
+05'30'

(Roopendra Kumar Sharma)
Chief Engineer
Central Warehousing Corporation
मुख्य अभियंता
केंद्रीय भंडारण निगम

28.6. Mid-Term Evaluation of Deendayal Antyodaya Yojana- National Urban Livelihood Mission (NULM).

Completion Certificate

K-12011(11)/29/2017-UPA III SECTION (E-3146172)

Government of India
Ministry of Housing & Urban Affairs

Nirman Bhawan, New Delhi
Dated the 23rd June, 2022

PROJECT COMPLETION CERTIFICATE

Project Name: "Mid-term evaluation of Deendayal Antyodaya Yojana- National Urban Livelihoods Mission"

This is to certify that M/s Quality Council of India(QCI) has satisfactorily completed the assessment, verification tasks and documentation work in accordance to Contract No. IN-DL50809353038608P related to "**Mid-Term Evaluation of Deendayal Antyodaya Yojana-National Urban Livelihoods Mission**".

We appreciate the efforts put in by M/s QCI for successfully completing the project.



(Balachandran B.S.)
Under Secretary to the Government of India
Ministry of Housing and Urban Affairs
Nirman Bhawan, New Delhi-110011

काव्यत रे. एल. BALACHANDRAN B. S.
अवर सचिव/Under Secretary
आवासन और कस्बों खाते मंत्रालय
Ministry of Housing and Urban Affairs
एनए भवन, नई दिल्ली
Nirman Bhawan, New Delhi-110011

28.7. PAN India Trans Fat Survey

Completion Certificate

राकेश कुमार
निदेशक
Rakesh Kumar
Director




भारतीय खाद्य संस्था एवं मानक प्राधिकरण
स्वास्थ्य एवं परिवार कल्याण मंत्रालय
भारत सरकार
FOOD SAFETY AND STANDARDS AUTHORITY OF INDIA
Ministry of Health & Family Welfare
Government of India

TO WHOMSOEVER IT MAY CONCERN

It is to certify that the Quality Council of India (QCI) had conducted the PAN India survey to identify the presence of industrially produced trans-fatty acid content in selected six food categories, on the basis of the SOP, methodology, analysis and parameters designed by Food Safety and Standards Authority of India (FSSAI).

To conduct the Survey, QCI assessors visited 419 cities/districts across 34 States/UTs to collect the samples (6,245 samples of packaged products) and analysed the samples in 8 selected NABL accredited testing laboratories.

As per the agreement, the aforementioned project was successfully completed and QCI delivered all the deliverables between August, 2021 to November, 2021 and the final payment was made to QCI on 25th November, 2021 by FSSAI.



राकेश कुमार / RAKESH KUMAR
निदेशक / Director
भारतीय खाद्य संस्था एवं मानक प्राधिकरण
Food Safety and Standards Authority of India
(स्वास्थ्य एवं परिवार कल्याण मंत्रालय)
(Ministry of Health & Family Welfare)
भारत सरकार / Government of India
एफ.सी.ए. भवन, कोटला रोड, नई दिल्ली-110002
FDA Bhawan, Kotla Road, New Delhi-110002

Work Order

F.No.11020/7/2021/RARD/FSSAI
Food Safety and Standards Authority of India
(A Statutory Authority established under the Food Safety & Standards Act, 2006)
(Quality Assurance Division)
FDA Bhawan, Kotla Road, New Delhi - 110002

Dated: 31.03.2021

To,
The CEO,
National Accreditation Board for Certification Bodies (NABCB)
Quality Council of India
2nd Floor, Institution of Engineers Building
2, Bahadur Shah Zafar Marg,
New Delhi-110002, India

Dear Sir,

Greetings from FSSAI.

FSSAI has proposed to conduct PAN India Trans fat Survey in order to understand the current scenario of usage of trans-fats in processed foods and in industrial trans-Fats in fats/ oils so as to eliminate the trans-fat in a phased manner. FSSAI, considered the project proposal submitted by Quality Council of India (QCI) for conducting the aforesaid survey.

2. In view of above, I am directed to convey the approval of Competent Authority of FSSAI to Quality Council of India for conducting the Trans fat Survey in a time bound manner as per your project proposal.

3. The salient features of the survey are as follows:

- i. QCI will collect a total of 6600 samples, for the 6 product categories mentioned in the proposal from the 425 cities/districts as given in the list shared in the proposal and out of which 42 samples per city are to be collected from the 50 cities (7 samples per product category) and 12 samples per city from 375 cities/districts (2 samples per product category).
- ii. QCI shall carry out the analysis in NABL accredited/FSSAI recognized labs only. Further to test the parameters as indicated in the proposal for two trans-Fats-Elaidioate (9t-C18:1; 9t-octadecenoate) and Linoelaidioate (9t,12t-C18:2; 9t,12t-octadecadienoate) based on AOAC 996.06 or AOAC 996.01 or any other equivalent validated method using GC-FID covered under the scope of



accreditation. For Acrylamide, the analysis shall be carried out based on validated method using LCMS-MS covered under the scope of accreditation.

- iii. FSSAI would facilitate to support the requirements as stated under point 6 of your proposal. Other than this, the sample collection, transportation, laboratory testing as well as generating final report will be done QCI.
- iv. FSSAI will pay @ Rs. 7212 per sample + GST to QCI. This includes sample pick up, transportation and analytical charges.
- v. The total project cost would be as follows:
 - a. Cost of Analysis (including sample pick up and transportation to your testing lab): Rs. 7212/- + GST per sample
 - b. Approximate Number of Samples = 6600
 - c. Total Cost (excluding GST) for 6600 samples: Rs. 4,76,00,000, GST will be paid at 18%

vi. The payment schedule will be as follows:

S.No	Phases	Payment Schedule	% of total cost	Amount in INR(excluding GST)
1.	I	Advance payment on award of Work order	30	1,42,80,000
2.	II	Completion of on ground food sample collection	30	1,42,80,000
3.	III	Completion of analysis by the Lab	20	95, 20,000
4.	IV	Completion and submission of final Trans Fat Survey report	20	95, 20,000
5.		Total	100	4,76,00,000

4. QCI shall conduct the Survey including laboratory analysis of samples followed by compilation of result and submission of report in a time-bound manner.

(Yours Sincerely)


 31/3/2021
 (Shailender Kumar)
 Assistant Director (QA)

28.8. Assessment of various ODF, ODF+, & ODF++ status

Completion Certificate

Page 14

आर. एस. जयाल

R. S. JAYAL

उप सचिव

Deputy Secretary (SBM-II)

Tel: 011-23061187

भारत सरकार
आवासन और शहरी कार्य मंत्रालय
निर्माण भवनGOVERNMENT OF INDIA
MINISTRY OF HOUSING AND URBAN AFFAIRS
NIRMAN BHAWAN

नई दिल्ली-110011, तारीख 20

New Delhi-110011, dated the 20
Dated : 02 September 2020TO WHOM IT MAY CONCERN

This is certified that under a contract agreement signed between **this Ministry** and **M/s Quality Council of India (QCI), New Delhi**, assessment was done by M/s QCI of various Urban Local Bodies (ULBs) for their **Open Defecation Free (ODF)** status. ODF certification was done after assessment of the ULBs from **19.07.2016, till date**. Further, ULBs were also assessed and certified on **ODF+ and ODF++ protocol**, as per the extended scope of the Contract Agreement vide this Ministry's work order No 15/3/2018-SBM-II dated 01.07.2019.

2. These agreements for ODF, ODF+ and ODF++ assessment and certification of ULBs are valid till **30.09.2020**.

3. Further, it is certified that M/s Quality Council of India has delivered their services satisfactorily for these projects.



(R. S. JAYAL)

Deputy Secretary to Govt. of India
Swachh Bharat Mission (Urban) Divisionराजेंद्र सिंह जयाल/R.S. JAYAL
उप सचिव/Deputy Secretary
आवासन और शहरी कार्य मंत्रालय
Ministry of Housing And Urban Affairs
निर्माण भवन, नई दिल्ली
Nirman Bhawan, New Delhi


F.C. Srivastava ★
Deputy Director
(Accounts & Administration)
