

Third Party Evaluation of the Programme - National Programme for Dairy Development (NPDD)

Document Type:	Proposal
Version:	1.0
Date (DD/MM/YYYY):	01/05/2025
Submitted to:	Department of Animal Husbandry and Dairying (DAHD)
QCI Node:	Project Planning & Implementation Division (PPID)



Quality Council of India (QCI) is an autonomous organisation established in 1997, through joint initiative of the Government of India and the Indian industry, pursuant to resolution of the Indian Cabinet in 1996. It is registered as a Society under the Societies Registration Act, 1860 with the mandate to establish and operate the national accreditation system in India and promote quality in all aspects of life, industry, environment, and governance. It is a self-sustaining independent organisation with complete financial, administrative, and functional autonomy. The Department for Promotion of Industry and Internal Trade (DPIIT), Ministry of Commerce and Industry, Government of India is the nodal point in the government for QCI and all matters concerning quality. The Governing Council of the Society is the apex governing organ of QCI and consists of equal representation of government, industry, and other stakeholders. Chairperson, QCI is nominated by the Prime Minister of India.

Regd. Office: 2nd Floor, Institution of Engineers Building, 2, Bahadur Shah Zafar Marg, New Delhi-02
Ph.: +91-11-2323 8736, +91 98990 15306, +91 70096 22718

TABLE OF CONTENTS

Introduction	3
1. Background.....	3
2. Context	3
Quality Council of India (QCI).....	4
3. Introduction to QCI.....	4
4. Mandate & Structure	4
5. Key projects	5
National Programme for Dairy Development (NPDD) Scheme.....	6
6. About National Programme for Dairy Development (NPDD) Scheme	6
Genesis of the Study.....	6
7. Understanding of the Evaluation Context	6
Scope and Objectives	7
8. Objective of the Study.....	7
9. Scope of Work.....	7
Methodological Framework	8
10. Research design and approach	8
11. Proposed Activities/Actions and Expected Insights	9
12. Identification of Stakeholders.....	10
Sampling.....	10
13. Sampling Strategy.....	10
14. Proposed Sampled States & Districts	10
Operational Framework & Execution Plan.....	11
15. Preliminary Analysis and Development of Evaluation Framework.....	11
16. Preparation and Optimization of IT Platform.....	11
17. Pilot Study	11
18. Training and Deployment of Assessors	11
19. Primary Survey, Stakeholder Interviews and Focus Group Discussions (FGDs).....	11
20. Data Quality Assurance.....	12
21. Data Analysis and Interpretation	12
22. Final Reporting	12
Brief Work Plan & Key Deliverables	13
Financial	14
23. Project Financials	14
24. Payment Structure:	14

Annexures.....	15
25. QCI's Previous Projects with DAHD	15
25.1. Third-Party Evaluation of Animal Infrastructure Development Fund (AHIDF) Scheme 15	
25.2. Screening of Applications received through online National Award Portal for National Gopal Ratna Award 2024, 2023, & 2022 (<i>on Nomination Basis</i>)	20
26. QCI's Previous Projects on Nomination Basis with different Ministries	26
26.1. National Horticulture Board (NHB), Ministry of Agriculture & Farmers Welfare, GoI 26	
26.2. Third-Party Re-Assessment of FCI owned Warehouses	31
26.3. Third-Party Assessment of Procurement Centers in KMS 2021-22 & RMS 2022-23 36	
26.4. Third-Party Assessment of FCI Warehouses	41
26.5. Audit Assessment and Issuance of Warehouse rating for CWC warehouses on warehouse management practices, safety standards and infrastructure including the audit from point of improvement in efficiency and new initiatives.	45
26.6. Mid-Term Evaluation of Deendayal Antyodaya Yojana- National Urban Livelihood Mission (NULM).	47
26.7. PAN India Trans Fat Survey	48
26.8. Assessment of various ODF, ODF+, & ODF++ status.....	51

List of Figures

Figure 1: QCI Organisational Structure	4
Figure 2: Triangulation Approach	8

List of Tables

Table 1: Proposed Activities/Action and Expected Insights from Third-Party NPDD Scheme Evaluation	9
Table 2: Proposed States & Districts for Sampling	10
Table 3: Project Financials	Error! Bookmark not defined.
Table 4: Payment Structure.....	14

Introduction

1. Background

- 1.1. Dairy is the largest agricultural commodity in India, ranking first in milk production, contributing 5% to the national economy, employing over 8 crore farmers directly and contributing 25 percent to the world's total milk output. India's milk production has grown remarkably over the past decade, with a Compound Annual Growth Rate (CAGR) of 6 percent where production increased from 187.30 million tons in 2018-19 to 230.58 million tons in 2022-23¹. Approximately 50-60% of the total value of dairy output, flows back to the farmers which has a substantial influence on the income of dairy farmers.
- 1.2. Currently, a comparatively small portion of the overall milk production (about 30%) is managed by the organized sector which includes cooperatives and private dairy organizations.
- 1.3. However, dairy sector in India faces several challenges including inadequacy of infrastructure for production of quality milk, insufficient cold chain infrastructure for storage and transportation, shortage of good quality feed and fodder for cattle, disease outbreaks, lack of training and awareness, etc.
- 1.4. To overcome these challenges, National Programme for Dairy Development (NPDD) is being implemented since Feb-2014 across the country with an objective of creating/strengthening of infrastructure for Production of quality milk, Procurement, Processing and Marketing of Milk & Milk Products through State Implementing Agency (SIA) i.e. State Cooperative Dairy Federation. NPDD scheme has been restructured/realigned in July 2021 for implementation from 2021-22 to 2025-26 with the aim to enhance quality of milk and milk products and increase share of organized procurement, processing, value addition and marketing.

2. Context

- 2.1. In June 2024, the Department of Animal Husbandry and Dairying (DAHD), under the Ministry of Fisheries, Animal Husbandry and Dairying, Government of India, issued a Request for Proposal (RfP) for conducting the Third-Party Evaluation of the National Programme for Dairy Development (NPDD). However, as the department did not receive any suitable bids in response to the RfP, the tender was subsequently cancelled.
- 2.2. Considering its long-standing association with DAHD — including successful engagements for the National Gopal Ratna Awards (2022, 2023, 2024) and the Third-Party Evaluation of the Animal Husbandry Infrastructure Development Fund (AHIDF) Scheme in 2023 — the Quality Council of India (QCI) proactively approached DAHD to express its interest and showcase its capabilities for undertaking the evaluation of the NPDD programme.
- 2.3. On 30th January 2025, a delegation from QCI met with the Secretary, Animal Husbandry and Dairying, to formally present QCI's expertise and readiness to execute the evaluation of the NPDD scheme effectively and within stipulated timelines.
- 2.4. Subsequent to this meeting, QCI and DAHD held discussions regarding the scope of the evaluation. DAHD requested QCI to submit a formal proposal outlining its strategic approach for the Third-Party Evaluation of the National Programme for Dairy Development (NPDD).

¹ <https://static.pib.gov.in/WriteReadData/specificdocs/documents/2024/may/doc2024531339201.pdf>

Quality Council of India (QCI)

3. Introduction to QCI

- 3.1. The Quality Council of India (QCI) has been set up as a non-profit autonomous society registered under the Societies Registration Act XXI of 1860 to establish an accreditation structure in the country and to spread quality movement in India by undertaking a National Quality Campaign.
- 3.2. QCI was established as the National body for Accreditation on recommendations of the Expert Mission of the EU after consultations between the Inter-Ministerial Task Force, Committee of Secretaries, and Group of Ministers and finally a Cabinet decision in 1996.
- 3.3. The Council was made an autonomous non-profit organisation through seed funding initially by the Government of India and the Indian Industry represented by the three premier industry associations: Associated Chambers of Commerce and Industry of India (ASSOCHAM), Confederation of Indian Industry (CII) and Federation of Indian Chambers of Commerce and Industry (FICCI).
- 3.4. The Department for Promotion of Industry and Internal Trade (DPIIT), Ministry of Commerce and Industry is the nodal point for all matters connected with Quality and QCI. The Council was established to create a mechanism for third-party assessment of products, services, and processes.

4. Mandate & Structure

- 4.1. Quality Council of India (QCI) has been set up as a non-profit autonomous society to establish and operate the national accreditation system in the country and to spread the quality movement in India by undertaking a national quality campaign.
- 4.2. It was formed by a joint initiative of the Government of India and the Indian Industry associations like the Associated Chambers of Commerce and Industry of India (ASSOCHAM), Confederation of Indian Industry (CII) and Federation of Indian Chambers of Commerce and Industry (FICCI).
- 4.3. QCI has established Constituent Boards, Divisions, and Cells catering to various aspects of quality. Its Boards are full members of international systems of accreditation and have multilateral mutual recognition arrangements (MRAs/MLAs) that allow for international equivalence and recognition of conformity assessment outcomes.

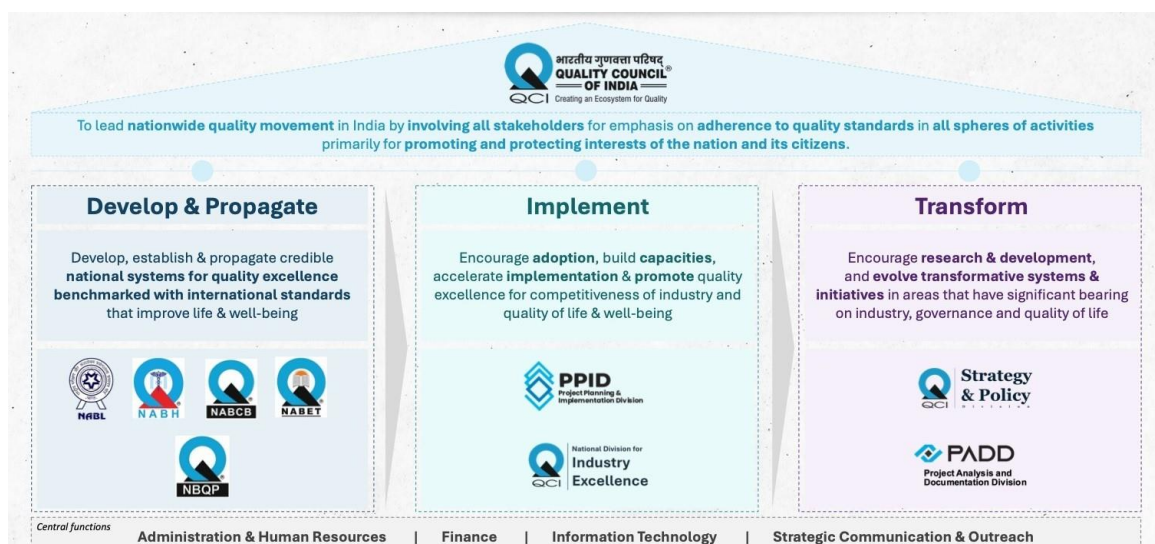


Figure 1: QCI Organisational Structure

4.4. Constituent Boards

- 4.4.1. **National Accreditation Board for Testing & Calibration Laboratories (NABL):** NABL accredits testing, calibration, and medical labs, as well as proficiency testing providers and reference material producers, based on international standards. NABL is a member of ILAC and APAC.
- 4.4.2. **National Accreditation Board for Certification Bodies (NABCB):** NABCB accredits Certification, Inspection, and Validation/Verification Bodies based on international standards and is a full member of IAF, ILAC, and APAC.
- 4.4.3. **National Accreditation Board for Hospitals and Healthcare Providers (NABH):** NABH accredits hospitals and healthcare organisations, with internationally recognized accreditations.
- 4.4.4. **National Accreditation Board for Education & Training (NABET):** NABET accredits education, training, and skill development organisations to national and international standards, enhancing quality and credibility. It operates under the Quality Council of India (QCI).
- 4.4.5. **National Board for Quality Promotion (NBQP):** NBQP promotes quality and excellence in India by setting standards, providing certifications, and conducting audits to enhance competitiveness and customer satisfaction.
- 4.4.6. **Special Projects Group (Cells and Divisions)**
 - 4.4.6.1. **Project Planning and Implementation Division (PPID)**
 - 4.4.6.2. National Division for Industry Excellence (NDIE)
 - 4.4.6.3. Projects Analysis and Documentation Division (PADD)
 - 4.4.6.4. Strategy & Policy Division (SPD)

5. Key projects

- 5.1. In 25 years, the Quality Council of India (QCI) has improved quality of life through initiatives in green development, inclusive growth, digital economy, public infrastructure, and technology. It involves stakeholders to uphold quality standards and enhance citizens' well-being.
- 5.2. As the National Accreditation body of the country, it has been ranked 5th in the world in the recent Global Quality Infrastructure Index (GQII) 2021. In the past 10 years, QCI Professionals have engaged with 90+ ministries and departments of the Union and State Governments in executing 400+ projects across multivariate spheres.
- 5.3. The various Third-Party Evaluation of projects undertaken by QCI include the following:
 - 5.3.1. Third-Party Evaluation of Animal Husbandry & Infrastructure Development Fund (AHIDF) Scheme

List of few projects being awarded to QCI on nomination basis:

- 5.3.2. National Gopal Ratna Award 2022
- 5.3.3. National Gopal Ratna Award 2023
- 5.3.4. National Gopal Ratna Award 2024
- 5.3.5. Third-Party Evaluation of Scheme 1 & 2 of National Horticulture Board (NHB)

- 5.3.6. MSME Sustainable (ZED) Certification Scheme for FY 2023-24 (Ongoing)
- 5.3.7. Third Party Sampling & Analysis of Coal (Ongoing)
- 5.3.8. GeM vendor assessment
- 5.3.9. Quality Intervention to create a Quality Ecosystem for Khadi
- 5.3.10. Transformation of Food Corporation of India – Assessment of FCI Warehouses

and more than 100 further projects are being awarded to QCI on nomination basis. Work Order will be provided as per requirement.

National Programme for Dairy Development (NPDD) Scheme

6. About National Programme for Dairy Development (NPDD) Scheme

- 6.1. The National Programme for Dairy Development (NPDD) is designed to provide both technical and financial assistance to support the holistic development of the dairy sector. The scheme primarily focuses on strengthening the infrastructure for milk production, processing, procurement, and marketing, while also supporting capacity-building initiatives for dairy farmers through structured training programmes.
- 6.2. Implemented with the objective of promoting dairying in a scientific and integrated manner, the scheme seeks to enhance the overall efficiency and productivity of milk production systems. By supporting Milk Federations and Milk Unions in extending their operations and infrastructure, NPDD plays a crucial role in meeting the growing domestic demand for milk. Ultimately, NPDD contributes towards “enhancing the quality of milk and milk products, increasing the share of milk procurement under organized channels, and facilitating sustainable growth in milk production & farmer income through cooperative structure”.
- 6.3. The scheme has following two components with their respective objectives:
 - 6.3.1. Component "A" of NPDD focuses on creating/ strengthening of infrastructure for quality milk testing equipment as well as primary chilling facilities for State Cooperative Dairy Federations/ District Cooperative Milk Producers' Union/ SHGs/ Milk Producer Companies/ Farmer Producer Organizations throughout the country.
 - 6.3.2. Component 'B' of the NPDD scheme "Dairying through Cooperatives" aims to increase sale of milk and dairy products by increasing farmer's access to organized market, upgrading dairy processing facilities and marketing infrastructure and enhancing the capacity of producer owned institutions, thereby contributing to increase in returns to milk producers in the project area.

Genesis of the Study

In view of evaluating the effectiveness, outcomes, and areas for improvement within NPDD scheme, QCI proposes the following brief approach and work plan to carry out a third-party assessment.

7. Understanding of the Evaluation Context

- 7.1. Assess the implementation status and on-ground outcomes of NPDD components A & B.
- 7.2. Capture beneficiary-level experiences and feedback on the programme.
- 7.3. Identify operational bottlenecks, highlight best practices, and recommend improvements for future policy iterations.

- 7.4. Provide evidence-based insights on the programme's contribution to the dairy sector's growth and sustainability.

Scope and Objectives

8. Objective of the Study

- 8.1. To study and evaluate / appraise the impact of different components of NPDD Scheme on the targeted beneficiaries / sectors / areas in terms of both quantitative and qualitative factors.
- 8.2. To do the physical assessment of infrastructure created under the component A and Component B of NPDD on sample basis.
- 8.3. To undertake an output-outcome analysis of NPDD as per the objectives of the scheme.
- 8.4. To assess if the funds released by GoI under NPDD has been utilized as per the NPDD scheme guidelines / Operational Guidelines / Financial Management Manual and only for the purposes for which the funds were provided, assess diversion or duplication in project implementation if any.
- 8.5. To study the gaps in implementation if any, qualitative aspects of implementation, and suggest measures for improvement in the future.
- 8.6. To give suitable recommendations for the continuation / modification / dis-continuation of components / activities of the scheme.

9. Scope of Work

- 9.1. Review program documents, guidelines, and reports to gain a comprehensive understanding of the program's objectives, strategies, and implementation modalities.
- 9.2. Conduct field visits to project sites across different regions in India to assess the on-ground implementation of the Program.
- 9.3. Collecting and analyzing relevant data and information from various stakeholders, including dairy farmers, end implementing agencies, relevant State departments, and government officials participating under the program.
- 9.4. Assessment of the program's impact on key performance indicators, such as increment in the milk procurement, enrollment of new members including women members, increase in sales & marketing, improvement in quality of raw & processed milk, decrease in losses due to sourage, decrease of adulteration in milk, increase in milk price paid to farmers, increase in income of SIA/EIA/DCS etc., ICT infra utilization & its outcome/benefit, increase in the milk and value added product processing capacities & its utilization, increase in production and productivity of farmers covered under the productivity enhancement activities and other project components.
- 9.5. Deployment of resources by Project Implementing Agencies under Productivities Enhancement Program as per the scheme guideline as per the project.
- 9.6. Identifying successful practices, innovations, and lessons learned from the implementation of the program to inform future interventions and replication in other regions or countries.
- 9.7. Providing actionable recommendations for enhancing the program's effectiveness, efficiency, and sustainability.

Methodological Framework

10. Research design and approach

- 10.1. To conduct a robust evaluation of the National Programme for Dairy Development (NPDD), QCI proposes a comprehensive methodological framework rooted in a mixed-methods research design. This approach leverages both quantitative and qualitative data to assess the programme's implementation, outcomes, and stakeholder experiences. The framework is designed to ensure evidence-based insights, regional representativeness, and practical recommendations.
- 10.2. The evaluation will follow a triangulation-based model, incorporating:
 - 10.2.1. Research (Primary & Secondary)
 - 10.2.1.1. Primary research (field surveys, beneficiary interviews, KIIs, FGDs)
 - 10.2.1.2. Secondary research (policy documents, scheme guidelines, reports)
 - 10.2.2. Expert/stakeholder consultations (including SIAs, milk unions, and DAHD officials)
 - 10.2.3. Financial Assessment (assessment of funds released by GoI under NPDD and its utilization as per NPDD Scheme guidelines/ Operational Guidelines/ Financial Management Manual and only for the purpose the fund was provided)
- 10.3. Triangulation Approach will offer a comprehensive analysis of NPDD Scheme, by integrating primary research, secondary research, and expert/stakeholder consultations.

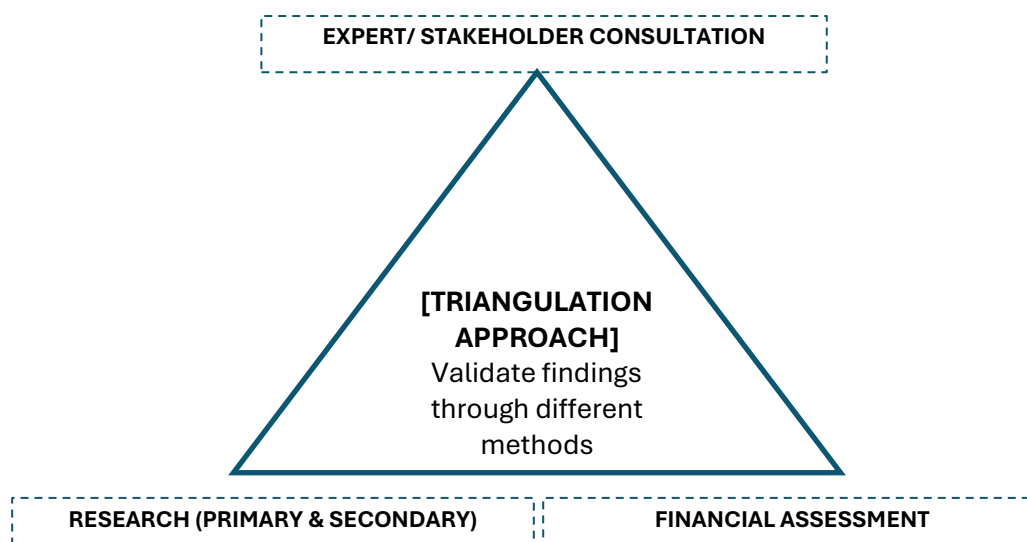


Figure 2: Triangulation Approach

- 10.4. This blended approach ensures a multi-perspective understanding of the programme, helping validate findings, highlight best practices, and identify areas for policy strengthening.

11. Proposed Activities/Actions and Expected Insights

Table 1: Proposed Activities/Action and Expected Insights from Third-Party NPDD Scheme Evaluation

Sr. No.	Research Method	Activities/Actions	Expected Insights
1	Research (Primary & Secondary)	- Review scheme documents, DPRs, fund release orders, monitoring reports, operational manuals, and MIS data. - Design and deploy structured & semi-structured evaluation framework & tools (questionnaires, discussion guides) - Conduct primary data collection via household surveys, KIs, and FGDs.	- Contextual understanding of implementation models across states (sample basis). - Trends in fund disbursal, utilization, and physical achievement. - Ground-level feedback from beneficiaries and implementing agencies.
2	Output-Outcome cum Gap Analysis	- Develop a Framework Matrix aligned with scheme objectives and components. - Map outputs (e.g., infrastructure created) to outcomes (e.g., increased procurement, improved milk quality). - Analyze data through comparative and time-series aspects.	- Degree of alignment between intended and actual outcomes. - Effectiveness of infrastructure in meeting programme objectives. - Identification of areas where output hasn't translated into impact. - Identification of Gaps (if any) in implementation of the scheme.
3	Financial Assessment	- Review fund allocation, release, and utilization reports. - Assess compliance with financial guidelines and fund flow processes. - Examine utilization certificates, audit records, and potential duplication/ diversion of funds.	- Efficiency and timeliness of financial processes. - Financial compliance across implementing agencies. - Insights into potential bottlenecks in fund usage or reporting.
4	Stakeholder & Expert Consultation	- Conduct consultations with DAHD, NDDB, SIAs, Milk Federations, Milk Unions, and DCSs. - Hold expert panels and roundtables with domain specialists in dairy economics and cooperative governance. - Analyze qualitative feedback and policy suggestions.	- Strategic and operational feedback from key Informants. - Identification of systemic challenges and good practices. - Recommendations for future policy improvement. - Identification of successful practices, innovation & lessons learned.

12. Identification of Stakeholders

To ensure a comprehensive and grounded evaluation of the NPDD scheme, QCI has identified the following key stakeholders for structured interactions and consultations:

- Department of Animal Husbandry and Dairying (DAHD) – Central Nodal Ministry
- National Dairy Development Board (NDDB) – Technical and implementation support agency
- State Implementing Agencies (SIAs) – State-level nodal agencies
- Milk Federations and Milk Unions – Key intermediaries in dairy infrastructure and procurement
- Dairy Cooperative Societies (DCSs) – Grassroots-level implementing and beneficiary interface
- Beneficiary Farmers – End users and direct recipients of scheme benefits
- Subject Matter Experts and Policy Advisors – Specialists in dairy economics, cooperative management, and infrastructure governance

These stakeholders will be engaged through in-depth interviews, focus group discussions (FGDs), and field-level interactions to gather diverse and meaningful insights across operational, financial, and policy dimensions of the programme.

Sampling

For the purpose of ensuring balanced regional representation, QCI proposes to divide the country into six zones, namely *North & Central, South, East, West, North East, & Norther Hilly States*.

The final selection of states and districts will be undertaken in consultation with the Department of Animal Husbandry and Dairying (DAHD). However, to initiate the planning process, QCI proposes the following indicative sampling distribution across levels for respective zones.

13. Sampling Strategy

To ensure national representation and capture regional diversity, the proposed sampling framework adopts a zone-based, multi-stage stratified sampling approach. The sampling plan is as follows:

- No. of States: Min. 2 states per zone
- No. of Union Territory: Any 1 UT
- No. of Districts: Min. 2 District per State
- No. of Federation: Min. 1 State Level Federation per State
- No. of Milk Unions: Min. 2 Unions/State & 1 Union of UT
- No. of DCS: Min. 10 Villages/Union
- No. of Farmers: Min. 10 Farmers/Village

14. Proposed Sampled States & Districts

The following is the proposed distribution of states and districts for field data collection, aligned with the zonal sampling strategy. Final selection will be undertaken in consultation with DAHD.

Table 2: Proposed States & Districts for Sampling

S. No.	Zone	Proposed State	Proposed District
1	North	Uttar Pradesh	Badaun, Jaunpur/Pratapgarh
		Punjab	Bhatinda, Jalandhar
		Madhya Pradesh	Indore, Katni
2	South	Karnataka	Bangalore, Mandya
		Kerala	Malabar- Wayanad, Palakkad or Ernakulam- Ernakulam, Thrissur

		Tamil Nadu	Coimbatore, Madurai
3	East	Bihar	Bhojpur, Rohtas/ Muzaffarpur
		Orissa	Cuttack, Puri
4	West	Gujarat	Anand, Mehsana
		Rajasthan	Bhilwara, Jaipur
5	North East	Meghalaya	East Khasi Hills, Ribhoi
		Sikkim	Gangtok, Pakyong
6	Northern Hilly State	Himachal Pradesh	Mandi, Bilaspur
		Uttarakhand	Champawat, Pithoragarh
7	UT	Jammu & Kashmir	Jammu, Pulwama/Anantnag

Operational Framework & Execution Plan

To ensure timely, efficient, and high-quality execution of the evaluation, QCI proposes a structured operational framework comprising the following key stages:

15. Preliminary Analysis and Development of Evaluation Framework

A preliminary exploratory review will be conducted through consultations with key stakeholders and a scan of existing documents. Based on this, an Evaluation Framework will be developed, outlining the key indicators, domains of inquiry, and analytical models aligned with NPDD's objectives and components.

16. Preparation and Optimization of IT Platform

QCI will deploy latest and most convenient technology platforms for the digital data collection via mobile/tablet-based platform to execute the study that includes real time monitoring of the study to maintain the highest level of accuracy. The approved questionnaires shall be uploaded onto the CAPI platform with all necessary checks and balances, leaving no room for error. It shall include features such as flagging, geo-tagging, time-stamping of images, short (30 seconds) video-recording, and real-time monitoring of the primary collected data to maintain the integrity of the data captured.

17. Pilot Study

A pilot study will be conducted to check the effectiveness of the questionnaire and the data collection tools. The learnings and observations from the pilot study will be shared with the DAHD for inputs (if any). It will be helpful to identify and address the probable challenges, resolve the bottlenecks, and make the evaluation study smooth and seamless. The inputs and recommendations from DAHD will be further incorporated in the study.

18. Training and Deployment of Assessors

A team of enumerators and field supervisors will undergo detailed training on scheme objectives, survey tools, digital platforms, and ethical guidelines. Deployment will be staggered across zones to ensure coordinated and high-quality data collection.

19. Primary Survey, Stakeholder Interviews and Focus Group Discussions (FGDs)

Extensive field surveys/ interviews will be conducted with identified beneficiaries and stakeholders across sampled locations. This includes structured interviews with farmers, Dairy Cooperative Society (DCS) members, district level milk union and state level federation officials, and implementation personnel.

Focus Group Discussions (FGDs) will be organized to complement quantitative data with collective qualitative insights. These discussions will focus on implementation experiences, challenges, and context-specific dynamics among key stakeholder groups.

20. Data Quality Assurance

A dedicated team of professionals will be deployed at the QCI headquarters for real-time monitoring of the interviews and feedback to the ground team of interviewers. The collected data will be quality checked in real time by the QCI professional at the backend and will be further re-checked at multiple levels by the experienced quality check professionals to eliminate the margin of error and maintain the quality and authenticity of the data.

During the on-ground assessment, a team of senior QCI professionals will visit the locations for monitoring and providing the required support where the interviewers will be deployed for assessment.

21. Data Analysis and Interpretation

The data collected through the primary survey will be collated and analyzed using appropriate statistical and thematic techniques for drawing observations and suggestions for the report as per the NPDD scheme objectives.

22. Final Reporting


Findings will be synthesized into a comprehensive report, including insights, best practices, and actionable recommendations. A stakeholder presentation will be made before final submission of the evaluation report, datasets, case studies, and supporting annexures.

Brief Work Plan & Key Deliverables

QCI proposes 4 months implementation plan from the date of the award of work for the successful execution of activities including key activities like conceptualization and development of evaluation framework including schedules/questionnaires, training of assessors and deployment/mobilization plan of resources, pilot, improvisation based on pilot experiences, field survey, data analysis and reporting after the contract is awarded. Mentioned below is the timeline breakup (*the timeline is subject to cooperation from DAHD, including necessary approvals and review*).

Key Activity	Activity Start (Months)	Activity End (Months)	Duration (Months)	Key Deliverable
Framework development & Submission of Inception Report	0	0.5	0.5	Inception Report
Field Survey covering a minimum of 40% of the sample and preparation of Mid-term Report	0.5	2	1.5	Mid-term Report & Presentation
Preparation and submission of draft final report	2	3.5	1.5	Draft Report
Presentation before DAHD/ seeking comments of DAHD on the draft report	3.5	3.75	0.25	Presentation on Draft Report
Submission of Final Report	3.75	4	0.25	Final Report
Total		4 Months		

Graphical representation of the project timelines are as follows:

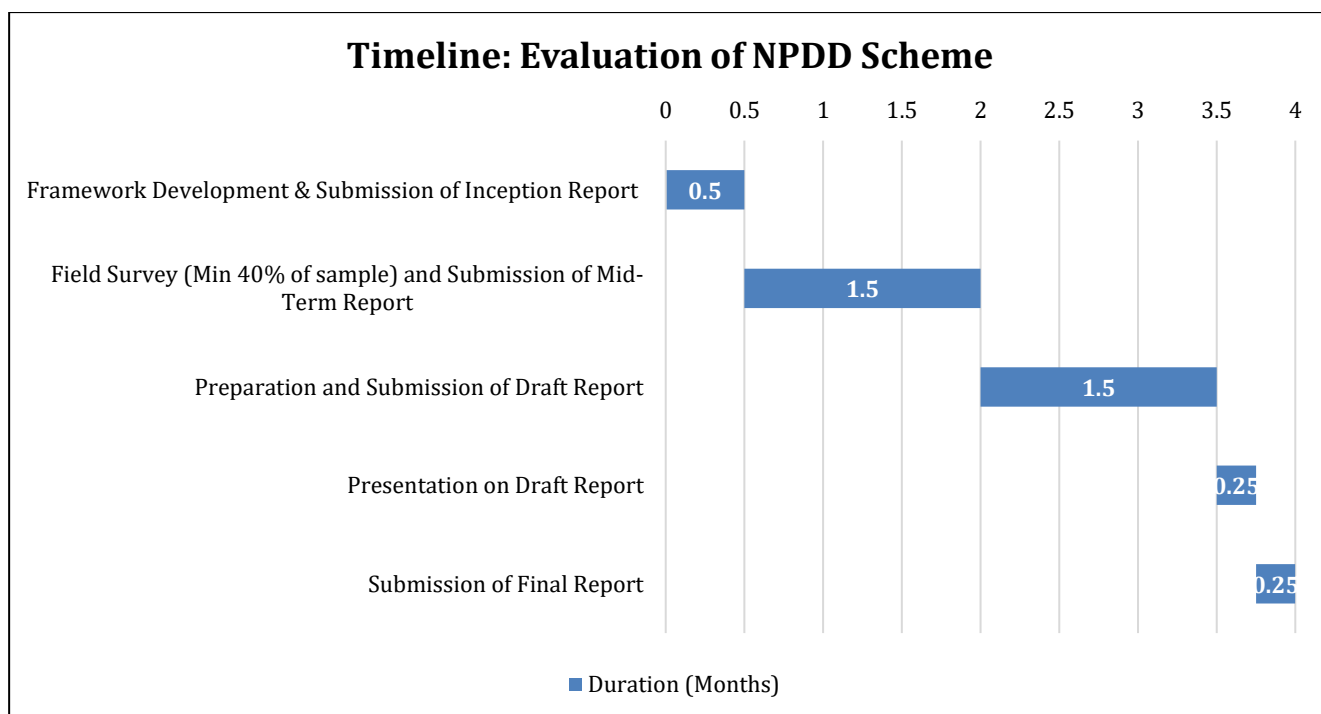

Financial

23. Project Financials

The total cost for conducting the Third-Party Evaluation of the National Programme for Dairy Development (NPDD) is **Rs. 84,96,000/-** (including all taxes) proposed to be borne by the Department of Animal Husbandry and Dairying (DAHD), Ministry of Fisheries, Animal Husbandry and Dairying, Government of India (GoI).

Note:

- In the event of any extension in project timeline or scope, additional charges will be applicable on a pro-rata basis.
- The above financials do not include any additional costs related to:
 - Dashboard or portal development, if required separately.

24. Payment Structure:

The payment structure for the proposed methodology is outlined based on this timeline.

Table 3: Payment Structure

Sr. No.	Schedule / Milestones	Percentage (%) of Contract Value
1	Award of Work Order (Mobilization Advance)	30 %
2	Submission of Draft Report on Completion of On-Field Assessment	40 %
3	Submission & Approval of Final Report	30 %

Note:

- The schedule/milestones mentioned earlier under “Brief Work Plan & Key Deliverables” will be applicable to the total cost.
- Any term/condition that is unaccounted for would not be considered waived and would be determined in consultation with both parties.

Annexures

25. QCI's Previous Projects with DAHD

25.1. Third-Party Evaluation of Animal Infrastructure Development Fund (AHIDF) Scheme

Completion Certificate AHIDF Scheme Evaluation

217210/2024/ADMIN_3-DADF

डॉ. ओ.पी. चौधरी
Dr. O.P. Chaudhary


 सत्यमेव जयते

संयुक्त सचिव
भारत सरकार
मत्स्यपालन, पशुपालन एवं डेयरी मंत्रालय
पशुपालन एवं डेयरी विभाग
कृषि भवन, नई दिल्ली-110001
Joint Secretary
Government of India
Ministry of Fisheries, Animal Husbandry & Dairying
Department of Animal Husbandry and Dairying
Krishi Bhawan, New Delhi-110001

D.O.No.AA-17/1/2023-NLM-DADF

Dated.01.07.2024

Dear Mr. Prakash Sir,

This completion certificate is to certify that the "Mid-Term Third-Party Evaluation of Animal Husbandry Infrastructure Development Fund (AHIDF)" as per the F. No.: AA-17/1/2023-NLM-DADF dated 23rd December 2023 was satisfactory concluded by Quality Council of India (QCI) and submitted all deliverables within the stipulated project timelines. QCI was selected for the said assessment through a competitive bidding process. The evaluation study was commenced on 2nd January 2024 and final report after the brief presentation was submitted on 28th March 2024. The project details are as follows:

- a) **Project Name:** Third-Party Evaluation of Animal Husbandry Infrastructure Development Fund (AHIDF)
- b) **Duration:** 3 Months
- c) **Location:** PAN India
- d) **Project Fee:** ₹ 87,68,816/- (Eighty-Seven Lakh Sixty-Eight Thousand Eight Hundred Sixteen Only)
- e) **Key Components:** Impact Evaluation of the AHIDF Scheme on the overall creation/enhancement of capacities/capabilities associated with the following sectors:
 - i. Dairy Processing and Value Addition Industries
 - ii. Meat Processing and Value Addition Industries
 - iii. Breed Improvement Technology and Breed Multiplication Farm
 - iv. Animal Feed Manufacturing Industries
 - v. Animal Waste to Wealth Management Units
 - vi. Veterinary Vaccine and Drug Production Facilities
- f) **Client:** Department of Animal Husbandry and Dairying (DAHD), Ministry of Fisheries, Animal Husbandry and Dairying, Government of India
- g) **Scheme Budget:** ₹ 15,000 Crore for FY 2020-21 to 2022-23

2. QCI fulfilled all requirements and delivered the final report after a brief presentation, demonstrating comprehensive evaluation and adherence to project timelines.
3. This certificate is issued as recognition of QCI's commitment and professionalism in executing the evaluation study.

Warm Regards,

Dr. Hari Prakash
Director, PPID
Quality Council of India (QCI)


(Dr. O.P. Chaudhary)

1

File No. AA-17/1/2023-NLM-DADF, Tel: +91-11-23386115, Fax: +91-11-23386115, E-mail: jspfdadf@gmail.com, jspfdadf@nic.in
Generated from eOffice by LPI SAIKAWAL, DEPUTY COMMISSIONER(NLM-DADF), DEPUTY COMMISSIONER, DADF-DEPARTMENT on 02/07/2024 02:17 PM

Work Order AHIDF Scheme Evaluation

F. No. AA-17/1/2023-NLM-DADF

Government of India

Ministry of Fisheries, Animal Husbandry and Dairying
Department of Animal Husbandry and Dairying

Chandralok Building, New Delhi.

Dated, the 23rd December, 2023

To,

M/s Quality Council of India
2nd Floor, Institution of Engineers Building
Bahadur Shash Zafar Marg, New Delhi – 110002.

Subject:- Appointment of an agency for evaluation study of Animal Husbandry Infrastructure Development Fund (AHIDF)

Sir,

I am directed to convey the approval of the competent authority for appointment of M/s Quality Council of India as a mid-term evaluation Agency for evaluation of AHIDF with the following terms and conditions including those mentioned under **Other Conditions**:

2. Terms of Reference (TOR) for the evaluation study are, as follows:

- i. Infrastructure created vis-à-vis the infrastructure requirement i.e., the infrastructure gap vis-à-vis the level of production of dairy/feed/meat poultry/agro-waste in the States
- ii. Capacity utilization of the assets created
- iii. Impact of the scheme across the value chains including the benefit flowing down the line
- iv. Impact on availability of milk and meat & poultry products to consumers
- v. Impact on unorganized dairy and meat & poultry sector
- vi. Impact on export promotion w.r.t to dairy and meat & poultry products
- vii. Availability of quality and cost-effective concentrated animals feed to the cattle, buffalo, sheep, goat, pig and poultry
- viii. The impact on the level of income of farmers and proportion of local farmers benefited directly and indirectly
- ix. The impact on generation of employment i.e., both in number and types of employment generated directly and indirectly.
- x. Recommendations for the overall improvement of the functioning of the scheme
- xi. The implementation/ operational difficulties on the ground and suggest/recommend corrective measures to improve efficiency of implementation
- xii. Suggestion on changes/modification in the Scheme Guidelines for timely & effective implementation of the scheme


अनामिका निगम / Anamika Nigam
अवर सचिव / Under Secretary
भारत सरकार / Govt. of India
मत्स्यपालन, पशुपालन एवं डेयरी विभाग
Ministry of Fisheries, Animal Husbandry & Dairying
पशुपालन और डेयरी विभाग
Department of Animal Husbandry & Dairying
एचि बरद नई दिल्ली/Krishi Bhavan, New Delhi-110001

- xiii. Performance of the scheme based on the Output / Outcome indicators, among others, in the following format:

S.No.	Output	Outcome
a)	Number of applicants/beneficiaries/units supported for development of infrastructure	No. of Animal Husbandry and allied sector units operationalised
b)	Investment leveraged	Capacity Creation/enhancement
c)	Amount of interest subvention provided to beneficiaries	Employment Generated

NOTE: Site visits are envisaged as part of the Mid-term Evaluation Agency's scope of work.

Other Conditions:

- This work order of engagement of M/s Quality Council of India as Mid-term Evaluation Agency shall be valid for 3 (three) months from the date of acceptance of this work order. However, its performance as Mid-term Evaluation Agency shall be reviewed initially, after completion of 1 month from the date of acceptance of this work order by M/s Quality Council of India.
- All technical information and manuals, from time to time, shall be drawn up in English language.
- M/s Quality Council of India shall, at its sole cost and expense, deploy staff and personnel as indicated in the Technical Bids according to the requisite qualification mentioned in the Technical Bid of the company. The number of manpower to be provided has already been mentioned in the RFP. The manpower shall not be liable for frequent replacement unless the personal resigned from the post where has been deputed. In case of resignation, prior intimation at least one month before to be indicated to DAHD.
- M/s Quality Council of India shall ensure that the information/details related to the assignment which comes to the knowledge of M/s Quality Council of India or its personnel, during the course of provision of services under this work order, are kept confidential and are not, directly or indirectly, disclosed to any third party.
- If any dispute or difference of any kind whatsoever arises between DAHD and M/s Quality Council of India in connection with or arising out of or relating to or under this order, both parties shall promptly and in good faith negotiate with a view to its amicable resolution and settlement. In the event that no amicable resolution or settlement is reached within a period of thirty (30) days from the date on which the above mentioned dispute or difference arose, such dispute or difference shall be settled finally by Secretary, DAHD whose decision shall be final and binding.



अनामिका निगम / Anamika Nigam
अवर सचिव / Under Secretary
भारत सरकार / Govt. of India
मत्स्यपालन, पशुपालन एवं डायरी विभाग
Ministry of Fisheries, Animal Husbandry & Dairying
पशुपालन और डायरी विभाग
Department of Animal Husbandry & Dairying
प्लॉट नं. 1, टिकरी/55555 Bikaner, New Delhi-110021

- f) DAHD shall have the right to terminate the appointment vide this order by giving a notice of 15 (Fifteen) days in writing. In the event of termination of the appointment for reasons not solely attributable to M/s Quality Council of India, DAHD will reimburse all the expenses incurred by M/s Quality Council of India upon submission of appropriate evidence by M/s Quality Council of India. If the appointment is terminated due to reasons attributable solely to M/s Quality Council of India or in case of termination of the appointment by M/s Quality Council of India for reasons not solely attributable to DAHD, the latter will forfeit the performance security, if any, of M/s Quality Council of India.
- g) For carrying out services as Mid-term Evaluation Agency as per this order DAHD shall pay, M/S Quality Council of India @ Rs. 87,68,816/- (Rs. Eighty Seven Lakh Sixty Eight Thousand Eight Hundred Sixteen only) inclusive of all taxes as per terms of RFP for evaluation study of Animal Husbandry Infrastructure Development Fund (AHIDF).
- h) Rs 4,38,500/- (Rupees Four Lakh Thirty Eight Thousand Five Hundred only) shall be deposited by M/s Quality Council of India as Performance Security (equivalent to 5 (Five) percent of the cost of financial proposal) from a Nationalized/Scheduled Bank, before start of work on assignment, in form of a Bank Guarantee substantially in the form specified at Annexure A of the Work Order in RfP. Performance Security will be retained by DAHD until the completion of the assignment by the M/s Quality Council of India and be released 60 (Sixty) Days after the completion of the assignment.
- i) Work Order shall be issued, in duplicate, by the DAHD to M/ Quality Council of India and M/s Quality Council of India shall, within 3 (three) days of the receipt of the Work Order, sign and return the duplicate copy of the Work Order in acknowledgement thereof. In the event the duplicate copy of the Work Order duly signed by M/s Quality Council of India is not received within 3 (three) days of the receipt of the Work Order, DAHD may, unless it consents to extension of time for submission thereof, appropriate the Earnest Money Deposit of such Applicant in full or to the extent of mutually agreed pre-estimated loss and damage suffered by DAHD on account of failure M/s Quality Council of India to acknowledge the Work Order, and the next highest ranking Applicant shall be considered.
- j) Payments to M/s Quality Council of India
- DAHD will not consider advance payment to M/s Quality Council of India.
 - M/s Quality Council of India will submit pre-receipted invoices in triplicate, complete in all respects, on satisfactory completion of work, for necessary settlement to DAHD. Payment would be made by DAHD within 30 days of submission of invoice, subject to successful completion of the required work detailed in the RfP Document. The invoice should be submitted along with complete details of the work undertaken during the contract, supporting documents and bills (if required) as well



अनामिका निगम / Anamika Nigam
 अवर सचिव / Under Secretary
 भारत सरकार / Govt. of India
 मत्स्यपालन, पशुपालन एवं डेयरी विभाग
 Ministry of Fisheries, Animal Husbandry & Dairying
 पशुपालन और डेयरी विभाग
 Department of Animal Husbandry & Dairying
 एन सी ई विस्स / NCEI Building - New Delhi-110021

as copies of the work/ material / produced during the contract, for which the bills are submitted.

- iii. For facilitating Electronic transfer for funds, the M/s Quality Council of India shall be required to indicate the name of the Bank and Branch, account number (i.e. bank names, IFSC Code and Bank A/c No.) and also forward a cheque leaf duly cancelled to verify the details furnished to DAHD. These details should also be furnished on the body of bill submitted for payment by M/s Quality Council of India.
- iv. Currency: The price is payable to M/s Quality Council of India in local currency i.e. Indian Rupees.
- v. Payment for Additional Services: For the purpose of determining the remuneration due for additional services as may be agreed under relevant clauses for modification in this Work Order by DAHD.
- k) The Evaluation team of M/s Quality Council of India shall report to Joint Secretary, AHIDF for necessary directions.
- l) All future communications by M/s Quality Council of India shall be done with the office of Joint Secretary AHIDF (email jspf-dadfi@nic.in, cc to lipi.s@gov.in).
- m) The conditions mentioned in RfP shall be considered to be integral part of this Work Order.

This issues with the approval of the Competent Authority and as concurred by IFD vide No. 117/25383 dated 18.12.2023.

Yours faithfully,



(Anamika Nigam)

Under Secretary to Government of India

Copy to:

- 1 PPS to Secretary, AHD
- 2 PPS to AS&FA, DAHD
- 3 PPS to Animal Husbandry Commissioner, DAHD
- 4 PPS to JS (NLM/PC)
- 5 JC (AH)/DC (AHIDF)
- 6 NIC for uploading the work order on Department's website

अनामिका निगम / Anamika Nigam
अवर सचिव / Under Secretary
भारत सरकार / Govt. of India
मत्स्यपालन, पशुपालन एवं डेयरी मंत्रालय
Ministry of Fisheries, Animal Husbandry & Dairying
पशुपालन और डेयरी विभाग
Department of Animal Husbandry & Dairying
एन सी ई विंग / NCE Wing, New Delhi-110001

Copy for Information to:

1. PPS to Hon'ble Union Minister for Fisheries, Animal Husbandry & Dairying
2. PPS to Hon'ble MoS for Animal Husbandry & Dairying

25.2. Screening of Applications received through online National Award Portal for National Gopal Ratna Award 2024, 2023, & 2022 (on Nomination Basis)

Work Order for National Gopal Ratna Award 2024

F. No. N-05015/114/2020-CDD (E-17998)
Government of India
Ministry of Fisheries, Animal Husbandry and Dairying
Department of Animal Husbandry and Dairying
R. No 532, Krishi Bhawan, New Delhi
Date: 3rd October, 2024

To,
The Secretary General,
Quality Council of India(QCI),
2nd Floor, Institution of Engineering Building,
Bahadurshah Zafar Marg, New Delhi.

Subject: Work order for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2024-reg.

Sir,

I am directed to refer to your proposal submitted vide e-mail dated 04.09.2024 on the above subject and to convey the approval of the Competent Authority for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2024 as under:

S No.	Scope of Work/Exercise	No. of Resources/ day	Duration (tentative) in days	Total fees to be paid by DAHD (Amount in Rs.)
1.	Updating the strategy and evaluation scorecard, in consultation with DAHD, and developing a detailed roadmap for timely execution of the project			
2.	Data cleaning of applications received to find unique nominations	4 (1 Project Lead and 3 Research Associate)	1 st – 15 th Oct 2024 (15 Days)	Rs. 4,20,000/- (Rupees four lakh twenty thousand only) (Exclusive GST)
3.	Scrutinizing and scoring of all the applications as per score card provided by DAHD (enclosed) and selecting top 20 applications from non- NER States and 10 applications from NER States in each of the three categories			
4.	Re-scoring and creating detailed profiles for selected top 20 applications from non- NER States and 10 applications from NER States (as instructed by DAHD) in each of the three categories-based post field verification i.e. on the basis of factual information collected by NDDB/DAHD.	4 (1 Project Lead and 3 Research Associate)	1 st -10 th Nov., 2024 (10 days)	
5.	Creating detailed profiles for the top 20 applications in each category for non-NER States and top 10 applications in each category for NER States based on the parameters mentioned in the objective for Award Screening Committee.			

1 /2...




-2-

2. Statutory tax/GST will be applicable as per GST rules. Resource cost is calculated by considering various factors- Professional fee, Promotion & Bonus, Logistical support like Travel & Food Allowance, Laptop, stationery and Phone Allowance e.t.c. The QCI will provide the name of all project team members for the duration of project before the start of the project to enable them entry-pass of DAHD. The undersigned is the nodal officer /contact point for the NGRA 2024.
3. If necessary, the time schedule may be reduced with the mutual consent of QCI & DAHD, accordingly, QCI will have to depute more manpower to complete the task within the given timeframe.
4. The QCI will provide scoring of all the applications and detailed profiles of the top 20 shortlisted applications in each category for non-NER States and top 10 applications in each category for NER States to DAHD in soft and hard copies, duly signed, on it's letter head.
5. The payment of project fee shall be paid by DAHD as 30% advance and remaining 70% after the satisfactory completion of the project.
6. An agreement between DAHD and QCI regarding terms and condition will be finalized by QCI and signed by DAHD & QCI both.
7. QCI is therefore requested to start the work as mentioned above right from the date of issue of this letter.
8. This issues with the approval of the competent authority and AS&FA vide Dy No. E-17998 Note#608 dated 01.10.2024.

Encl. Score card

Yours sincerely


(Ajith Kumar K.)
Assistant Commissioner (DD)
011-23383812
[e-mail : ajith.kk@gov.in]

Copy to:

1. The Joint Commissioner (RGM), DAHD, Krishi Bhawan NEW Delhi –With the request to make 30% advance payment to QCI from RMG head.
2. PPS to the Additional Secretary (CDD), DAHD

Work Order for National Gopal Ratna Award 2023

F. No. N-05015/114/2020-CDD (E-17998)
Government of India
Ministry of Fisheries, Animal Husbandry and Dairying
Department of Animal Husbandry and Dairying
R. No 532, Krishi Bhawan, New Delhi
Date: 12th October, 2023

To,
The Secretary General,
Quality Council of India(QCI),
2nd Floor, Institution of Engineering Building,
Bahadurshah Zafar Marg, New Delhi

Subject: Work order for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2023(to be conferred on 26.11.2023).

Sir,

I am directed to refer to your proposal vide e-mail dated 25.09.2023 on the above subject and convey the approval of the Competent Authority for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2023(to be conferred on 26.11.2023) as under:

S No.	Scope of Work/Exercise	No. of Resources/ day	Duration (tentative) in days	Total fees to be paid by DAHD (Amount in Rs.)
1.	Updating strategy and evaluation score card in consultation with DAHD, and developing a detailed roadmap for timely execution of the project.	4 (1 Project Lead and 3 Research Associate)	16 th -25 th Oct 2023 (10 Days)	Rs. 2,75,360/- (Rupees Two lakh seventy five thousand three hundred sixty only) (Inclusive of GST/all taxes)
2.	Data cleaning of applications received to find unique nominations.			
3.	Analyzing data provided by applicants, verifying claims made in the nominations via secondary research and looking for more relevant information via open search (social media, internet and other source platforms), while making the profiles.			
4.	Scrutinizing and scoring of all the received applications based on the evaluation score card and selecting top 20 applications in each of the three categories and handed over to the Award Screening Committee, DAHD.			
5.	Re-scoring and creating detailed profiles for selected top 20 applications in each category, post field verification by NDDDB/DAHD.	4 (1 Project Lead and 3 Research Associate)	11 th -15 th Nov, 2022 (5 days)	

1 / 2...

Cond...

-2-

2. If necessary, the time schedule may be reduced with the mutual consent of QCI & DAHD, accordingly, QCI will have to depute more manpower to complete the task within the given timeframe.
3. The QCI will provide the name of all project team members for the duration of project before the start of the project to enable them entry-pass of DAHD. The undersigned is the nodal officer /contact point for the NGRA 2023.
4. The payment of project fee shall be paid by DAHD as 30% advance and remaining 70% after the satisfactory completion of the project.
5. An agreement between DAHD and QCI regarding terms and condition will be finalized by QCI and signed by DAHD & QCI both.
6. QCI is therefore requested to start the work as mentioned above right from the 16th October 2023.

This issues with the approval of the competent authority and AS&FA vide Dy No. E-17998 Note#457 dated 10.10.2023

Yours sincerely



(Ajith Kumar K.)
Assistant Commissioner (DD)
011-23383812
[e-mail : ajith.kk@gov.in]

Copy to:

1. The Joint Commissioner (RGM), DAHD, Krishi Bhawan NEW Delhi –With the request to make 30% advance payment to QCI from RMG head before the closing date of the applications i.e 15th Oct-2023.
2. PPS to the Secretary(AHD)/ PPS to Additional Secretary (CDD), DAHD

Work Order for National Gopal Ratna Award 2022

N-050158114/2020-CDD(Part(1) [E-23066]
Government of India
Ministry of Fisheries, Animal Husbandry and Dairying
Department of Animal Husbandry and Dairying
(Dairy Division)

R. No 532, Krishi Bhawan, New Delhi

Date: 7th October, 2022

To,
The Secretary General,
Quality Council of India(QCI),
2nd Floor, Institution of Engineering Building,
Bahadurshah Zafar Marg,
New Delhi

Subject: Work order for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2022(to be conferred on 26.11.2022).

Sir,

I am directed to refer to your proposal vide e-mail dated 26.09.2022 on the above subject and convey the approval of the Competent Authority for engagement of services of the Quality Council of India (QCI) for screening of applications received through online national award portal for National Gopal Ratna Award 2022(to be conferred on 26.11.2022) as under:

S No.	Scope of Work/Exercise	No. of Resources/ day	Duration (tentative) in days	Total fees to be paid by DAHD (Amount in Rs.)
1.	Updating evaluation scorecard and checklist for field verification in consultation with DAHD, and developing a detailed roadmap for timely execution of the project.	4	11 th Oct - 20 th Oct 2022 (10 Days)	Rs. 2,04,848/- (Rupees two lakh four thousand eight hundred forty eight only) (Inclusive of GST/all taxes)
2.	Data cleaning of applications received to find unique nominations.			
3.	Analyzing data provided by applicants, verifying claims made in the nominations via secondary research and looking for more relevant information via open search (social media, internet and other source platforms), while making the profiles.			
4.	Scrutinizing and scoring of all the received applications and selecting top 20 applications (as instructed by DAHD) in each of the three categories and handed over to DAHD by 20 th Oct 2022 for field verification.			
5.	Creating detailed profiles for the top 20 applications in each category based on the parameters mentioned in the objective evaluation scorecard and on the basis of factual information collected via field verification by NDDB. To recommend best 20 applications in each category to the Award Screening Committee constituted by DAHD.	7	7 th -9 th Nov,2022 (3 days)	


1 /2...

Cond...

2. If necessary, the time schedule may be reduced with the mutual consent of QCI & DAHD, accordingly, QCI will have to depute more manpower to complete the task within the revised timeframe.
3. The QCI will provide the name of all project team members for the duration of project before the start of the project to enable them entry-pass of DAHD. The undersigned is the nodal officer /contact point for the NGRA 2022.
4. The payment of project fee shall be paid by DAHD as 30% advance and remaining 70% after the satisfactory completion of the project.
5. An agreement between DAHD and QCI regarding terms and condition will be finalized by QCI and signed by DAHD & QCI both.
6. QCI is therefore requested to start the work as mentioned above right from the 11th October 2022.

This issues with the approval of the competent authority and AS&FA vide Dy No. E-23066, Note#20 dated 06.10.2022.

Yours sincerely,


(Ajith Kumar K.)
Assistant Commissioner (DD)
011-23383812
[e-mail : ajith.kk@gov.in]


Copy to:

1. The Joint Commissioner (RGM), DAHD, Krishi Bhawan NEW Delhi –With the request to make 30% advance payment to QCI from RGM head (as per concurrence of AS&FA vide Dy No. E-23066, Note#20 dated 06.10.2022) before the closing date of the applications i.e 10th Oct-2022.
2. PPS to the Additional Secretary (CDD), DAHD

26. QCI's Previous Projects on Nomination Basis with different Ministries

26.1. National Horticulture Board (NHB), Ministry of Agriculture & Farmers Welfare, GoI

Completion Certificate cum Receipt of Payment

 राष्ट्रीय बागवानी बोर्ड National Horticulture Board	 75 आज़ादी का अमृत महोत्सव	राष्ट्रीय बागवानी बोर्ड कृषि एवं किसान कल्याण मंत्रालय, भारत सरकार 85, इन्स्टीट्यूशनल एरिया, गुरुग्राम-122005 National Horticulture Board Ministry of Agriculture & Farmers Welfare, Govt. of India Plot No. 85, Sector-18, Institutional Area, Gurgaon-122015
NHB/CC/QCI/2024-25/ 14555		By <u>Handel</u> March, 27 2025
To, M/s Quality Council of India 2nd Floor, Institution of Engineers Building, 2, Bahadur Shah Zafar Marg New Delhi-110002		
Sub:- Payment of Rs. 62,47,045/- to M/s Quality Council of India, New Delhi for conducting of 3rd Party evaluation for the Schemes of NHB for the years 2019-20 to 2022-23 -Reg.		
Sir, With reference to your letter dated 29.07.2024 regarding QCI's Invoices for the "Third Party Evaluation of the NHB Schemes 1 & 2 for the "FY 2019-20 to 2022-23". In this regard, I am directed to inform that the amount of Rs. 62,47,045/- (Rupees Sixty two lakh forty seven thousand and forty five only) (After deduction TDS@10% Rs. 5,89,344/- and IGST TDS@2% Rs. 1,17,870/-) vide APPA No. C012553145320 dated 01.02.2025 through NEFT/RTGS. Kindly acknowledge the receipt of the same. Thanking you Yours faithfully  (C.P. Gandhi) Joint Director (Coord)		

Work Order of National Horticulture Board (NHB)



राष्ट्रीय बागवानी बोर्ड
National Horticulture Board

राष्ट्रीय बागवानी बोर्ड
कृषि एवं किसान कल्याण मंत्रालय, भारत सरकार
85, इंस्टीट्यूशनल एरिया, सेक्टर-18, गुडगाँव-122015
National Horticulture Board
Ministry of Agriculture & Farmers Welfare, Govt. of India
85, Institutional Area, Sector - 18, Gurgaon - 122015

NHB/HD/CC/QCI/2023-24

To

M/s Quality Council of India
2nd Floor, Institution of Engineers Building,
2, Bahadur Shan Zafar Marg,
New Delhi-110002

November 8, 2023

Subject : Work Award letter for conducting 3rd party evaluation for the schemes of NHB for the years 2019-20 to 2022-23 and also concurrent evaluation of the schemes for the year 2023-24 – reg.

Sir,

Kindly refer to the correspondence held between NHB and QCI on the subject, resting with your email dated 03.08.2023 with a final revised proposal for conducting 3rd party evaluation for the schemes of NHB for the years 2019-20 to 2022-23 and also your email/proposal dated 23.10.2023 for conducting concurrent 3rd party evaluation for the projects funded by NHB during the year 2023-24. Copies of the both the proposals are attached herewith for ready reference.

In this regard, I am directed to convey the approval of competent authority to the following projects for conducting above said 3rd party evaluation:

Project – I : Conducting 3rd party evaluation for the schemes of NHB for the years 2019-20 to 2022-23

Schemes	Total Population	Sample size (at 95% CL and 5% MoE)	Population component
Scheme I	1094	285	Open Field Cultivation, Protected Cultivation, PHM, Primary Processing Units, & Others
Scheme II	127	96	Cold Storage establishment
Total	1221	381	

NHB shall make payment of Rs. 58,93,440/- plus GST for the above assignment as per following details:-

Sl. No.	Activity	Total Cost
1	Professional & Quality Control Cost	₹ 16,65,000.00
2	Assessment Cost	
2.1	Assessment of Scheme- I (285 Projects)	₹ 21,66,389.00

.../-

[Signature]

दूरभाष / Tel. : (0124) - 2347439-42, 2343416-17, 2342989-92, 2343414, 2348313, 2341209, 2341239, 2343348
फैक्स / Fax: (0124) - 2342991, ईमेल / E-mail: md@nhb.gov.in
वेबसाइट / Website: www.nhb.gov.in

2.2	Assessment of Scheme- II (96 Projects)	₹ 12,30,611.00
3	Technology, IT Infrastructure, & Reporting Cost	₹ 2,00,000.00
QCI Admin Cost @12%		₹ 6,31,440.00
Total Project Cost		₹ 58,93,440.00*
		+ Applicable Taxes.

Project – 2 : Conducting concurrent 3rd party evaluation for the schemes of NHB during the year 2023-24, as per following details :

Schemes	Total Population	Sample size (10% of Sanctioned Projects)	Population component
Scheme I	900 (Approx.)	90	1. Open Field Cultivation, 2. Protected Cultivation, 3. PHM, 4. Primary Processing Units, & 5. Others
Scheme II	80 to 100 (Approx.)	8 to 10	1. Cold Storage establishment

NHB shall make payment of Rs. 18,34,924/- plus GST for the above assignment as per following details:-

Sl. No.	Activity	Total Cost
1	Professional & Quality Control Cost	₹ 6,50,000.00
2	Assessment Cost	
2.1	Assessment of Scheme- I (10% of sanctioned projects under scheme I)	₹ 7,60,136.00
2.2	Assessment of Scheme- II 10% of sanctioned projects under scheme II)	₹ 1,28,189.00
3	Technology, IT Infrastructure, & Reporting Cost	₹ 1,00,000.00
QCI Admin Cost @12%		₹ 1,96,599.00
Total Project Cost		₹ 18,34,924.00*
		+ Applicable Taxes

*This amount is exclusive of any taxes and levies.

Handwritten signature

- 3 -

The payment milestones for each of the above projects will be as under:-

Project-1		
Milestones	Stages	Amount to be disbursed
Milestone 1	On Submission of Inception Report	25%
Milestone 2	After completion of 50% of On-Field Assessment	25%
Milestone 3	After completion of 100% of On-Field Assessment	25%
Milestone 4	On Final Submission of Assessment Report	25%
Project-2		
Milestones	Stages	Amount to be disbursed
Milestone 1	After completion of 50% of On-Field Assessment for phase I and Phase II	50%
Milestone 2	On Final Submission of Assessment Report for phase I and Phase II	50%


The other terms and conditions of the contract, scope and objective of third party evaluation, development of framework, training and deployment of Assessors, data quality check, data analysis, reports, deliverables linked to the project timeline etc. will be strictly as per the project proposals submitted by QCI to NHB as attached to this letter.

Further, the QCI will use tech enabled GIS based services to verify the works and provide good quality photographs (Google Map image with location, images of the infrastructure with important component with time and date stamp and a brief mention how the facility has been used in the last three years). QCI

Submission of Report: QCI will submit a detailed report with all kinds of analytics for NHB to enable it to take appropriate decisions. The Enumerator of QCI will also point out any anomaly he/she enumerates in the field and take photographs with time, date and GPS stamp. The final list of selected sites will be as per sampling formulae and should not be changed after that. **QCI will handover the App being used in enumeration of the projects to NHB and it will be a property of NHB.** At least three hard copies of Draft report and Final Report shall be submitted by QCI.

Amendment of Agreement: No amendment or modification of the agreement authorizing this project shall be valid unless it is made in writing jointly by both parties or by their authorized representatives, especially stating the amendments reason to this agreement. The modification/changes shall be effective from the date they are made/executed unless otherwise agreed to.

Force Majeure: The parties shall ensure compliance with the terms of this agreement. However, no party shall be liable for any claim for any loss or damage whatsoever arising out of failure to carry out the terms of the agreement to the extent such a failure is due to force



-4-

majeure events such as fire, rebellion, mutiny, civil commotion, riots, strike, lockout, the force of nature, accident, the of God, or any other reason beyond the control of the concerned party.

Arbitration: The disputes, if arising, shall be settled by arbitration with the sole arbitrator (to be jointly appointed in 30 days) following the procedure prescribed in the Indian Arbitration and Conciliation Act, 1996 or any statutory modification or reenactment thereof and the Rules made thereunder and for the time being in force. Proceedings shall unless otherwise agreed by the parties, be held in Delhi, India. The governing law will be the laws of India. The language will be English.


Termination of Contract : Either party shall have the right to terminate this contract at any time by giving thirty days' notice in writing in advance indicating reasons for the same to the other party. The reasons, however, will need to be justified, and in case the termination leads to delay/pause/abortion of the project, the Authority reserves the right to not make any payments further to the date of project termination as indicated by either party.

Confidentiality:

Both the parties shall maintain confidentially or information and the interaction between them and shall not disclose any relevant confidential information to any third parties. Disclosure of any confidential information by the staff members or agencies hired by any party shall be deemed disclosure of such confidential information by such party, which shall be held liable for breach of this agreement.

You are requested to kindly convey your acceptance to the above said offer of NHB for conducting the third party evaluation for its schemes alongwith its terms and conditions and thereafter, you may start the evaluation work as per miles at the earliest.

Yours sincerely,



(C.P. Gandhi)

Deputy Director (Coord.)

Copy to :

1. Accounts Officer, NHB
2. PS to MD/DMD

26.2. Third-Party Re-Assessment of FCI owned Warehouses Completion Certificate

FCI HQ-S-C012(18)/2/2022-S C

I/614819/2023

तार : 'फूडकोर्प'
 Gram : 'FOODCORP'
 फ़ैक्स नं: एचएफसीआई एन डी
 Fax No.: HFCI ND
 00911123413241
 00911143527433

भारतीय
खाद्य
निगम



FOOD
CORPORATION
OF INDIA

मुख्यालय
नई दिल्ली
Head Quarters
New Delhi

No. FCI HQ-S-C012(18)/2/2022-S C
Signature Date

Date:

Project Completion Certificate

This is to certify that the project titled 'Third Party Reassessment of FCI Owned Warehouses', undertaken by Quality Council of India for the Food Corporation of India as per work order no. FCI HQ-S-C012(18)/1/2022-SC dated 07.12.22, and with total amount of Rs.89,19,120 has been successfully completed in accordance with the agreed-upon terms and specifications within the timeline.

Key Output

- Reassessment of 489 upgraded depots and comparative statement to FCI with original grading and upgraded rating.
- Identification of best practices within the current system. Focus on replicating these practices and implementing necessary reforms.

Submissions by QCI:

- Submission of reports of all 489 warehouses re-assessed.
- A consolidated National Report summarizing the findings and recommendations.

This certificate is issued in recognition of the successful completion of the aforementioned project.

Signed by Ram Babu Meena
 (Ram Babu Meena)
 Date: 05-10-2023 15:56:10
 Asstt. Genl. Manager (S&C)
 Reason: Approved

Work Order

I/24498/2022

FCI HQ-S-C012(18)/1/2022-S C**Dated: 07.12.2022**

The Secretary General,
Quality Council of India,
Bahadur Shah Zafar-Marg, New Delhi

Sub: Third party re-assessment of FCI owned warehouses-reg.**Ref:**

1. MOU between QCI and FCI dated 24.03.2021 concerning transformation of FCI.
2. This Office letter of even no. 68756/2022/S&C-HQ dated 03.10.22 and 18.11.22
3. QCI Proposal for re-validation of 492 FCI owned depots dated 27.11.22.

Sir,

A Memorandum of Understanding (MOU) was signed on 24.03.2021 between FCI and QCI with the objective of taking up projects for transformation of FCI. Following clauses are part of the MOU:-

4.1.a.i - Review current standards and guidelines and benchmark them to global best practices and international standards and suggest relevant changes, whenever required, to be implemented immediately.

4.1.e.i - Third party audit of complete value chain, including stages of procurement and distribution for a period of 5 years or mutually agreed time period to monitor and standardize the processes based on mutually agreed audit plans conducted through professionally qualified experts engaged through a transparent process of price discovery.

In pursuance to the above MoU, work order was issued to QCI vide this office letter no E.1(1)/QCI/2021/Stg VIII, dated: 12.08.2021. QCI submitted its final report to FCI in the month of July 2022 and accordingly improvements were made in all the FCI owned depots. FCI Regional / Zonal offices have reported that 492 depots have been up-graded to 4 Star, 5 Star and Excellent Category.

It is directed by DFPD to get all the FCI owned depots re-validated from QCI, that have been up-graded to 4 Star, 5 Star and Excellent Category. Accordingly, QCI was requested vide this office letter of even no. dated 03.10.22 and 18.11.22 to submit proposal for the same. Subsequently, QCI submitted the proposal on 27.11.22.

The proposal dated 27.11.22 has been examined and the Competent Authority has accorded approval for undertaking Third party re-assessment of 492 warehouses (FCI owned) at the estimated cost of Rs 92,94,880/- (Ninety two lakhs ninety four thousand eight hundred and eighty only) excluding taxes, to be carried out by professionally qualified experts engaged through a transparent process of price discovery. Following shall be the Terms and Conditions:

Scope of Work:

The parameters as stated at Annexure-I & II of the QCI proposal dated

I/24498/2022

27.11.2022, which are attached herewith, shall be covered under the third party assessment. QCI will capture information of the up-graded depots in the same format as was done for the original assessment. The marking scheme shall also remain the same.

Exercise is to be undertaken for all the 492 FCI Owned up-graded warehouses across Pan-India. List enclosed.

Key Output:

- All 492 up-graded depots will be reassessed with respect to original grading and up-graded rating. The comparative statement be submitted to FCI.
- Best practices within the current system for replication with a focus on reforms required for improving the performances/ efficient utilization of warehousing space.
- Action plan for improving the performance to international best practices.

Payment:

The proposal dated 27.11.2022 has been worked out on the basis of 492 warehouses for which estimated cost worked out is Rs 92,94,880/- (Ninety two lakhs ninety four thousand eight hundred and eighty only). The proposal of QCI has fixed and variable cost. The fixed cost shall remain the same and the variable cost will vary based on number of man days (fixed as per capacity) which is based on actual number of depots inspected. It is clarified that the extra cost on account of change in technology during the assessment shall not be payable to QCI.

The actual payment shall be made as per criteria provided in the QCI proposal and the number of warehouses covered during the exercise. The Schedule of Payment shall be as under:

Sl.	Schedule / Milestones	Percentage (%) of Contract Value
1	Award of Work Order	10%
2	Submission and acceptance of final Report	90%

The QCI will raise all the claim bills in FCI Hqrs. The storage Division shall collect the details from Regions and process the same accordingly. Certificate of GM (Region) regarding number of man days utilized (not exceeding the ceiling) will be the basis of regulating the final payment. The Zonal Offices shall compile data on submission of draft report of Regions under their jurisdiction and submit the same to FCI, Hqrs. (the Storage Division, FCI, Hqrs. will seek and compile such information for the purpose of processing the claim).

It shall be made clear that no additional claim on whatsoever, ground for any other payment/re-imbursement of expenditure on other account would be entertained.

Timeline:

- The timeline for completing the said work is 2 Months which commences from the date of receipt of Work Order from this office.
- In case, QCI fails to submit the reports (complete in all respect)

I/24498/2022

within 60 days (including all the holidays) from the date of issue of work order from this office, Liquidated damages will be applicable for delay based on the number of days by which the submission of report is delayed (10% of sub-total, as mentioned under the head "7. Financials" i.e. Rs. 82,99,000/- for every 15 days and part thereof).

2. In case of delay in completion of study for the reasons beyond the control of the party, suitable extension of the time shall be considered at the sole discretion of FCI.

Submission of Report: At least three hard copies each of Draft and Final Report shall be submitted by QCI.

Amendment of Agreement: No amendment or modification of the agreement authorizing this project shall be valid unless it is made in writing jointly by both parties or by their authorized representatives, especially stating the amendment's reason to this agreement. The modification/changes shall be effective from the date they are made/executed unless otherwise agreed to.

Force Majeure:

The parties shall ensure compliance with the terms of this agreement. However, no party shall be liable for any claim for any loss or damage whatsoever arising out of failure to carry out the terms of the agreement to the extent such a failure is due to force majeure events such as fire, rebellion, mutiny, civil commotion, riots, strike, lockout, the force of nature, accident, the act of God, or any other reason beyond the control of the concerned party.

Arbitration:

The disputes, if arising, shall be settled by arbitration with the sole arbitrator (to be jointly appointed in 30 days) following the procedure prescribed in the Indian Arbitration and Conciliation Act, 1996 or any statutory modification or reenactment thereof and the Rules made thereunder and for the time being in force. Proceedings shall unless otherwise agreed by the parties, be held in Delhi, India. The governing law will be the laws of India. The language will be English.

Notice:

All notices permitted or required to be given under the provisions of this agreement shall be deemed to be sufficiently given if written and delivered personally or sent to the other party by telefax or certified or registered airmail or email and addressed to the registered office of the other party as follows or to such other party address as the party may give notice in writing.

Unless otherwise provided herein, all such notices shall be deemed to have been given as of the date they are personally delivered or transmitted by telefax or email or deposited in the mail.

Termination of agreement:

Either party shall have the right to terminate the agreement at any time by giving thirty days' notice in writing in advance indicating reasons for the same to the other party. The reasons, however, will need to be justified, and

I/24498/2022

in case the termination leads to delay/pause/abortion of the project, the Authority reserves the right to not make any payments further to the date of project termination as indicated by either party.

Confidentiality:

Both the parties shall maintain confidentiality of information and the interaction between them and shall not disclose any relevant confidential information to any third party. Disclosure of any confidential information by the staff members or agencies hired by any Party shall be deemed disclosure of such confidential information by such Party, which shall be held liable for breach of this Agreement.

Formal acceptance of the work order and its terms and conditions may be communicated to FCI immediately.

Yours Faithfully

Signed by Alok Kumar Uday
Bhanu Singh

Dy. General Manager (FCI)
Date: 06-12-2022 13:23:43
Reason: Approved

Attachment: List of 492 depots.

Copy to:

1. Secretary (DFPD), MoCAF&PD Krishi Bhawan, New Delhi... for information.
2. PA to C&MD, FCI Hqrs., New Delhi... for information.
3. General Manager (PI Cell/ QCI/ Purchase) FCI Hqrs., New Delhi... for information.
4. ED (Zone), Zonal offices (North, East, West, South, NE)... for information.
5. General Manager (All FCI Regions).... for information.
6. Board Cell, FCI Hqrs., New Delhi... for information.

26.3. Third-Party Assessment of Procurement Centers in KMS 2021-22 & RMS 2022-23

Completion Certificate

FCI HQ-Proc021/5/2023-PROC

I/1390490/2024

Project Completion Certificate

This is to certify that the project titled **Third Party Assessment of Procurement Centers in KMS 2021-22 and RMS 2022-23**, undertaken by Quality Council of India for the Food Corporation of India as per work order no. **Proc. I/1(1)/2021/QCI** dated **10.12.2021**, has been successfully completed in accordance with the agreed-upon terms and specifications.

Key Output:

- Analysis report on the current infrastructural facilities available at the procurement center.
- Comprehensive assessment report on activities performed at procurement centers from observations and data analysis.
- Feedback from farmers and other stakeholders.
- Data of grain analyzed (defining the moisture contents, physical parameters) at which they were procured.

Submissions by QCI:

- Submission of reports for 23 states involved in the project.
- A consolidated National Report summarizing the findings and recommendations.
- Provision of a link to access the Procurement Dashboard.

This certificate is issued in recognition of the successful completion of the aforementioned project.

Signed by
Sanjay Pathy
Date: 31-07-2024 14:52:07
Asstt. Genl. Manager(Procurement)

No: FCI HQ-Proc021/5/2023-PROC(154270) Dated: 31-07-2024

re it is once again rem-
 a. Scientific and Conserv-
 1967 1968
 1969 1970
 1971 1972
 1973 1974
 1975 1976
 1977 1978
 1979 1980
 1981 1982
 1983 1984
 1985 1986
 1987 1988
 1989 1990
 1991 1992
 1993 1994
 1995 1996
 1997 1998
 1999 2000
 2001 2002
 2003 2004
 2005 2006
 2007 2008
 2009 2010
 2011 2012
 2013 2014
 2015 2016
 2017 2018
 2019 2020
 2021 2022
 2023 2024
 2025 2026
 2027 2028
 2029 2030
 2031 2032
 2033 2034
 2035 2036
 2037 2038
 2039 2040
 2041 2042
 2043 2044
 2045 2046
 2047 2048
 2049 2050
 2051 2052
 2053 2054
 2055 2056
 2057 2058
 2059 2060
 2061 2062
 2063 2064
 2065 2066
 2067 2068
 2069 2070
 2071 2072
 2073 2074
 2075 2076
 2077 2078
 2079 2080
 2081 2082
 2083 2084
 2085 2086
 2087 2088
 2089 2090
 2091 2092
 2093 2094
 2095 2096
 2097 2098
 2099 2100
 2101 2102
 2103 2104
 2105 2106
 2107 2108
 2109 2110
 2111 2112
 2113 2114
 2115 2116
 2117 2118
 2119 2120
 2121 2122
 2123 2124
 2125 2126
 2127 2128
 2129 2130
 2131 2132
 2133 2134
 2135 2136
 2137 2138
 2139 2140
 2141 2142
 2143 2144
 2145 2146
 2147 2148
 2149 2150
 2151 2152
 2153 2154
 2155 2156
 2157 2158
 2159 2160
 2161 2162
 2163 2164
 2165 2166
 2167 2168
 2169 2170
 2171 2172
 2173 2174
 2175 2176
 2177 2178
 2179 2180
 2181 2182
 2183 2184
 2185 2186
 2187 2188
 2189 2190
 2191 2192
 2193 2194
 2195 2196
 2197 2198
 2199 2200
 2201 2202
 2203 2204
 2205 2206
 2207 2208
 2209 2210
 2211 2212
 2213 2214
 2215 2216
 2217 2218
 2219 2220
 2221 2222
 2223 2224
 2225 2226
 2227 2228
 2229 2230
 2231 2232
 2233 2234
 2235 2236
 2237 2238
 2239 2240
 2241 2242
 2243 2244
 2245 2246
 2247 2248
 2249 2250
 2251 2252
 2253 2254
 2255 2256
 2257 2258
 2259 2260
 2261 2262
 2263 2264
 2265 2266
 2267 2268
 2269 2270
 2271 2272
 2273 2274
 2275 2276
 2277 2278
 2279 2280
 2281 2282
 2283 2284
 2285 2286
 2287 2288
 2289 2290
 2291 2292
 2293 2294
 2295 2296
 2297 2298
 2299 2300
 2301 2302
 2303 2304
 2305 2306
 2307 2308
 2309 2310
 2311 2312
 2313 2314
 2315 2316
 2317 2318
 2319 2320
 2321 2322
 2323 2324
 2325 2326
 2327 2328
 2329 2330
 2331 2332
 2333 2334
 2335 2336
 2337 2338
 2339 2340
 2341 2342
 2343 2344
 2345 2346
 2347 2348
 2349 2350
 2351 2352
 2353 2354
 2355 2356
 2357 2358
 2359 2360
 2361 2362
 2363 2364
 2365 2366
 2367 2368
 2369 2370
 2371 2372
 2373 2374
 2375 2376
 2377 2378
 2379 2380
 2381 2382
 2383 2384
 2385 2386
 2387 2388
 2389 2390
 2391 2392
 2393 2394
 2395 2396
 2397 2398
 2399 2400
 2401 2402
 2403 2404
 2405 2406
 2407 2408
 2409 2410
 2411 2412
 2413 2414
 2415 2416
 2417 2418
 2419 2420
 2421 2422
 2423 2424
 2425 2426
 2427 2428
 2429 2430
 2431 2432
 2433 2434
 2435 2436
 2437 2438
 2439 2440
 2441 2442
 2443 2444
 2445 2446
 2447 2448
 2449 2450
 2451 2452
 2453 2454
 2455 2456
 2457 2458
 2459 2460
 2461 2462
 2463 2464
 2465 2466
 2467 2468
 2469 2470
 2471 2472
 2473 2474
 2475 2476
 2477 2478
 2479 2480
 2481 2482
 2483 2484
 2485 2486
 2487 2488
 2489 2490
 2491 2492
 2493 2494
 2495 2496
 2497 2498
 2499 2500
 2501 2502
 2503 2504
 2505 2506
 2507 2508
 2509 2510
 2511 2512
 2513 2514
 2515 2516
 2517 2518
 2519 2520
 2521 2522
 2523 2524
 2525 2526
 2527 2528
 2529 2530
 2531 2532
 2533 2534
 2535 2536
 2537 2538
 2539 2540
 2541 2542
 2543 2544
 2545 2546
 2547 254

Dated: 10.12.2021

Ref: QCI proposal for Third party assessment Procurement Centers dated 17.11.2021.

A Memorandum of Understanding (MOU) was signed on 25.03.2021 between FCI and QCI with the objective of taking up projects for transformation of FCI. Following clauses are part of the MOU:-

- 4.1.a.i - Review current standards and guidelines and benchmark them to global best practices and international standards and suggest relevant changes, wherever required, to be implemented immediately.
- 4.1.e.i - Third party audit of complete value chain, including stages of procurement and distribution for a period of 5 years or mutually agreed time period to monitor and standardize the processes based on mutually agreed audit plans conducted through professionally qualified experts engaged through a transparent process of price discovery.

In Pursuance to the above, proposal was received from QCI vide e-mail dated 17.11.2021 for conducting a Third-Party Assessment of Procurement centers based on indicative parameters as per **Annexure I** to IV of the proposal. The proposal has been examined and the Competent Authority has accorded in-principle approval for proposal submitted by QCI for undertaking third party assessment of procurement centers to be carried out by professionally qualified experts, engaged through a transparent process of price discovery, over 8 months. Following shall be the Terms and Conditions:

Scope of Work:

The parameters as stated in the QCI proposal dated 17.11.2021, which are attached herewith, shall be covered under the third-party assessment.

Third party assessment is to be carried out in 434 purchase centers as per the state wise list attached as Annexure I, over 8 months covering both Kharif Marketing Season and Rabi Marketing Season.

- a) Assessment of infrastructural facilities at the procurement centre.
- b) Comprehensive assessment of activities performed in procurement centres vis-à-vis standard operating procedures.
- c) Detailed feedback from farmers and other stake holders.
- d) Random assessment of quality of grain procured.



Key Output:

- Analysis report on the current infrastructural facilities available at the procurement center.
- Comprehensive assessment report on activities performed at procurement centers from observations and data analysis.
- Feedback from farmers and other stakeholders.
- Data of grain analyzed (defining the moisture contents, physical parameters) at which they were procured.

Following outcomes anticipated from the exercise

- Identification of necessary areas for intervention for bridging gaps and curation of technology interventions in procurement operations
- Identification of good practices which can be replicated and ideation of prototype of a modern grain procurement centre
- Identification of current practices and gaps between policies and implementation
- Identification of concerns and pain points of stakeholders at the time of procurement.
- Assessment of the quality of grain being procured.

Costing and Payment:

The financial proposal submitted in the proposal in respect of 3 items are hereby approved as under:

- | | |
|---------------------------------------|---|
| 1. A.1 QCI Professionals * | : Rs. 2,30,40,000/- |
| (36 Professionals X 80,000/Month X 8) | |
| 2. Logistics and Travel Cost | : Rs. 98,82,000/- |
| 3. Administrative Cost @ 12% * | : On actuals, based on total cost of project. |

* Final payment shall be made based on utilization Certificate alongwith particulars of personnel engaged for the project.

For all other items of cost mentioned in the proposal, approval is hereby conveyed subject to the condition that QCI shall follow the procedure as mentioned in Annexure V of the proposal and ensure proper price discovery. The final cost payable for each of these items will be the discovered price with the upper ceiling of the unit prices mentioned in the Clause 6 (Financials) of the proposal, after due verification of relevant documents.

The proposal of QCI has elements of fixed and variable costs. The fixed cost shall remain the same and the variable cost will vary based on number of man days actually consumed. It is clarified that the extra cost on account of change in technology or any other factor during the assessment shall not be payable. Further, taxes on the above mentioned cost will be levied as applicable.

The actual payment shall be made as per criteria provided in the QCI proposal and the number of purchase centers covered during the exercise. The Schedule of Payment shall be as under:





Sl.	Schedule / Milestones	Percentage (%) of Contract Value
1	Award of Work Order	10%
2	End of Assessment and submission of Draft report	60%
3	Submission and acceptance of final Report	30%

The QCI will raise all the claim bills in FCI Hqrs. The Procurement Division shall collect the details from regions and process the same accordingly. Certificate of GM (Region) regarding number of purchase centers covered (not exceeding the ceiling) will be the basis of regulating the final payment. The Procurement Division FCI Hqrs will seek and compile such information for purpose of processing the claim.

It shall be made clear that no additional claim on whatsoever ground for any other payment/reimbursement of expenditure on any other account would be entertained.

The formats and the Questionnaires for conducting the study shall be formulated in consultation with FCI, Hqrs.


Time line:

1. The timeline for completing the said work is 8 (Eight) months which commences from the date of receipt of Work Order by QCI.
2. In case of delay in completion of study for the reasons beyond the control of the party, suitable extension of the time shall be considered at the sole discretion of FCI.

Submission of Report: At least three hard copies of Draft report and Final Report shall be submitted by QCI. The draft reports may be discussed with the respective regional GMs before submission to HQ.

Amendment of Agreement: No amendment or modification of the agreement authorizing this project shall be valid unless it is made in writing jointly by both parties or by their authorized representatives, especially stating the amendment's reason to this agreement. The modification/changes shall be effective from the date they are made/executed unless otherwise agreed to.

Force Majeure: The parties shall ensure compliance with the terms of this agreement. However, no party shall be liable for any claim for any loss or damage whatsoever arising out of failure to carry out the terms of the agreement to the extent such a failure is due to force majeure events such as fire, rebellion, mutiny, civil commotion, riots, strike, lockout, the force of nature, accident, the act of God, or any other reason beyond the control of the concerned party.



26.4. Third-Party Assessment of FCI Warehouses Completion Certificate

FCI HQ-S-C012(18)/2/2022-S C

I/631663/2023

तार : 'फूडकोर्प'
 Gram : 'FOODCORP'
 फ़ैक्स नं: एचएफसीआई एन डी
 Fax No.: HFCI ND
 00911123413241
 00911143527433

भारतीय
 खाद्य
 निगम


 FOOD
 CORPORATION
 OF INDIA

मुख्यालय
 नई दिल्ली
 Head Quarters
 New Delhi

16-20, बाराकम्बा लेन, नई दिल्ली - 110001, दूरभाष: 011- 43527697, 43527698
 16-20, BARAKHAMBA LANE, NEW DELHI - 110001, PHONE: 011-43527697, 43527698

No. FCI HQ-S-C012(18)/2/2022-S C
Signature Date

Date:

Project Completion Certificate

This is to certify that the project titled 'Third Party Assessment of FCI Warehouses', undertaken by Quality Council of India for the Food Corporation of India as per work order no. **E.1(1)/QCI/2021/Stg VIII** dated **12.08.21**, and with a total amount of Rs.2,29,77,360 has been successfully completed in accordance with the agreed-upon terms and specifications within the timeline.

Key Output

- Report cards for each warehouse with specific grades based on predefined parameters.
- Finalization of draft report in consultation with the concerned GM(Region).
- Identify best practices within the current system for potential replication.
- Focus on reforms needed to improve warehouse performance and space utilization.
- Develop a plan for aligning with international best practices in warehousing.

Submissions by QCI:

- Submission of individual reports for all 2,147 assessed warehouses.
- Submission of reports covering all 26 Regions in the project.
- A consolidated National Report providing a summary of findings and recommendations.
- Ownership-specific reports categorized by FCI, CWC, SWC, PEG Owned, Private Owned, and PWS Owned warehouses.
- Provision of a link to access the Warehouse Dashboard.

This certificate is issued in recognition of the successful completion of the aforementioned project.

Signed by Ram Babu Meena
 (Ram Babu Meena)
 Asstt. Genl. Manager (S&C)
 Date: 11-10-2023 09:55:43
 Reason: Approved

Work Order

नाम : 'फूडकॉर्पोरेशन'
 Group : 'FOODCORP'
 पंजीकृत नं : एचएफसीआई एनडी
 Fax No : HFCEI ND
 00911123413241
 00911123413103

भारतीय खाद्य निगम
 FOOD CORPORATION OF INDIA
 आइट-एच-ओ 9001:2000 प्रमाणित
 16-20, बाराकम्बा लाने, नई दिल्ली - 110001, फ़ोन : 011-23413271, 23414872, 23414873, 23414874
 16-20, BARAKAMBA LANE, NEW DELHI-110001. PHONE : 011-23413271, 23414872, 23414873, 23414874

मुख्यालय
 110001 दिल्ली
 Head Quarters
 New Delhi

No. E.1(1)/QCI/2021/Stg VIII

Dated: 12.08.2021

The Secretary General,
 Quality Council of India,
 Bhadur Shah Zafar-Marg, New Delhi

Sub: Third party assessment of FCI warehouses-reg.

Ref: QCI proposal for Third party assessment of FCI (Own & Hired) warehouses dtd 23.07.2021.

Sir,

A Memorandum of Understanding (MOU) was signed on 25.03.2021 between FCI and QCI with the objective of taking up projects for transformation of FCI. Following clauses are part of the MOU:-

- 4.1.a.i - Review current standards and guidelines and benchmark them to global best practices and international standards and suggest relevant changes, wherever required, to be implemented immediately.
- 4.1.e.i - Third party audit of complete value chain, including stages of procurement and distribution for a period of 5 years or mutually agreed time period to monitor and standardize the processes based on mutually agreed audit plans conducted through professionally qualified experts engaged through a transparent process of price discovery.

In Pursuance to the above, proposal was received from QCI vide e-mail dated 23.07.2021 for conducting a Third Party Assessment of FCI warehouses based on framework parameters. The proposal has been examined and the competent authority has accorded in-principle approval for proposal submitted by QCI for undertaking Third party assessment of warehouses (FCI owned and hired) at the estimated cost of Rs 2,39,89,840/- (Two Crore Thirty-Nine Lakhs Eighty-Nine Thousand Eight Hundred Forty only) to be carried out by professionally qualified experts engaged through a transparent process of price discovery. Following shall be the Terms and Conditions:

Scope of Work:

The parameters as stated at Annexure-I & II of the QCI proposal dated 23.07.2021, which are attached herewith, shall be covered under the third party assessment.

Exercise is to be undertaken for all the warehouses with FCI (both owned & hired) across Pan-India. Since the number of depots is a dynamic figure and varies from month to month due to hiring and de-hiring of godowns, QCI may undertake the exercise for actual number of godowns as available during the audit period. As on 30.06.2021, total number of godowns was 2323.

Key Output:

- A report card for each warehouse against current SoPs with specific grading prepared based on pre-defined parameters (Annexure I & II). The draft report will be finalized in consultation with concerned GM(Region).
- Best practices within the current system for replication with a focus on reforms required for improving the performances/ efficient utilization of warehousing space.
- Action plan for improving the performance to international best practices.



Page 1/3

नाम : 'फूडकोर्प'
 Gram : 'FOODCORP'
 क्षेत्र : 'एकलक्षित' (एकलक्षित)
 Fax No. : HFCI ND
 00911123413241
 00911123413103

भारतीय खाद्य निगम
 FOOD CORPORATION OF INDIA
 315-एफ-30- 0001-2000 एमएल
 15-20, बाराहम्बा लाने, न्यू देली-110011, फोन : 011-23413871, 23413872, 23413873
 15-20, BARAHAMBA LANE, NEW DELHI-110011, PHONE : 011-23413871, 23413872, 4880

मुख्यालय
 नई दिल्ली
 Head Quarters
 New Delhi

Payment:

The proposal dated 23.07.2021 has been worked out on the basis of 2272 warehouses for which estimated cost worked out is Rs 2,39,89,840/- (Two Crore Thirty-Nine Lakhs Eighty-Nine Thousand Eight Hundred Forty only). The proposal of QCI has elements of fixed and variable cost. The fixed cost shall remain same and the variable cost will vary based on number of man days (fixed as per capacity) which is based on actual number of depots inspected. It is clarified that the extra cost on account of change in technology during the assessment shall not be payable to QCI.

The actual payment shall be made as per criteria provided in the QCI proposal and the number of warehouses covered during the exercise. The Schedule of Payment shall be as under:

Sl.	Schedule / Milestones	Percentage (%) of Contract Value
1	Award of Work Order	10%
2	End of Assessment and submission of Draft report	60%
3	Submission and acceptance of final Report	30%

The QCI will raise all the claim bills in FCI Hqrs. The Storage Division shall collect the details from Regions and process the same accordingly. Certificate of GM (Region) regarding number of mandays utilized (not exceeding the ceiling) will be the basis of regulating of the final payment. The Zonal Offices shall compile data of submission of draft reports of Regions under their jurisdiction and submit the same to FCI Hqrs (The Storage Division FCI Hqrs will seek and compile such Information for purpose of processing the claim).

It shall be made clear that no additional claim on whatsoever ground for any other payment/reimbursement of expenditure on any other account would be entertained.

Time line:

1. The timeline for completing the said work is 8 (Eight) weeks which commences from the date of receipt of Work Order from this office.
2. In case of delay in completion of study for the reasons beyond the control of the party, suitable extension of the time shall be considered at the sole discretion of FCI.

Submission of Report: At least three hard copies of Draft report and Final Report shall be submitted by QCI.

Amendment of Agreement: No amendment or modification of the agreement authorizing this project shall be valid unless it is made in writing jointly by both parties or by their authorized representatives, especially stating the amendment's reason to this agreement. The modification/changes shall be effective from the date they are made/executed unless otherwise agreed to.

Force Majeure: The parties shall ensure compliance with the terms of this agreement. However, no party shall be liable for any claim for any loss or damage whatsoever arising out of failure to carry out the terms of the agreement to the extent such a failure is due to force majeure events



Page 2/3

भारतीय खाद्य निगम
 Grain : FOODCORP
 किराने व उपसाधन विभाग
 Fax No. : HFCE ND
 00011123413241
 00011123413103

भारतीय खाद्य निगम
 FOOD CORPORATION OF INDIA
 315-271-30-00012000 ग्राहक
 10-20, मणिकपुर रोड, नई दिल्ली - 110011, फोन : 011-2341071, 2341072, 2341080
 10-20, MANIKPUR ROAD, NEW DELHI-110011, PHONE : 011-2341071, 2341072, 2341080

मुख्यालय
 Hq. Delhi
 Head Quarters
 New Delhi

such as fire, rebellion, mutiny, civil commotion, riots, strike, lockout, the force of nature, accident, the act of God, or any other reason beyond the control of the concerned party.

Arbitration: The disputes, if arising, shall be settled by arbitration with the sole arbitrator (to be jointly appointed in 30 days) following the procedure prescribed in the Indian Arbitration and Conciliation Act, 1996 or any statutory modification or reenactment thereof and the Rules made thereunder and for the time being in force. Proceedings shall unless otherwise agreed by the parties, be held in Delhi, India. The governing law will be the laws of India. The language will be English.

Notice: All notices permitted or required to be given under the provisions of this agreement shall be deemed to be sufficiently given if written and delivered personally or sent to the other party by telefax or certified or registered airmail or email and addressed to the registered office of the other party as follows or to such other party address as the party may give notice in writing.

Unless otherwise provided herein, all such notices shall be deemed to have been given as of the date they are personally delivered or transmitted by telefax or email or deposited in the mail.

Termination of agreement: Either party shall have the right to terminate the agreement at any time by giving thirty days' notice in writing in advance indicating reasons for the same to the other party. The reasons, however, will need to be justified, and in case the termination leads to delay/pause/abortion of the project, the Authority reserves the right to not make any payments further to the date of project termination as indicated by either party.

Confidentiality

Both the parties shall maintain confidentiality of information and the interaction between them and shall not disclose any relevant confidential information to any third parties. Disclosure of any confidential information by the staff members or agencies hired by any Party shall be deemed disclosure of such confidential information by such Party, which shall be held liable for breach of this Agreement.

Formal acceptance of the work order and its terms and conditions may be communicated to FCI immediately.

This issues with the approval of CMD.

Yours Faithfully


 (Vinod Kumar)

Dy. General Manager (S&C)

Copy to:

1. Secretary(DFPD), MoCAF&PD Krishi Bhawan, New Delhi.....for information.
2. PA to CMD, FCI Hqrs. New Delhi.....for information.
3. General Manager (PI-Cell)/General Manager(QCI/Purchase), FCI Hqrs. New Delhi.....for information.
4. Board Cell, FCI Hqrs. New Delhi....for information.


 Dy. General Manager (S&C)

Page 3/3

26.5. Audit Assessment and Issuance of Warehouse rating for CWC warehouses on warehouse management practices, safety standards and infrastructure including the audit from point of improvement in efficiency and new initiatives.

Completion Certificate



केन्द्रीय भण्डारण निगम
(भारत सरकार का उपक्रम)
CENTRAL WAREHOUSING CORPORATION
(A Govt. of India Undertaking)
जन-जन के लिए भण्डारण/Warehousing for Everyone



क्रमांक: CWC-CO-QS0QS/6/2023-24/ **दिनांक: 23.07.2024**

TO WHOM IT MAY CONCERN

This is to certify that work cited below was awarded to M/s Quality Council of India, 2nd Floor, Institution of Engineers Building, Bahadur Shah Zafar Marg, New Delhi-11002. They have completed the work as per details given below: -

यह प्रमाणित किया जाता है कि नीचे उल्लिखित कार्य मेसर्स क्वालिटी काउंसिल ऑफ इंडिया, द्वितीय तल, इंस्टीट्यूशन ऑफ इंजीनियर्स बिल्डिंग, बहादुर शाह जफर मार्ग, नई दिल्ली-11002 को सौंपा गया था। उन्होंने नीचे दिए गए विवरण के अनुसार कार्य पूरा कर लिया है: -

1.	Name of work कार्य का नाम	Audit, assessment and issuance of Warehouse ratings for CWC Warehouses on warehouse management practice, safety standards and infrastructure including the audit from point of improvement in efficiency and new initiatives. गोदाम प्रबंधन पद्धति, सुरक्षा मानकों और बुनियादी ढांचे पर सीडब्ल्यूसी गोदामों के लिए गोदाम रेटिंग का लेखा-परीक्षण, मूल्यांकन और जारी करना, साथ ही दक्षता में सुधार और नई पहलों के दृष्टिकोण से भी लेखा-परीक्षण करना।
2.	Letter of Acceptance No. स्वीकृति पत्र सं.	CWC-CO-QS0QS/6/2022/2022-23 Dt. 27.02.2023
3.	Total contract period कुल अनुबंध अवधि	03 Years 03 वर्ष
4.	Scope of Service सेवा का दायरा	a) To develop in consultation with CWC the framework consisting the audit parameters for evaluation and award of star rating based on CWC operations in warehouses, CFS, ICDs and rail linked terminals. b) To conduct audit, assess and evaluate CWC warehouses for release of Warehouse ratings on warehouse management practice, safety standards and infrastructure based on mutually accepted parameters including the audit from the point of improvement in efficiency and new initiatives. c) To submit a report card evident with photographic views for each warehouse with specific grading (marking), area of improvement required, good practices followed and award the star ratings.

कॉर्पोरेट कार्यालय: 4/1, सिरि इंस्टीट्यूशनल एरिया, अगस्त क्रांति मार्ग, हाउस खस, नई दिल्ली -110016, दूरभाष -011-49857894
Corporate Office: 4/1, Siri Institutional Area, August Kranti Marg, Hauz Khas, New Delhi-110016, Tel.Off-011-49857894
Telefax : 011-49857894, E-mail: head.ens@cewacor.nic.in, website : www.cewacor.nic.in




केन्द्रीय भण्डारण निगम
 (भारत सरकार का उपक्रम)
CENTRAL WAREHOUSING CORPORATION
 (A Govt. of India Undertaking)
जन-जन के लिए भण्डारण/Warehousing for Everyone



		क) सीडब्ल्यूसी के परामर्श से गोदामों, सीएफएस, आईसीडी और रेल लिंकड टर्मिनलों में सीडब्ल्यूसी संचालन के आधार पर मूल्यांकन और स्टार रेटिंग प्रदान करने के लिए लेखापरीक्षा मापदंडों से युक्त रूपरेखा विकसित करना। ख) दक्षता में सुधार और नई पहलों के दृष्टिकोण से लेखापरीक्षा सहित पारस्परिक रूप से स्वीकृत मापदंडों के आधार पर गोदाम प्रबंधन अभ्यास, सुरक्षा मानकों और बुनियादी ढांचे पर वेयरहाउस रेटिंग जारी करने के लिए सीडब्ल्यूसी गोदामों का लेखापरीक्षा, आकलन और मूल्यांकन करना। ग) प्रत्येक गोदाम के लिए विशिष्ट ग्रेडिंग (मार्किंग), आवश्यक सुधार के क्षेत्र, अपनाई गई अच्छी कार्यप्रणाली के साथ फोटोग्राफिक दृश्यों के साथ एक रिपोर्ट कार्ड प्रस्तुत करना और स्टार रेटिंग प्रदान करना।
5.	Actual Work done Amount under 1 st Iteration प्रथम पुनरावृत्ति के अंतर्गत वास्तविक कार्य की मात्रा	Rs. 80,29,994.00 (Rupees Eighty Lakh Twenty-Nine Thousand Nine Hundred Ninety-Four Only) रु. 80,29,994.00 (रुपये अस्सी लाख उनतीस हजार नौ सौ चौरानबे मात्र)
6.	Status of completion of Work कार्य पूर्ण होने की स्थिति	Audit and rating of 376 Nos. of warehouses completed. 376 गोदामों का ऑडिट और रेटिंग पूरा हो गया।

The certificate is issued at the request of M/s Quality Council of India for tendering purposes only.
यह प्रमाण-पत्र केवल निविदा प्रयोजन हेतु मेसर्स क्वालिटी काउंसिल ऑफ इंडिया के अनुरोध पर जारी किया गया है।



Digitally signed by
Roopendra Kumar Sharma
Date: 2024.07.23 10:57:19
+05'30'

(Roopendra Kumar Sharma)
Chief Engineer
Central Warehousing Corporation
मुख्य अभियंता
केंद्रीय भण्डारण निगम

कॉर्पोरेट कार्यालय: 4/1, सिरि इंस्टीट्यूशनल एरिया, अगस्त क्रान्ति मार्ग, हाउज खास, नई दिल्ली -110016, दूरभाष -011-49857894
 Corporate Office: 4/1, Siri Institutional Area, August Kranti Marg, Hauz Khas, New Delhi-110016, Tel.Off-011-49857894
 Telefax : 011-49857894, E-mail: hod.enge@cewacor.nic.in, website : www.cewacor.nic.in

26.6. Mid-Term Evaluation of Deendayal Antyodaya Yojana- National Urban Livelihood Mission (NULM).

Completion Certificate

K-12011(11)/29/2017-UPA III SECTION (E-3146172)

Government of India
Ministry of Housing & Urban Affairs

Nirman Bhawan, New Delhi
Dated the 23rd June, 2022

PROJECT COMPLETION CERTIFICATE

Project Name: "Mid-term evaluation of Deendayal Antyodaya Yojana- National Urban Livelihoods Mission"

This is to certify that M/s Quality Council of India(QCI) has satisfactorily completed the assessment, verification tasks and documentation work in accordance to Contract No. IN-DL50809353038608P related to **"Mid-Term Evaluation of Deendayal Antyodaya Yojana-National Urban Livelihoods Mission"**.

We appreciate the efforts put in by M/s QCI for successfully completing the project.



(Balachandran B.S.)
Under Secretary to the Government of India
Ministry of Housing and Urban Affairs
Nirman Bhawan, New Delhi-110011

काव्यत री. एल.ए. BALACHANDRAN B. S.
अधर सचिव/Under Secretary
आवासन और कस्बरी कार्य मंत्रालय
Ministry of Housing and Urban Affairs
एनर शासन/Govt of India
निर्मण भवन, नई दिल्ली
Nirman Bhawan, New Delhi-110011

26.7. PAN India Trans Fat Survey

Completion Certificate

राकेश कुमार
निदेशक
Rakesh Kumar
Director



भारतीय खाद्य संरक्षा एवं मानक प्राधिकरण
स्वास्थ्य एवं परिवार कल्याण मंत्रालय
भारत सरकार
FOOD SAFETY AND STANDARDS AUTHORITY OF INDIA
Ministry of Health & Family Welfare
Government of India

TO WHOMSOEVER IT MAY CONCERN

It is to certify that the Quality Council of India (QCI) had conducted the PAN India survey to identify the presence of industrially produced trans-fatty acid content in selected six food categories, on the basis of the SOP, methodology, analysis and parameters designed by Food Safety and Standards Authority of India (FSSAI).

To conduct the Survey, QCI assessors visited 419 cities/districts across 34 States/UTs to collect the samples (6,245 samples of packaged products) and analysed the samples in 8 selected NABL accredited testing laboratories.

As per the agreement, the aforementioned project was successfully completed and QCI delivered all the deliverables between August, 2021 to November, 2021 and the final payment was made to QCI on 25th November, 2021 by FSSAI.


राकेश कुमार / RAKESH KUMAR
निदेशक / Director
भारतीय खाद्य संरक्षा एवं मानक प्राधिकरण
Food Safety and Standards Authority of India
(स्वास्थ्य एवं परिवार कल्याण मंत्रालय)
(Ministry of Health & Family Welfare)
भारत सरकार / Government of India
एफ.सी.ए. भवन, कोटला रोड, नई दिल्ली-110002
FDA Bhawan, Kotla Road, New Delhi-110002

Work Order

F.No.11020/7/2021/RARD/FSSAI
Food Safety and Standards Authority of India
(A Statutory Authority established under the Food Safety & Standards Act, 2006)
(Quality Assurance Division)
FDA Bhawan, Kotla Road, New Delhi - 110002

Dated: 31.03.2021

To,
The CEO,
National Accreditation Board for Certification Bodies (NABCB)
Quality Council of India
2nd Floor, Institution of Engineers Building
2, Bahadur Shah Zafar Marg,
New Delhi-110002, India

Dear Sir,

Greetings from FSSAI.

FSSAI has proposed to conduct PAN India Trans fat Survey in order to understand the current scenario of usage of trans-fats in processed foods and in industrial trans-Fats in fats/ oils so as to eliminate the trans-fat in a phased manner. FSSAI, considered the project proposal submitted by Quality Council of India (QCI) for conducting the aforesaid survey.

2. In view of above, I am directed to convey the approval of Competent Authority of FSSAI to Quality Council of India for conducting the Trans fat Survey in a time bound manner as per your project proposal.

3. The salient features of the survey are as follows:

- i. QCI will collect a total of 6600 samples, for the 6 product categories mentioned in the proposal from the 425 cities/districts as given in the list shared in the proposal and out of which 42 samples per city are to be collected from the 50 cities (7 samples per product category) and 12 samples per city from 375 cities/districts (2 samples per product category).
- ii. QCI shall carry out the analysis in NABL accredited/FSSAI recognized labs only. Further to test the parameters as indicated in the proposal for two trans-Fats-Elaidioate (9t-C18:1; 9t-octadecenoate) and Linoelaidioate (9t,12t-C18:2; 9t,12t-octadecadienoate) based on AOAC 996.06 or AOAC 996.01 or any other equivalent validated method using GC-FID covered under the scope of



- accreditation. For Acrylamide, the analysis shall be carried out based on validated method using LCMS-MS covered under the scope of accreditation.
- iii. FSSAI would facilitate to support the requirements as stated under point 6 of your proposal. Other than this, the sample collection, transportation, laboratory testing as well as generating final report will be done QCI.
 - iv. FSSAI will pay @ Rs. 7212 per sample + GST to QCI. This includes sample pick up, transportation and analytical charges.
 - v. The total project cost would be as follows:
 - a. Cost of Analysis (including sample pick up and transportation to your testing lab): Rs. 7212/- + GST per sample
 - b. Approximate Number of Samples = 6600
 - c. Total Cost (excluding GST) for 6600 samples: Rs. 4,76,00,000, GST will be paid at 18%

vi. The payment schedule will be as follows:

S.No	Phases	Payment Schedule	% of total cost	Amount in INR(excluding GST)
1.	I	Advance payment on award of Work order	30	1,42,80,000
2.	II	Completion of on ground food sample collection	30	1,42,80,000
3.	III	Completion of analysis by the Lab	20	95, 20,000
4.	IV	Completion and submission of final Trans Fat Survey report	20	95, 20,000
5.		Total	100	4,76,00,000

4. QCI shall conduct the Survey including laboratory analysis of samples followed by compilation of result and submission of report in a time-bound manner.

(Yours Sincerely)


 31/3/2021
 (Shailender Kumar)
 Assistant Director (QA)

26.8. Assessment of various ODF, ODF+, & ODF++ status

Completion Certificate

Page 14

आर. एस. जयाल
R. S. JAYAL

उप सचिव
Deputy Secretary (SBM-II)
Tel: 011-23061187



भारत सरकार
आवासन और शहरी कार्य मंत्रालय
निर्माण भवन
GOVERNMENT OF INDIA
MINISTRY OF HOUSING AND URBAN AFFAIRS
NIRMAN BHAWAN

नई दिल्ली-110011, तारीख 20
New Delhi-110011, dated the 20
Dated : 02 September 2020

TO WHOM IT MAY CONCERN

This is certified that under a contract agreement signed between **this Ministry** and **M/s Quality Council of India (QCI), New Delhi**, assessment was done by M/s QCI of various Urban Local Bodies (ULBs) for their **Open Defecation Free (ODF)** status. ODF certification was done after assessment of the ULBs from **19.07.2016, till date**. Further, ULBs were also assessed and certified on **ODF+ and ODF++ protocol**, as per the extended scope of the Contract Agreement vide this Ministry's work order No 15/3/2018-SBM-II dated 01.07.2019.

2. These agreements for ODF, ODF+ and ODF++ assessment and certification of ULBs are valid till **30.09.2020**.

3. Further, it is certified that M/s Quality Council of India has delivered their services satisfactorily for these projects.



(R. S. JAYAL)

Deputy Secretary to Govt. of India
Swachh Bharat Mission (Urban) Division

राजेश्वर सिंह जयाल/R.S. JAYAL
उप सचिव/Deputy Secretary
आवासन और शहरी कार्य मंत्रालय
Ministry of Housing And Urban Affairs
निर्माण भवन, नई दिल्ली
Nirman Bhawan, New Delhi


F.C. Srivastava ★
Deputy Director
(Accounts & Administration)
